



Office of the Chief Executive Officer

Zachary L. Williams
Executive Assistant, Chief Operating Officer

Chief Executive Officer
Lorraine Cochran-Johnson

Board of Commissioners

District 1
Robert Patrick

District 2
Michelle Long Spears

District 3
Nicole Massiah

District 4
Chakira Johnson

District 5
Mereda D. Johnson

District 6
Edward "Ted" Terry

District 7
LaDena Bolton

Via Electronic Mail and U.S. Mail

March 2, 2026

Chief, Clean Water Branch
ATTN: Mr. Paul Schwartz
Water Protection Division
U.S. Environmental Protection Agency, Region 4
61 Forsyth Street, S.W.
Atlanta, GA 30303

RE: Clean Water Act Consent Decree 1:10cv 4039-SDG
Annual Report #14 Submittal due March 2, 2026

Dear Mr. Schwartz:

As required by §IX. Reporting Requirement of the Consent Decree associated with the above referenced civil action, we are submitting the following document for your review and comment:

- **Annual Report #14**

I certify under penalty of law that these documents and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering such information, the information submitted is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fines and imprisonment for knowing violations pursuant to CWA Section 309(c)(4).

If you have questions or comments regarding this submittal, please call me at 404-371-2174.

Respectfully,

Zachary L. Williams

Zachary L. Williams,
Chief Operating Officer and Executive Assistant
DeKalb County, Georgia

cc: Georgia EPD
Maria V. Houser, Director of Consent Decree and Environmental Compliance
Reginald Wells, Director, DWM
E. Fitzgerald Veira, Troutman Pepper
Matthew C. Welch, Deputy County Attorney
Dora De Taboada, Assistant Director Regulatory Compliance

Annual Report No. 14

January 1, 2025, to December 31, 2025
Civil Action No. 1:10cv4039 - SDG

DeKalb County
Department of Watershed Management



DeKalb County
G E O R G I A

March 2, 2026

Table of Contents

Acronyms	iii
Introduction	1
Executive Summary	1
Part I – Capacity, Management, Operations and Maintenance (CMOM) Programs’ Implementation	
Activities Completed	4
1. CERP (CD VI.B.i)	4
2. FOG Management Program (CD VI.B.ii)	4
3. Sewer Mapping Program (CD VI.B.iii)	5
4. Maintenance Management System Program (CD VI.B.iv)	6
5. Collection and Transmission Systems Training Program (CD VI.B.v)	7
6. System-Wide Flow and Rainfall Monitoring Program (CD VI.B.vi).....	7
7. System-Wide Hydraulic Model (CD VI.B.vii).....	8
8. Financial Analysis Program (CD VI.B.viii)	9
9. Infrastructure Acquisitions Program (CD VI.B.ix)	9
10. Priority Areas Sewer Assessment and Rehab Program (CD VI.B.x).....	10
11. Ongoing Sewer Assessment and Rehabilitation Program (CD X 38.).....	14
12. Supplemental Environmental Project (CD VIII)	15
Attachment A MMS KPIs	16
Attachment B Priority Fix List Status.....	19
Part II Sanitary Sewer Overflow Trends Analysis	33
Executive Summary	33
1. Classification of SSO Types and Causes.....	37
2. Number and Volume of SSOs.....	39
3. Average Duration of SSOs.....	42
4. Causes of SSOs	44
5. Other Trends	48
6. Summary	57

Acronyms

ARV	air release valve
CAP	Capacity Assurance Program
CARL	Clean All Required Lines
CCTV	closed-circuit television
CD	Consent Decree
CERP	Contingency and Emergency Response Plan
CIP	capital improvement program
CIPP	cured in place pipe
CM	corrective maintenance
CMMS	computerized maintenance management system
CMOM	capacity, management, operations, and maintenance
CV360	CloudVergent 360
DIP	ductile iron pipe
DOE	Date of Entry
DWM	Department of Watershed Management (DeKalb County)
EM	emergency maintenance
EPA	U.S. Environmental Protection Agency
FOG	Fats, Oils, and Grease
FSE	food service establishment
EPD	Environmental Protection Division (Georgia)
GIS	geographic information system
GSRR	Gravity Sewer Rehabilitation and Replacement
I/I	infiltration/inflow
KPI	key performance indicator
LF	linear feet
MCA	manhole condition assessment
MCD	Modification to Consent Decree
MMS	maintenance management system
NTP	Notice to Proceed
O&M	operations and maintenance
OSARP	Ongoing Sewer Assessment and Rehabilitation Program
PACP	Pipeline Assessment and Certification Program
PASARP	Priority Areas Sewer Assessment and Rehabilitation Program
PFL	Priority Fix List
PM	preventive maintenance
QA/QC	quality assurance and quality control
SSO	sanitary sewer overflow
TISCIT	Totally Integrated Sonar and Camera Inspection Technology
USGS	United States Geological Survey
WAM	work and asset management
WCTS	wastewater collection and transmission system

Introduction

DeKalb County (the “County”) Department of Watershed Management (DWM) submits this 14th Annual Report in accordance with Section IX, Paragraph 58 of the Consent Decree (CD) (Civil Action 1:10cv4039-SDG) to provide:

- a) “A narrative summary of progress made, including key accomplishments and significant activities, under the Capacity, Management, Operations, and Maintenance (CMOM) programs implemented or modified pursuant to this Consent Decree for the most recent twelve (12) month period.”
- b) “A trends analysis of the number, volume, average duration, and cause of the County’s Sanitary Sewer Overflows (SSOs) for the previous twenty-four (24) month period.”

On September 22, 2021, a Modification to Consent Decree (MCD) was entered, which among other things, extends the timeline to complete the assessment and rehabilitation work under the Priority Areas Sewer Assessment and Rehabilitation Program (PASARP) to December 20, 2027. The MCD also modified the County’s reporting obligations, including the provisions governing annual reports. According to the MCD:

- c) “The Minimum Linear Footage of Pipe Review, Design, and Rehabilitation completed in each Project Category for that calendar year, a detailed written description of the work that was done to complete such rehabilitation, and a detailed written description of how the County calculated the Minimum Linear Footage of Pipe Review, Design and Rehabilitation completed and how it apportioned such rehabilitation to each Project Category.”
- d) “A description of any lift station rehabilitation and/or construction and construction of additional storage undertaken and/or completed pursuant to modified paragraph 35(i).”
- e) “A detailed written description of all ongoing or completed work at the locations on the Priority Fix List and a list of such locations that have been adequately rehabilitated, relieved, fixed, or otherwise addressed so that no future SSOs are predicted to occur at any such locations as a result of a representative two (2) year twenty-four (24) hour storm event.”

Executive Summary

The report that follows is divided into two sections as required by the CD. Part I reports on the CMOM Programs’ Implementation Activities. Part II, the Sanitary Sewer Overflow (SSO) Trends Analysis, is intended to meet the County’s reporting obligations as referenced above. This document details, in narrative form, progress made in the 2025 timeframe as well as significant program accomplishments and SSO trends analysis. Any revised milestones and the associated corrective implementation plans are noted in the previously submitted Semi-Annual Report.

During the period from January 1, 2025, to December 31, 2025, the following DWM CMOM implementation programs, reports, and deliverables were submitted to the U.S. Environmental Protection Agency (EPA) and Georgia Department Environmental Protection Division (EPD), as noted in Table ES-1.

Table ES-1 Consent Decree Submittals – Schedule and Status

Consent Decree #	Title	DWM Final Submittal
IX.(56)	4th Quarterly Report 2024	1/30/25
IX.(57)	26th Semi-Annual Report	1/30/25
VI.(35)	2025 Minimum Linear Footage of Pipe Review, Design, and Rehabilitation	2/3/25
IX.(58)	Annual Report #13	3/3/25
IX.(56)	1st Quarterly Report 2025	4/30/25
IX.(57)	27th Semi-Annual Report	7/30/25
IX.(56)	2nd Quarterly Report 2025	7/30/25
IX.(56)	3rd Quarterly Report 2025	10/30/25

Table ES-2 summarizes the major activities and key milestones completed in 2025.

Table ES-2 2025 Major Consent Decree Milestones and Accomplishment Summary

Program or Project	Milestones and Accomplishments
Contingency and Emergency Response Plan (CERP)	<ul style="list-style-type: none"> ✓ Trained DWM personnel and contractors in CERP definitions, responses, and reporting. ✓ For all SSOs, even after the initial response, follow-up actions included a combination of closed-circuit television (CCTV); FOG education; root control; system cleaning; point repairs, etc. as necessary ✓ Proactively discovered 5 spills from in stream monitoring and potentially prevented 7 overflows from occurring by utilizing flow monitor alarms.
Fats, Oils, and Grease (FOG) Management Program	<ul style="list-style-type: none"> ✓ Removed 7.7 MG of FOG as logged through the Hauler Company Assessment Program. ✓ Continued FOG enforcement for non-compliant food service establishments (FSEs) and continued public education of facilities located around grease-related spills. <ul style="list-style-type: none"> – Delivered 1,277 warning notices – Delivered 175 court summons ✓ Performed FOG inspections, evaluations, and tracked data: <ul style="list-style-type: none"> – Total number of FOG inspections: 9,940 – Total number of FOG permits issued: 3,030 ✓ 2025 monthly average permitted active FSEs: 253
Sewer Mapping Program	<ul style="list-style-type: none"> ✓ Continued to update the geographic information system (GIS) with sanitary sewer easement information to facilitate a more efficient access process for maintenance and capital projects. ✓ Used heat maps of root-caused SSOs to identify areas for chemical root control. ✓ Used GIS aerials to accurately estimate easement clearing areas for root intrusion prevention and efficient access during maintenance activities. ✓ Continued updates to GIS to reflect new developments, connectivity issues, sewer system improvements, and maintenance revisions.
Maintenance Management System (MMS) Program	<ul style="list-style-type: none"> ✓ Performed 2,965 sewer creek crossing inspections to monitor and maintain the structural integrity of sewer assets near waterways. ✓ Treated 2,756,160 linear feet (LF) of sewer to remove root intrusions and prevent blockages. ✓ Performed easement clearing to minimize root intrusion and allow efficient access to assets during maintenance activities. A total of 23,350,192 square feet of sewer easements were cleared. ✓ Completed 47 miles of small diameter sanitary sewer cleaning.
Collection and Transmission Systems Training Program	<ul style="list-style-type: none"> ✓ Completed 6,349 hours of technical, leadership, managerial, and skills training. ✓ Generated training reports to ensure employees completed scheduled training sessions within a specified timeframe.
System-Wide Flow and Rainfall Monitoring Program	<ul style="list-style-type: none"> ✓ Continued maintenance of County-wide flow monitoring and rain gauge system to be used for the development of the dynamic model and system flow analysis; supported monthly average of 311 flow monitors and 40 rain gauges; and performed flow meter maintenance visits. ✓ Placed temporary monitors in the system, as needed, to assist in determining available sewer capacity for specific projects.
System-Wide Hydraulic Model	<ul style="list-style-type: none"> ✓ Continued to use the dynamic model for sewer capacity evaluation requests. ✓ Developed and ran dynamic model simulations with updated data to verify various Capital Improvement Program (CIP) project designs. ✓ Continued to update the seven dynamic model networks covering the countywide sewer system with the latest GIS and field survey data.

Table ES-2 2025 Major Consent Decree Milestones and Accomplishment Summary

Program or Project	Milestones and Accomplishments
Financial Analysis Program	<ul style="list-style-type: none"> ✓ Tracked expenditures for both the operations and maintenance (O&M) budgets and CIP budgets. ✓ Continued use of work order management system (see MMS section) to track costs of emergency, corrective, and preventive work by asset.
Infrastructure Acquisitions Program	<ul style="list-style-type: none"> ✓ Evaluated and/or acquired 18,651 LF of pipe. ✓ Reviewed 1,659 plans and received 468 sewer capacity requests.
PASARP	<ul style="list-style-type: none"> ✓ Exceeded all MLF requirements for 2025. ✓ Under two Cooperative Agreements and Gravity Sewer Rehabilitation and Replacement (GSRR) Section 1, completed 17,255 LF lining/point repair construction. ✓ Through design-build rehabilitation packages, GSRR Section 2, and On-Call Water and Sewer Contracts, completed 10,456 LF of pipe replacement. ✓ Completed design of small diameter capacity relief projects through A/Es. ✓ Completed design on all identified trunk projects. ✓ Completed design of Snapfinger AWTF Influent Pump Station.
Ongoing Sewer Assessment and Rehabilitation Program (OSARP)	<ul style="list-style-type: none"> ✓ Completed CCTV and associated pipeline cleaning and manhole condition assessment (MCA) in the OSARP areas, including: 113,467 LF (21.5 miles) of acoustic inspection; 22,598 LF (4.3 miles) of smoke testing; 345,365 LF (65.4 miles) of CCTV; 80,045 LF (15.2 miles) of Totally Integrated Sonar and Camera Inspection Technology (TISCIT) surveys; and 974 MCAs.
Supplemental Environmental Project	<ul style="list-style-type: none"> ✓ Completed program in 2014.
Priority Fix List	<ul style="list-style-type: none"> ✓ Total of 270 sites on the PFL ✓ Reported 58 sites as Adequately Fixed in 2025 for a total of 237 Adequately Fixed sites.
SSO Trend Analysis	<ul style="list-style-type: none"> ✓ Completed a detailed SSO trends analysis and major spill analysis for the period from 2023 through 2025.

Part I – Capacity, Management, Operations and Maintenance (CMOM) Programs’ Implementation Activities Completed

1. CERP (CD VI.B.i)

DWM continued to implement the CERP in 2025 using the approved revised CERP CMOM plan to mobilize labor, materials, tools, and equipment to respond to and appropriately remedy conditions that may cause or contribute to an SSO. Considerable effort was made in 2025 to train DWM and contractor personnel in the CERP CMOM document and to verify that personnel were consistently and accurately applying the policies and procedures of the document through new employment orientation and refresher training.

Key Accomplishments and Significant Activities:

1. Completed the following activities to resolve and remedy current and potential SSOs:
 - a. Cleaning total 537,599 LF
 - i. First response and follow up 23,257 LF
 - ii. Contractor cleaning 514,342 LF¹
 - b. Point repairs 11²
 - c. CCTV 124,594 LF³
2. Responded to 150 reportable spill events and performed spill follow-up actions.
3. Conducted monthly SSO meetings with program area managers to review the previous month’s SSOs and discuss any emerging trends and possible mitigation efforts.
4. Distributed more than 711,600 FOG education flyers in areas where grease was identified as the cause of a spill to increase awareness of the impact of allowing grease to enter the sewer system and thus, potentially averting future SSOs.
5. Amplified community awareness and education efforts related to FOG as well as other causes of SSOs. Approximately 961,000 educational flyers were distributed by Nextdoor directly to the community.
6. Discovered and resolved five spills from in-stream monitoring.
7. Discovered and potentially prevented seven overflows from occurring using flow monitoring technology. High level alarms and data assessment alerted personnel to potential overflows at lift stations. Crews were able to respond before an actual overflow occurred.

2. FOG Management Program (CD VI.B.ii)

The DeKalb County FOG Management Program has met all major program milestones. However, to support the County’s ongoing implementation of the CD, the FOG program has taken on a greater role in the ongoing trends analysis efforts and in developing cleaning protocols pursuant to the MMS program. While the FOG program is designed to reduce the amount of FOG that enters the wastewater collection and transmission system (WCTS), the cleaning instituted under the MMS program is designed to remove FOG from the system. Together, these programs represent a fully integrated FOG prevention and elimination program.

In 2025, DWM continued its enforcement of the FOG ordinance and unregistered FSEs, as described below. DWM also increased the amount of public education about FOG and the effects of FOG on the sewer system through social media, media advertisements, and press releases. DWM successfully

¹Total encompasses all cleaning performed for SSO response as well as prevention of potential SSOs.

²Total reported reflects Point Repairs completed to address SSOs and are coordinated with PASARP construction.

³The total reported for CCTV activities in this section is limited to CCTV work performed as a follow up to an identified SSO and does not include CCTV work performed as a part of the assessment of the WCTS.

continued efforts to engage the municipalities within the County to ensure implementation of the FOG Management Program throughout the County.

Key Accomplishments and Significant Activities:

1. Distributed educational materials at multi-family apartment complexes and residential neighborhoods that have been identified as located near sewer spills and investigated nearby FSEs for grease violations.
2. Reviewed pump-out manifests as part of the Hauler Company Assessment program to ensure that haulers are properly disposing of FOG. A total of 7.7 million gallons of FOG was recorded as being removed from the system through this program.
3. Delivered 1,277 warning notices and 175 court summonses to non-compliant FSEs.
4. Performance Measures:
 - a. Total number of FOG inspections: 9,940
 - b. Total number of FOG evaluations: 606
 - c. 2025 monthly average permitted active FSEs: 253
5. Issued 3,030 permits.
6. Continued to sponsor the “No FOG, No Clog” campaign to educate students and adults about the hazards of grease clogs in sewer systems and provide information about FOG and its effect on the sewer system. Conducted 82 school presentations reaching approximately 22,650 students and adults. Conducted 34 outdoor community events reaching approximately 53,700 citizens.
7. While continued revision of the FOG ordinance is not a CD requirement, the FOG ordinance was revised beyond the scope of the CD to include multi-family residences and was passed by the Board of Commissioners on December 11, 2018. This ordinance extends the application of existing FOG-related regulations to certain multi-family dwelling units. For 2025, seven multi-family sites qualified to be under the FOG ordinance.

3. Sewer Mapping Program (CD VI.B.iii)

The purpose of the Sewer Mapping Program is to provide an integrated system capable of mapping, inventorying, and depicting system assets. In 2015, the Sewer Mapping Program enhancements and milestones were substantially completed, allowing the County in 2025 to: 1) produce certain maps using GIS technology; 2) integrate sewer system locations and attribute data with the hydraulic model and the computerized maintenance management system (CMMS); 3) reproduce maps in a manner that will allow use by O&M crew leaders in the field; and 4) identify and track problems geographically.

Though the County has achieved completion of the major components of the program, data updates to the GIS system continue for new developments or system changes that have been reported by DeKalb County personnel in the regular course of business or by non-DeKalb County personnel engaged in assessment and rehabilitation projects. Moreover, the information from the Sewer Mapping Program is being used in other CD-related programs including the hydraulic model, flow and rainfall monitoring, PASARP, OSARP, CERP, FOG, Infrastructure Acquisitions, and MMS programs.

Key Accomplishments and Significant Activities:

1. Continued to populate a geographic information system (GIS) layer for sanitary sewer easement information from record drawings and subdivision plats to augment existing data and facilitate a more efficient access process for maintenance and capital projects. Maps of easements were scanned into GIS software and digitized into the GIS layer. Attributes of the easement were recorded for future use. Approximately 122 easements have been identified from drawings and subdivision plats, scanned into GIS software, and added to the GIS layer.

2. Used heat maps of root-caused SSOs to prioritize areas needing chemical root control, address known root intrusions, and prevent potential future root-caused SSOs.
3. Used GIS aerial photographs to: 1) identify areas where sanitary sewer easements need clearing for maintenance access; 2) make accurate estimates of the work needed; and 3) provide contractors with precise areas to clear.
4. Created applications and workflows to streamline and organize the submission and retention of as-built drawings as the GIS is updated.
5. Continued to use GIS tools, such as dashboards, web-accessible maps, and web-accessible apps, to provide data to users throughout the County.
6. Continued updates to GIS to reflect new developments, connectivity issues, sewer system improvements, and maintenance revisions. As assets are added to GIS, they are also added to the MMS program for maintenance and evaluation. Maintenance activity is regularly updated to the GIS and used in planning for continuing maintenance.
7. Continued to update two interactive online dashboards known as sewer capacity requests. One is public-facing and the other is for internal use only.
8. Implemented DWM's Asset Management Program services Strategic Asset Management Plan (SAMP) and collected all GIS asset data.

4. Maintenance Management System Program (CD VI.B.iv)

The County's MMS program involves a combination of preventive, corrective, and predictive inspection and maintenance activities to maintain the WCTS. The program is divided into two key areas: 1) tools that support the maintenance activities and 2) specific maintenance activities performed for the County's gravity system, lift stations, and force mains. Communication systems, physical inspection and testing, information management systems, and inventory management are tools used to support maintenance activities. Gravity system maintenance and lift stations, force mains, and air release valve (ARV) maintenance describe the County's maintenance activities established under the MMS program. Finally, the MMS provides key performance indicators (KPIs) that will enable the County to measure its performance.

Key Accomplishments and Significant Activities:

1. Inventory Management

- a. Successfully performed physical inventory at each warehouse location. The DWM Operations' warehouse location achieved outstanding audit results of 96 percent for 2025, demonstrating that DWM is accurately tracking and maintaining the computerized inventory of the warehouse.
- b. DWM warehouse inventory value was \$11,627,007 for 2025, thus providing the assets needed to ensure efficient maintenance and repair activities.

2. Gravity System Maintenance

- a. Performed 2,965 sewer creek crossing inspections.
- b. Continued chemical root control application in the system to remove root intrusions identified during assessment. A total of 2,756,160 LF of sewer mains were treated for roots.
- c. Continued sewer easement clearing in the system to allow efficient access to assets during maintenance activities. A total of 23,350,192 square feet of sewer easements were cleared.
- d. Continued to input repair and maintenance data into CMMS, including lining, point repairs, cleaning, etc., to track these maintenance activities and their effectiveness on system operation.

e. Completed 47 miles of small-diameter sanitary sewer cleaning.

3. Lift Station, Force Main, and ARV Maintenance

a. Working statistics:

- i. Completed 5,146 preventive maintenance work orders (428 per month) to ensure proper maintenance and continued functioning of the assets.
- ii. Maintained a backlog of two or less work orders per month for 12 months to ensure work is being conducted efficiently and within a short time after being identified and planned. One month had zero backlogged work orders.
- iii. Averaged two lift stations per month with one pump-out for service to minimize the risk of an entire station being without pumping capacity.
- iv. Inspected 66 force main easements to ensure continued access for maintenance and assess if any vegetative growth could potentially affect the structural integrity of the force main.
- v. Inspected 66 discharge manholes for structural integrity.
- vi. Performed force main pressure testing at 66 stations to test for any pipe leakage.
- vii. Inspected 55 of 55 ARVs to ensure they were operating automatically to release air pockets in the force main.
- viii. Completed lift station work orders:
 1. 99.1 percent preventive maintenance
 2. 0.9 percent corrective maintenance
 3. 0 percent emergency maintenance

b. DWM performed electrical ground testing (amp and volt readings) and thermal scans of 66 lift stations as a preventive measure to ensure proper operation and identify any potential electrical problems.

4. Tracked KPIs (refer to Attachment A).

5. Collection and Transmission Systems Training Program (CD VI.B.v)

In 2025, the County continued to deliver technical and skills training to DWM personnel related to applicable job responsibilities. CERP training is a focus each year and included coordination with New Employee Orientation classes to train all new DWM personnel on CD responsibilities (in earlier years, only new Operations personnel received CERP training).

Key Accomplishments and Significant Activities:

1. Continued to implement the updated Training Program Plan (2018) using the Training Matrix, Training Calendar, and Compliance Software. As of September 2022, DWM has transitioned from using Compliance Suite to CloudVergent 360 (CV360) to track and schedule training.
2. Completed 6,349 hours of technical, leadership, managerial, and skills training.
3. Developed training reports to ensure employees completed scheduled training sessions within a specified timeframe.

6. System-Wide Flow and Rainfall Monitoring Program (CD VI.B.vi)

The program's goal is to provide an efficient and effective data monitoring network to assess capacity and infiltration/inflow (I/I) issues within the WCTS. All major milestones for this program have been completed. The ongoing program's focus is on data collection for analysis of capacity requests and I/I

reduction efforts. Moreover, the County continues to use the program for SSO reduction efforts and identification of areas that could possibly lead to an SSO.

Key Accomplishments and Significant Activities:

1. Maintained the County-wide flow monitoring and rain gauge system for the dynamic model and system flow analysis.
2. Continued implementing a maintenance and calibration program, supporting a monthly average of 311 flow monitors and 40 rain gauges. Maintenance field operations are supported by daily, weekly, and monthly quality assurance (QA)/quality control (QC) measures to identify meters in need of additional attention. Flow monitoring field crews performed maintenance site visits. The County engaged contractors to support flow monitoring operations and to supplement County resources.
3. Maintained and deployed temporary flow monitors in the system to assist in determining available sewer capacity and collecting additional data on known collection system issues.
4. Deployment and maintenance of temporary flow monitors in the system to isolate locations of high I/I.
5. Continued collecting data to support multiple CMOM programs and engineering studies.
 - a. Generated reports for intergovernmental billing.
 - b. Determined spill volumes, where possible, as part of CERP.
 - c. Performed I/I studies for areas with suspected new or changing system flow.
 - d. Investigated other non-ideal flow, including backwater and surcharge conditions.
6. Continued implementation of an audit program to quantify and track data quality. The audit program includes consideration for timeliness of maintenance visits, consistency, and timeliness of QA/QC communications and minimizing data loss.
7. Used system depth information from flow meters, combined with manhole-specific level alarms, to alert field personnel of possible operational issues that could result in an SSO.

7. System-Wide Hydraulic Model (CD VI.B.vii)

The County revised and resubmitted the dynamic hydraulic model reports to EPA/EPD for all model areas. EPA/EPD approved the model reports on September 23, 2021, allowing the County to begin using the dynamic hydraulic models.

Since completion of the CD requirements, the modeling team has focused on updating the models with new GIS and survey data, as well as improving the calibration using the full groundwater infiltration module in InfoWorks ICM. The calibrated models have been used to identify capacity relief projects County-wide as well as to verify planned capacity improvement projects.

Key Accomplishments and Significant Activities:

1. Continued updating the dynamic model networks as new GIS and survey data became available.
2. Continued to use the dynamic model for sewer capacity evaluations requests.
3. Used the dynamic sewer models to evaluate ongoing CIP project designs and possible future alternatives in the Snapfinger, Pole Bridge, North Fork Peachtree Creek, Nancy Creek, Intrenchment Creek, and South Fork Peachtree Creek sewersheds. New projects and previously proposed projects were re-evaluated as new information became available.

4. Prepared model packages in response to requests from design engineers. Model packages included existing and future sewer networks covering the areas of interest, as well as all the necessary supplemental files to run the model simulations.
5. Supported the System-Wide Flow and Rainfall Monitoring Program by evaluating flow splits in the dynamic model. The model provided insights into how water moves through the sewer system between flow monitors.

8. Financial Analysis Program (CD VI.B.viii)

The Financial Analysis Program incorporates aspects of revenue estimating, budgeting, cost analysis, and customer rate setting such that DWM provides the desired level of service to its customers while meeting its regulatory requirements. DWM continues to monitor its revenue and expenditure budgets and is on track to meet its revenue target and stay within its expenditure budget.

Key Accomplishments and Significant Activities:

1. Continued tracking of maintenance costs associated with work done on assets through a work-order-based CMMS software in the Operations Division. In 2025, this transitioned from Oracle WAM to Cityworks. The software tracks equipment, labor, and material costs, and classifies work order type as corrective, preventive, or emergency maintenance. All work associated with design and construction of sewer rehabilitation projects are tracked in the PASARP and OSARP tasks.
2. Table 8-1 lists the costs associated with work orders and maintenance type.

Table 8-1 2025 Sewer System Costs by Work Order Type

Work Order Type	Sewer System Costs (\$)	Sewer System Costs (%)
Corrective Maintenance	\$613,513	38.04%
Preventive Maintenance	\$13,094	0.81%
Emergency Maintenance	\$982,204	60.9%
Miscellaneous Maintenance	\$3,987	0.25%
Total	\$1,612,798	100%

9. Infrastructure Acquisitions Program (CD VI.B.ix)

The goals of the Infrastructure Acquisitions Program are to acquire infrastructure that meets County standards for design, construction, capacity, and efficiency, and to maintain a program that properly monitors the acquisition process, encourages input, and is efficient for contractors, developers, property owners, and the County.

Key Accomplishments and Significant Activities:

1. Evaluated and/or acquired 18,651 LF of pipe, thereby ensuring adherence with the County's design standards.
2. Reviewed 1,659 plans.
3. Reviewed 26 plats.
4. Received 468 sewer capacity requests.
5. Issued 257 sewer capacity letters either confirming available capacity, requiring a sewer action plan, or noting that the capacity request resulted in a zero or less impact to system capacity.
6. Continued using the I/I Banking Credit System as an alternative for processing sewer capacity approvals. Approved 184 service capacity requests utilizing the I/I Credit Bank.

7. Continued working with large sewer contributors to have developers financially contribute to sewer rehabilitation to generate I/I credits. Delivered sewer credits to ten impactful projects.

10. Priority Areas Sewer Assessment and Rehab Program (CD VI.B.x)

The main purpose of the PASARP is to provide for the identification, delineation, assessment, prioritization, and rehabilitation of Priority Areas (both Initial Priority Areas and Additional Priority Areas) as explained in the CD within the County WCTS. The Initial and Additional Priority Areas total approximately 844 miles of sewers (approximately 34 percent of the WCTS). In implementing the PASARP, the County is undertaking certain condition, structural, and hydraulic assessments within the Priority Areas to identify, prioritize, and complete appropriate rehabilitation measures within those areas. As part of the implementation process, the County is tracking rehabilitation measures completed within the Priority Areas and will determine the effectiveness of those measures, using selected KPIs.

In 2017, the County substantially completed the 2-year condition assessment phase of the PASARP, using a wide range of evaluative tools and programs including private lateral investigations, corrosion defect identifications, MCA, flow monitoring, CCTV inspection, gravity sewer line defect analysis, TISCIT, acoustical testing, and smoke testing. Because the PASARP assessment is complete, the focus is on continuing to package and prioritize cost-effective rehabilitation recommendations as well as construct capacity relief projects. The first of many prioritized rehabilitation contracts resulting from the assessment phase began in 2017.

Appendix E of the MCD includes additional definitions and milestones for the PASARP. As the assessment is complete in Priority Areas, the remaining design and construction is further categorized as “Simple Pipe Review,” “Simple Pipe Rehabilitation,” “Complex Pipe Design,” and “Complex Pipe Rehabilitation” with required Minimum Linear Footages to be completed annually per Table E-1. Projects listed in Tables E-2 and E-3 are complete.

Simple Pipe Review

Simple pipe review consists of conducting a visual review of Pipeline Assessment and Certification Program (PACP)-certified coded CCTV of the pipe segments and developing simple pipe rehabilitation recommendations to address severe defects noted during condition assessment. A total of 855,000 LF of simple pipe review was required to be completed by December 31, 2024, but this was exceeded and 883,835 LF was completed through 2021. No additional simple pipe review is currently planned within the PASARP areas. The total footage was calculated by taking the GIS length (verified by the CCTV length) of each pipe asset that was reviewed. Table 10-1 details the total length of pipe review by final rehabilitation recommendation.

Table 10-1 2025 Simple Pipe Review

Rehabilitation Recommendation	Pipe Length Reviewed (LF)
Simple Pipe Review Prior to 2025	
Replacement, Lining, Point Repairs	883,835
Simple Pipe Review in 2025	
Replacement, Lining, Point Repairs ⁴	0
Total through 2025	883,835

⁴ Simple Pipe Review milestone was met in 2021; no additional Review in this category needed in 2025.

Simple Pipe Rehabilitation

Simple pipe rehabilitation addresses structural issues identified during simple pipe review and may include lining, point repairs, and same-size pipe replacement. Simple pipe rehabilitation is not intended to provide a comprehensive capacity solution but to extend the life of the asset. A total of 805,000 LF of simple pipe rehabilitation was required to be completed by December 31, 2025, but this was exceeded and 813,912 LF was completed.

Table 10-2 2025 Simple Pipe Rehabilitation

Project Information	Rehabilitation Completed	Pipe Length Rehabilitated (LF)
Simple Pipe Rehabilitation Prior to 2025		
On-Call Emergency (RGI), DB1, DB2, DB3, AWS (RGI), AWS (Granite), Coop (Insituform), Coop (IPR)	Replacement, Lining, Point Repair	796,224 ⁵
Simple Pipe Rehabilitation in 2025		
Coop (SAK)	Lining and Point Repairs	10,432
Coop (Insituform)	Lining and Point Repairs	7,256
Subtotal for 2025		17,688
Total through 2025		813,912

Complex Pipe Design

Complex pipe design is determining how to address capacity limitations within the WCTS. This can be done by reducing flow through the existing system with comprehensive rehabilitation to remove I/I or by increasing physical capacity of the system through upsizing existing pipes, adding relief sewers, or adding storage. A total of 260,000 LF of complex pipe design was required to be completed by December 31, 2025, but this was exceeded and 398,269 LF was completed. Table 10-3 below provides the amount of complex pipe design completed per project. As noted above, there are various methods to address capacity limitations and based on the method, the applicable footage was calculated differently.

- Pipe upsizing – replacement of pipe with a pipe of larger diameter
 - Existing alignment – actual footage of pipe designed for replacement
 - New alignment – footage of the existing alignment that is abandoned
- Relief sewers – footage of the existing pipe segments that are being relieved by the parallel sewer
- Storage tanks – footage of the pipe upsizing and/or relief sewer that does not have to be designed due to the storage tank
- Comprehensive rehabilitation – footage of the pipe upsizing needed that the comprehensive rehabilitation is replacing

⁵ The total LF of Simple Rehabilitation is 19,666 LF more than the total 2024 LF reported in Annual Report 13. In early 2025, Construction Managers verified all of the segments that were completed by their contractors, and identified additional rehabilitated footage that was not recorded during the year.

Table 10-3 2025 Complex Pipe Design

Contract Package	Project Description	Pipe Length Designed (LF)
Complex Pipe Design Prior to 2025		
Packages 1-8, additional small diameter sewers, and large diameter trunk sewers	Pipe upsizing, comprehensive rehabilitation	340,366
<i>Packages 1-8, additional small diameter sewer and large diameter trunk sewers</i>	<i>Pipe upsizing outside PASARP</i>	<i>31,889⁶</i>
Complex Pipe Design in 2025		
Small Diameter Sewers		
Shoal Section 3A and 3B Interim Offline Storage	Shoal Creek, I-SF3, 100% Design	3,871
Interim Measures Comprehensive Rehabilitation	Shoal Creek, Cobb Fowler Creek, I-SF2, I-SF3, 100% Design	14,451
<i>Interim Measures Comprehensive Rehabilitation</i>	<i>Doolittle Creek, 100% Design</i>	<i>7,281⁶</i>
Large Diameter Trunk Sewers		
Cobb Fowler Trunk North	Cobb Fowler Creek, I-SF2, 100% Design	411
Subtotal for 2025		18,733/26,014 ⁷
Total through 2025		359,099/398,269 ⁷

Complex Pipe Rehabilitation

Complex pipe rehabilitation is the construction of the design solutions to address capacity limitations within the WCTS. Comprehensive rehabilitation, pipe upsizing, relief sewers, and storage are all potential solutions the County is evaluating for construction. A total of 198,000 LF of complex pipe rehabilitation was required to be completed by December 31, 2025, but this was exceeded and 208,597 LF was completed when including completed outside priority areas that addresses PFLs. Table 10-4 below provides the amount of complex pipe rehabilitation completed per project. As noted above, there are various methods to address capacity limitations and based on the method, the applicable footage was calculated differently.

⁶The County has continued with design and construction of projects outside of the PASARP that are intended to address capacity issues within the PASARP or PFL sites.

⁷ The County and EPA/EPD disagree on the methodology of counting completed work toward interim milestones. As explained in a June 24, 2024 letter to EPA/EPD, the County asserts that the same formulation used to derive 2019/2020 and 2021 MLF commitments (*i.e.*, including rehabbing linear footage from projects outside of Priority Areas where that work affected PFL sites) should continue for current MLF commitments. In a March 14, 2025 response, EPA/EPD disagreed and concluded that only work in Priority Areas should count toward current MLF commitments. This is one issue that the County is working to resolve in negotiating a second modification with EPA/EPD. In this Report, the County provides linear footage both for work completed in Priority Areas and work completed outside of Priority Areas that addresses PFL sites. This will be shown as xx/xx with the first number indicating footage within the Priority Areas and the second including footage outside of Priority Areas.

Table 10-4 2025 Complex Pipe Rehabilitation

Contract Package	Project Description	Pipe Length Rehabilitated (LF)
Complex Pipe Rehabilitation Prior to 2025		
Packages 1-8	Pipe upsizing, comprehensive rehabilitation	162,845
<i>Packages 1-8</i>	<i>Pipe upsizing outside PASARP</i>	<i>14,415⁶</i>
Complex Pipe Rehabilitation in 2025		
Package 5, Component 3	Shoal Creek, I-SF3	5,966
Package 5, Component 12	Cobb Fowler Creek, I-SF2, Cobb Branch/Brookfield	2,366
Package 7, Component 9	Intergovernmental Basin – North Fork Peachtree Creek, I-IG14	2,865
Upper Snapfinger Comprehensive Rehab	Upper Snapfinger Comprehensive Rehab	12,423
Package 8, Component 5	Nancy Creek, I-IG2, Tilly Mill	45
2 nd /3 rd Avenue	Intergovernmental Basin – Intrenchment Creek, A-SF6	1,952
<i>Package 8, Component 8</i>	<i>South Fork Peachtree Creek, Sowell Estates</i>	<i>442⁶</i>
<i>Keheley Drive</i>	<i>Intergovernmental Basin – Intrenchment Creek</i>	<i>1,230⁶</i>
<i>Roman Court</i>	<i>Intergovernmental Basin – South Fork Peachtree Creek</i>	<i>4,048⁶</i>
Subtotal for 2025		25,617/31,337 ⁷
Total through 2025		188,462/208,597 ⁷

Lift Station and Additional Storage

A 160 MGD influent pump station is currently under design to replace the existing influent lift station at the Snapfinger Advanced Wastewater Treatment Facility (AWTF). The new IPS will have a peak instantaneous pumping flow rate of 160 MGD, with a rate of 100 MGD flowing to the plant treatment facilities and 60 MGD diverted to on-site equalization facilities. Additional scope was added to include utilization of existing basins for storage. 100% Design documents were received by the County on December 5, 2025.

Priority Fix List

The MCD also introduces a Priority Fix List (PFL) of repeat SSOs with the original 103 sites listed in Appendix F of the MCD. Sites can be added to the PFL if a site experiences in any 12-month period either 2 capacity-related or 2 non-capacity-related SSOs within a 500-foot-radius area. In 2025, 24 additional sites were added onto the PFL for a total of 270 sites. 58 sites were declared as Adequately Fixed in 2025 for a total of 237 Adequately Fixed sites. Attachment B provides details of ongoing and completed work at PFL sites.

Key Accomplishments and Significant Activities:

1. Under Cooperative Agreements with two contractors continued construction of lining and point repairs.
2. Under GSRR Section 1 continued construction of lining and point repair.

3. Under GSRR Section 2 continued construction of Packages No. 5, No. 7, and No. 8 projects. This includes completing easement acquisition and beginning pre-construction activities of Package 7 Component 4 to address PFL 12. Additionally, under GSRR Section 2 contract, finished construction of Package 8 Sowell Estates.
4. Under On Call Water and Sewer Contract continued construction of Package No. 5 Project.
5. Continue analysis of alternative projects to adequately fix the PFL sites with Requests for Extension.
6. Completed 100% design for Cobb Fowler North Trunk Project.
7. Started easement acquisition for all trunk sewer projects.
8. Both the permitting and the procurement process are ongoing for Shoal Creek Trunk Section I project. Proposals for construction received October 24, 2025. Proposals for construction management were received July 7, 2025.
9. Completed design of Snapfinger Influent Pump Station.
10. Continued execution of project communications and community outreach for ongoing projects.
11. Tracked KPIs as shown in Table 10-5.

Table 10-5 2025 PASARP KPIs

KPI	2025 Performance
SSOs per 100 miles of WCTS within the Priority Areas per year	8.2 SSOs per 100 miles within the Priority Areas per year
SSOs per 100 miles of WCTS within the Priority Areas per year per inch of rain within the Priority Areas	0.20 SSOs per 100 miles per year per inch of rain within the Priority Areas
Total volume of spills per 100 miles of WCTS within the Priority Areas	338,776 gallons per 100 miles within the Priority Areas
Total volume of spills per 100 miles per inch of rain within the Priority Areas	8,171 gallons per 100 miles per inch of rain within the Priority Areas
Number of dry weather SSOs ^a within the Priority Areas	49 dry weather SSOs ^a within the Priority Areas

^a Dry weather SSO KPI; removed the SSOs with cause listed as STORM or I/I (assumed others were dry weather SSOs).

11. Ongoing Sewer Assessment and Rehabilitation Program (CD X 38.)

The main purpose of the OSARP is to ensure continuous assessment and rehabilitation of the County's WCTS. The OSARP governs assessment and rehabilitation of those areas outside the Priority Areas while the CD is in effect and will continue to exist after the CD expires. This program enables the County to continuously and proactively identify, delineate, and prioritize areas or sewer segments in the WCTS for condition assessment and rehabilitation, as appropriate, starting with areas not being addressed under the PASARP. The implementation of the OSARP takes into consideration data obtained through other ongoing County programs and operations including:

- CMOM programs and information obtained from customers and the public
- Assessment and rehabilitation work performed under the PASARP
- Hydraulic modeling results
- Knowledge and experience of County personnel

- Best engineering practices and/or best management practices

Key Accomplishments and Significant Activities:

1. Performed assessments and cleaning that included approximately:
 - a. 113,467 LF (21.5 miles) of acoustic inspection
 - b. 22,598 LF (4.3 miles) of smoke testing
 - c. 345,365 LF (65.4 miles) of CCTV and associated cleaning
 - d. 80,045 LF (15.2 miles) of TISCIT assessments
 - e. 974 manhole condition assessments
2. Under GSRR Section 2 contract completed construction of Package 8 Component 8 project to address PFL site Sowell Estates.
3. Tracked KPIs as shown in Table 11-1.

Table 11-1 2025 OSARP KPIs

KPI	2025 Performance
SSOs per 100 miles of WCTS per year within the OSARP areas	9.4 SSOs per 100 miles per year
SSOs per 100 miles of WCTS per year per inch of rain within the OSARP areas	0.23 SSOs per 100 miles per year per inch of rain
Total volume of spills per 100 miles of WCTS within the OSARP areas	605,313 gallons per 100 miles
Total volume of spills per 100 miles per inch of rain in the OSARP areas	14,600 gallons per 100 miles per inch of rain
Number of dry weather SSOs ^a in the OSARP areas	134 dry weather SSOs ^a

^a Dry weather SSO KPI; removed the SSOs with cause listed as STORM or I/I (assumed others were dry weather SSOs).

12. Supplemental Environmental Project (CD VIII)

The Supplemental Environment Project was completed in 2014.

Attachment A

MMS KPIs

KPI	Formula	2025 Results
Communication System Program		
Landline abandoned calls—no reason available for why caller abandoned call	Number of dropped calls	Average of 313 abandoned calls per month
Call Duration	Duration of calls in minutes divided by the number of calls	Average duration of call: 1minute 55 seconds Total number of calls in 2025: 65,523
Information Management		
Active SSO-Driven Sewer Work Order Percentage	Number of active SSO-driven sewer work orders ÷ number of completed sewer work orders in the reporting period x 100	7.6% SSO-driven sewer work orders
Inventory Management		
Percentage of out-of-stock items	For the reporting period, the number of parts out of stock when requested ÷ total number of parts requested x 100	2.5% of out-of-stock items
Percentage of Physical Inventory Performance	The percentage of items whose quantity on hand does match the quantity in Oracle Work and Asset Management (WAM)	96% of items match the quantity in Oracle WAM
Percentage of Physical Inventory Audit	The net cost difference in the value of the physical count vs. the value of inventory shown in Cityworks	5% net cost difference
Gravity System		
Percentage of Preventive Maintenance (PM): CCTV Inspection of Sewer Lines, Operations and Contractors	Number of miles inspected ÷ total miles of sewer line x 100	0.96% sewer lines inspected by CCTV
PM: Percentage of Sewer Lines Cleaned	Number of miles cleaned ÷ total miles x 100	1.9% sewer lines cleaned
PM: Linear feet of Root Treatment per Year	Number of feet of roots removed ÷ number of linear feet of sewer system x 100 Conversion factor: 5,280 feet per mile	20.7% of system (2,753,573LF of root treatment)
PM: Percentage of manholes inspected per year	Number of manholes inspected ÷ total number of manholes in system x 100	1.47% manholes inspected
Emergency Maintenance (EM): Number of sanitary sewer overflows (SSOs) per mile of gravity sewer line	Number of SSOs ÷ WCTS total miles of gravity lines x 100	9.0 SSOs per 100 miles of gravity sewer line

KPI	Formula	2025 Results
Lift Stations, Force Mains, and Appurtenances		
PM: Percentage of PM Hours Worked versus Corrective Maintenance (CM) and EM Hours Worked	Oracle WAM Value: PM hours total ÷ total hours worked CM and EM hours total ÷ total hours worked Each Number x 100 to show percentage. Display as ratio.	PM: 99.1% Corrective and Emergency Maintenance: 0.9%
PM: Percentage of Backlogged PM Work Orders	Number of work orders not completed ÷ total number of work orders (x 100)	0% backlogged PM work orders
PM: Completed PM Work Orders (based on timeframe specified)	Number of work orders completed by timeframe	> 30 days: 0 annually
CM: Percentage of lift stations with pumps out of service	Percent Value: Number of stations with pumps out of service ÷ total number of stations (x 100)	3.0% lift stations with pumps out of service
PM: Percent of ARVs inspected, flushed, and serviced	Number of ARVs inspected, flushed, and serviced per year ÷ total number of ARVs (x 100)	100% ARVs inspected, flushed, and serviced

Attachment B

Priority Fix List Status

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
1	1078 Beech Haven Road	Yes	09/16/24	CIPP and EPR of upstream and downstream segments
2	125 Beaumont Avenue	No	pre-DOE	Cleaned line as a temporary measure. Abandoned line as part of sewer realignment project in DB3.
3	1313 Stone Mill Way	No	pre-DOE	Sealed crack in pipe
4	1433 Deerwood Drive	Yes	pre-DOE	Rehabilitation completed removed I/I
5	1440 Sowell Estate	Yes	08/29/25	Package 8, Component 8 pipe upsizing project complete
6	1462 Lively Ridge Road	No	pre-DOE	Cleaned line as a temporary measure then repaired break in main
7	1496 Country Squire	Yes	04/09/22	Completed construction of capacity relief project
8	157 Hood Circle	Yes	pre-DOE	Completed realignment of pipe
9	1600 Autumn Hurst Court	No	pre-DOE	Performed routine chemical root control on these pipe segments
10	161 Hood Circle	Yes	pre-DOE	Completed realignment of pipe
11	1615 Melanie Court	Yes		Shoal Creek Trunk Section 1 construction in procurement. Design for Interim Measures 3A storage complete.
12	1707 Childerlee Lane	Yes		Under construction
13	1787 Whitehall Forest Court	No	pre-DOE	Cleaned main and lateral, educated customer on not pouring grease down the drain
14	1942 East Starmount Way	Yes	02/08/24	City of Atlanta agreed trunk sewers at this location are owned and maintained by City
15	1964 East Starmount Way	Yes	02/08/24	City of Atlanta agreed trunk sewers at this location are owned and maintained by City
16	1970 East Starmount Way	Yes	02/08/25	City of Atlanta agreed trunk sewers at this location are owned and maintained by City
17	2052 Grand Prix Drive	Yes	10/19/23	Completed construction of capacity relief project
18	2060 Keheley Drive	Yes	09/19/25	Construction of pipe upsizing project complete.
19	2089 Garden Circle	Yes	02/06/24	House laterals connected to new sewer main

⁸Pre-DOE (Date of Entry) denotes PFL sites confirmed as Adequately Fixed in connection with the 3Q 2021 reporting process

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
20	2301 Mountain Industrial Blvd	No	pre-DOE	Cleaned lines and provided FOG outreach in upstream area. Continuing to clean lines in area.
21	2480 Miriam Lane	Yes		Completed local comprehensive rehab. Shoal Creek Trunk Section 1 construction in procurement. Design for Interim Measures 3A storage complete.
22	2562 Tilly Mill Road	Yes	01/31/25	Package 8 Component 5 capacity relief project complete.
23	2804 Millwood Way	Yes	04/09/22	Completed construction of capacity relief project
24	2967 Henderson Mill Road	No	pre-DOE	Replaced 28 LF of 10-inch ductile iron pipe (DIP) from main break
25	307 2nd Avenue	Yes	10/18/25	Completed construction of capacity relief project
26	3075 Thrasher Circle	Yes		Shoal Creek Trunk Section 1 construction in procurement. Design for Interim Measures 3A storage complete.
27	3230 Boring Road	Yes		Shoal Creek Trunk Section 1 construction in procurement.
28	3330 Northlake Parkway	No	08/11/22	Performed 2 point repairs downstream of SSO
29	3433 Brookfield Lane	Yes	05/14/25	Package 5 Component 12 capacity relief project construction complete.
30	3449 Brookfield Lane	Yes	05/14/25	Package 5 Component 12 capacity relief project construction complete.
31	3488 Keswick Drive	No	pre-DOE	Cleaned lines of grease, cut roots, and performed point repair where roots intruded
32	3496 Panthersville	Yes	09/15/23	Completed rehabilitation upstream to reduce I/I
33	3540 Buford Highway	No	pre-DOE	Cleaned lines and performed pipe repair
34	3831 East Avenue	No	pre-DOE	Cleaned debris entering from break in pipe and performed point repair
35	3892 Buford Highway	No	pre-DOE	Cleaned lines and provide FOG outreach in upstream area
36	3924 Roman Court	Yes	11/21/25	Construction of capacity relief project complete.
37	3954 Memorial College Avenue	No	09/11/23	Cleaned lines and placed area on PM cleaning schedule

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
38	4004 Gladesworth Lane	No	pre-DOE	Cleaned lines and provide FOG outreach in upstream area
39	4075 Memorial Drive	No	pre-DOE	Cleaned lines and provided FOG outreach in upstream area. Lines are on PM cleaning schedule.
40	4124 Flakes Mill Road	Yes		Shoal Creek Trunk Section 1 construction in procurement.
41	4347 Flat Shoals Parkway	Yes	01/31/19	County repaired and reinstated a creek crossing along the Doolittle trunk sewer.
42	4437 Wesleyan Point	Yes		Receiving bids for bypass pumping to storage. Receiving quote for existing pump upgrades in ILS. Optimization of MBR clusters 1-4 under design.
43	4557 Meadow Creek Path	Yes		Receiving bids for bypass pumping to storage. Receiving quote for existing pump upgrades in ILS. Optimization of MBR clusters 1-4 under design.
44	4664 Flat Bridge Road	No	pre-DOE	Addressed non-potable water leak
45	4776 Snapfinger Woods Drive	No	pre-DOE	Cleaned lines and placed area on PM cleaning schedule.
46	4900 Central Drive	No	pre-DOE	Cleaned lines and placed area on PM cleaning schedule.
47	4905 Wind Cove Court	No	pre-DOE	Cleaned lines and placed area on PM cleaning schedule. Performed point repairs on offset joints.
48	5459 Bunky Way	No	06/22/23	Cleaned lines and performed point repair
49	5726 Southland Drive	No	pre-DOE	Cleaned lines, cut roots. Pipe was lined, FOG outreach provided to upstream area, and lines placed on PM cleaning schedule.
50	583 Rays Road	No	pre-DOE	Rodded the lateral to clean the blockage and performed point repair on lower lateral to fix offset joint
51	607 3rd Avenue	Yes	10/18/25	Completed construction of capacity relief project
52	608 South McDonough Street	Yes	02/23/21	Construction of local capacity relief project complete
53	6545 Swift Creek Drive	No	pre-DOE	Cleaned the lines and placed on PM cleaning schedule
54	6591 Tribble Street	No	pre-DOE	Cleaned the lines, FOG outreach provided to upstream area, and lines placed on PM cleaning schedule

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
55	101 Green Street	Yes	02/23/21	Construction of local capacity relief project complete
56	1580 Roadhaven Drive	No	pre-DOE	Cleaned the lines
57	1635 Sugar Downs Court	No	pre-DOE	Repaired creek crossing and cleaned lines; placed on PM cleaning schedule
58	1831 Briarcliff Circle	No	pre-DOE	Cleaned the lines, FOG outreach provided to upstream area, and lines placed on PM cleaning schedule
59	217 Green Street	Yes		Design for Interim Measures 3B storage complete.
60	2190 Meadowcliff Drive	No	pre-DOE	Cleaned the lines and repaired bypass pump
61	2396 Miriam Lane	No	pre-DOE	Repaired broken lateral, cleaned main line and placed on PM cleaning schedule, performed FOG outreach to upstream area
62	3546 Stanford Circle	No	pre-DOE	Cleaned the lines and placed on PM cleaning schedule
63	3731 Buford Highway	No	pre-DOE	Cleaned the lines and placed on PM cleaning schedule
64	4980 Hammermill Road	No	pre-DOE	Repaired breaker at lift station
65	8304 Union Grove Road	No	pre-DOE	Contractor bored through sewer line and performed point repair
66	1397 Witham Drive	No	pre-DOE	Replaced 34 LF of 8-inch sewer main
67	1430 Country Squire Drive	Yes	04/09/22	Completed construction of capacity relief project
68	2005 Bencal Drive	Yes	09/26/23	CIPPd pipes at and upstream of SSO site. Removed gravel from lines.
69	2311 Dunwoody Crossing	No	pre-DOE	Performed bypass pumping and repaired creek crossing
70	294 Pine Tree Circle	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule; performed FOG outreach to upstream area
71	3360 Mountain Drive	No	pre-DOE	Repaired downstream pipe, cleaned grease from upstream pipe and placed on PM cleaning schedule; performed FOG outreach to upstream area
72	3480 Mill Creek Road	No	pre-DOE	Repaired broken pipe
73	3528 Misty Valley Road	Yes	01/15/25	Package 5 Component 12 capacity relief project construction complete.

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
74	3643 Glenwood Road	No	pre-DOE	Performed point repair on 21-inch sewer main
75	3724 Eagles Beek Circle	No	pre-DOE	Repaired broken pipe
76	4203 Clevefont Road	No	pre-DOE	Removed 4" pipe obstructing flow in sewer main
77	4495 Village Spring Run	No	pre-DOE	Cleaned lines
78	4711 Bishop Ming Blvd	No	pre-DOE	Cleaned lines
79	506 South McDonough Street	Yes	02/23/21	Completed construction of local capacity relief project
80	5083 Biffle Road	No	pre-DOE	Cleaned main line and performed FOG outreach to upstream area
81	6701 Peachtree Industrial Blvd	No	pre-DOE	Performed point repair
82	2902 Mount Olive Drive	No	pre-DOE	Repaired sewer main
83	1410-1416, 1422 Cobb Branch Drive	Yes	01/15/25	Package 5 Component 12 capacity relief project construction complete
84	1420 South Hairston Road	No	11/16/21	Placed on PM cleaning schedule; performed FOG outreach to upstream area
85	1690 Chantilly Drive	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule; performed FOG outreach to upstream area
86	2000, 2200 Lithonia Industrial Boulevard	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule, performed FOG outreach to upstream area, and performed point repair
87	2175 Lawrenceville Highway	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule; performed FOG outreach to upstream area
88	2277 Munday Drive	No	pre-DOE	Cleaned debris and replaced pipe
89	2614 Lake Erin Drive	Yes	02/20/22	Water line leak in vicinity was repaired and sewers in area have been cleaned. CIPP and EPR of nearby sewer mains
90	2711 Fairlee Drive	Yes		Shoal Creek Trunk Section 1 construction in procurement. Design for Interim Measures 3A storage complete
91	3037 Toney Drive	Yes		Completed local comprehensive rehab; Shoal Creek Trunk Section 1 construction in procurement. Design for Interim Measures 3A storage complete
92	3046 East Ponce de Leon Avenue	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
93	352 Northern Avenue	No	pre-DOE	Cleaned grease, removed roots and performed repair on main
94	3548 Brookfield Lane	Yes	01/15/25	Package 5 Component 12 capacity relief project construction complete
95	3549 Panthersville Road	Yes		Shoal Creek Trunk Section 1 construction in procurement.
96	3765 Foxford Drive	No	pre-DOE	Cleaned line and cut roots
97	3907 Jerusalem Court	Yes	12/14/21	Sewer segment replaced
98	3911 Roman Court	Yes	11/21/25	Construction of capacity relief project complete.
99	4561 Amberly Court South	No	pre-DOE	Cleaned grease; most recent SSO was caused by contractor leaving plug in for flow control
100	4584 Lawrenceville Highway	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule, performed FOG outreach to upstream area
101	4948 Ardsley Drive	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule, performed FOG outreach to upstream area, and performed point repair
102	5495 East Mountain Street	No	pre-DOE	Cleaned main line and placed on PM cleaning schedule, and performed point repair
103	5557 Martina Way	No	06/22/23	Cleaned lines and performed point repair
104	5224 North Peachtree Road	No	pre-DOE	Cleaned lines and repaired broken lateral
105	3305 Lavista Road	No	pre-DOE	Cleaned lateral to restore flow
106	4547 Birch Ridge Trail	No	pre-DOE	Cleaned main of debris; building backup occurred from contractor cleaning main
107	4300 Carrollwood Drive	No	pre-DOE	Bypass pump from outside contractor failed
108	1995 Lithonia Industrial Blvd	No	pre-DOE	Cleaned main of debris and repaired break in sewer main
109	1427 Mockwell Court	No	pre-DOE	Performed point repair on creek crossing
110	1945 Ponce De Leon Avenue	No	pre-DOE	Cleaned main of bricks and debris
111	221 North Candler Street	No	pre-DOE	Repaired lateral
112	116 Clairemont Avenue	No	11/6/20	Cleaned main, performed FOG education upstream
113	2685 Milscott Drive	No	pre-DOE	Performed point repairs
114	3854 West Nancy Creek Place	No	pre-DOE	Repaired creek crossing
115	1125 Mayfield Drive	No	pre-DOE	Cleaned main and performed CIPP

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
116	2427 Briarcliff Road	No	pre-DOE	Performed point repair
117	3765 Brown Drive	No	pre-DOE	Cut roots from line
118	5005 Leeshire Trail	No	pre-DOE	Cleaned main and cut roots
119	5211 Peachtree Industrial Blvd	No	pre-DOE	Cleaned main
120	700 George Luther Drive	No	pre-DOE	Contractor adjusted bypass pump
121	2801 Candler Road	No	pre-DOE	Cleaned main
122	446 Clairemont Ave	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area
123	2012 Glenwood Avenue	No	pre-DOE	Cleaned main, performed point repairs, provided FOG outreach to upstream area
124	4037 Glenwood Road	No	pre-DOE	Cleaned lateral
125	3799 Buford Highway	No	pre-DOE	Cleaned main
126	3700 Buford Highway	No	pre-DOE	Cleaned main
127	808 Stonebridge Crescent	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
128	1442 Canoochee Drive	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
129	949 Church Street	No	8/23/22	Cleaned main of rocks and debris, placed on PM cleaning schedule
130	2649 Tanglewood Road	No	pre-DOE	Replaced one pipe segment and CIPP additional pipe segment
131	149 Norris Street	No	pre-DOE	Performed point repair
132	2881 West Fairington Parkway	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
133	6202 Peachtree Industrial Blvd	No	01/21/22	Performed point repair to remove blockage
134	4053 Bosenberry Way	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
135	5393 Greenhedge Court	No	01/23/23	Placed on PM cleaning schedule
136	3391 Warbler Drive	Yes		Shoal Creek Trunk Section 1 construction in procurement.
137	1764 Dresden Drive	No	pre-DOE	Cut roots, cleaned sand and gravel
138	4570 Memorial Drive	No	pre-DOE	Bypass pumps were removed
139	1129 Biltmore Drive	No	pre-DOE	Repaired broken main
140	4070 Greenstone Court	No	pre-DOE	Performed point repair

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
141	886 Granite Springs Lane	No	pre-DOE	Cleaned main
142	1846 Meadow Lane	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
143	212 Adair Street	No	10/04/24	Cleaned rags from main, replaced sewer main
144	2443 East Club Drive	No	04/23/24	Cleaned main of bricks, rags, and grease. CIPP complete
145	3569 Springside Drive	No	10/21/21	Cleared deodorant block holding flow
146	2716 Clairmont Road	No	pre-DOE	Cleaned main, provided FOG outreach in upstream area.
147	2849 Oakcliff Road	No	12/27/21	Conducted CIPP and manhole rehab
148	2495 Marsh Rabbit Bend	No	12/17/21	Replaced pipe with 8" DIP
149	4415 Memorial Drive	No	12/27/21	Cleaned main
150	804 Town Boulevard	No	02/19/21	Performed point repair
151	4386 Cedar Ridge Trail	No	05/25/22	Removed tree debris; reset and resealed pipe
152	1076 Village Main Street	No	10/11/22	Cleaned main, performed 2 point repairs upstream.
153	2914 Concord Drive	No	05/20/22	Replaced 140 LF of pipe
154	2225 Heritage Drive	No	04/24/22	Repaired sewer main and manhole
155	4503 Dogwood Farms Drive	No	02/23/22	Cleaned main line and placed on PM cleaning schedule
156	1357 Hearst Drive	No	05/01/23	Cleaned main, completed chemical root control
157	1205 Lake Hearn Drive	No	04/08/22	Removed bypass pump
158	981 Byrnwyck Road	No	06/07/22	Repaired creek crossing
159	1955 Montreal Road West	No	04/06/22	Cleaned debris and repaired leak in pipe
160	255 South Columbia Drive	Yes		Design for Interim Measures 3B storage complete.
161	3402 Northbrook Drive	No	02/17/23	Cleaned main, assigned to chemical root control
162	3239 Rehoboth Drive	No	04/16/22	Sealed leak in pipe
163	3752 Salem Springs Court	No	12/08/23	Cleaned grease and debris, rehabbed manhole and CIPP sewer main
164	4104 Tahoe Court	No	10/20/23	Cleaning complete, on CARLs list
165	2490 Brookcliff Way	No	12/03/22	Replaced broken pipe with steel pipe
166	4025 Kings Causeway	No	02/27/23	Cleaning complete, on CARLs list

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
167	511 Oakview Road	No	09/11/23	Cleaning complete, FOG education complete
168	1136 Parkwood Trace	No	09/21/22	Replaced portion of aerial creek crossing
169	2097 Vineyard Walk	No	02/20/23	Cleaning completed, on CARLs list, chemical root control complete
170	3841 Kensington Road	No	08/21/23	Cleaning completed, on CARLs list
171	3088 Rockaway Road	No	02/06/23	Reset pipe connection to manhole, supported and sealed
172	4061 Wintersweet Drive	No	08/10/23	Removed asphalt from sewer main
173	7320 Rockland Road	No	07/29/24	Cleaned debris and grease from sewer main.
174	111 Church Street	No	01/25/23	Repaired leak in sewer main
175	115 Perimeter Center Place	No	04/29/25	Cleaning complete, added to CARLs list
176	3664 Rockbridge Road	No	02/23/23	Bypass pumping completed
177	2200 Fair Oaks Road	No	03/23/23	Bypass pumping completed
178	2157 Tucker Industrial Road	No	01/27/23	Sewer main replacement completed
179	2740 Tryon Place	No	08/22/23	Heavy cleaning completed, monitor for additional cleaning
180	1034 McConnell Drive	No	06/26/25	Point repairs and cleaning completed.
181	1116 Fuller Road	No	07/17/24	Completed point repair and CIPP.
182	481 Pennybrook Drive	No	03/17/23	Repaired forcemain
183	3388 Garden Mill Lane	No	02/16/24	Cleaned sewer mains of grease
184	478 Sherwood Circle	No	11/08/23	Cleaned sewer mains of grease
185	2930 Belvedere Lane	No	06/22/23	Completed cleaning and FOG education, added to CARLs list
186	7566 Knoll Hollow Road	No	12/01/23	Cleaned construction debris from sewer main
187	1680 Clairmont Place	No	11/26/23	Completed EPR, cleaned sewer mains, performed chemical root control.
188	4250 Perimeter Park South	No	05/05/23	Cleaning complete, removed contractor's plug
189	2890 Cedar Creek Drive	No	06/15/23	Cleaning complete, chemical root control performed
190	421 Glendale Road	No	01/19/24	Construction complete in area, bypass pumps moved.
191	3070 Briarcliff Road	No	08/21/24	Cleaned sewer mains of grease
192	2477 Kings Point Drive	No	07/19/23	Cleaned sewer mains of grease and debris

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
193	3248 Chamblee Dunwoody Road	No	12/22/23	Cleaned sewer mains of debris
194	3174 Lynnray Drive	No	08/10/23	Cleaned sewer mains of grease
195	2182 Thorncliff Drive	No	03/29/24	Cleaned sewer mains of grease and debris, CIPP of sewer main
196	1531 Woodfern Drive	No	06/19/25	Initial cleaning complete, bypass pump removed
197	3273 Pinehill Drive	Yes	05/14/25	Package 5 Component 12 capacity relief project construction complete
198	1354 Weston Drive	Yes	01/15/25	Package 5 Component 12 capacity relief project construction complete
199	148 Desmond Drive	No	04/24/25	Manhole rehabilitation complete
200	3423 Tulip Drive	Yes	01/15/25	Package 5 Component 12 capacity relief project construction complete
201	3088 Rockaway Road	No	05/31/24	Manhole replaced
202	4601 Buford Highway	No	01/02/24	Heavy cleaning completed to remove grease
203	1127 Village Street	No	11/29/23	Completed point repair to remove root ball
204	3569 Larkspur Terrace	No	11/26/24	Construction in area complete and bypass pumps were removed
205	300 Hatton Dr	No	03/28/24	Replaced sewer main
206	1953 Crescent Centre Boulevard	No	12/06/23	Bypass pumps were removed
207	3009 Fair Creek Court	No	04/22/24	Cleaned sewer mains of grease
208	5062 Stone Trace	No	11/18/24	Manhole rehab and CIPP complete
209	4265 Glenwood Road	No	11/26/24	CCTV, cleaning and EPR complete
210	1530 Burnstone Drive	No	02/12/24	EPR complete. Met with contractor on cleaning protocols
211	1080 Bailiff Court	No	05/14/24	CCTV and cleaning sewer mains of grease complete.
212	725 San Miguel Drive	No	03/28/24	EPR complete and bypass has moved from this location
213	1517 Eidson Hall Drive	No	03/11/24	Creek crossing replaced
214	2317 Briarcliff Road	No	05/22/25	Heavy cleaning performed, bypass removed.
215	1817 Clifton Road	No	05/06/24	Cleaned sewer mains of grease
216	2413 Carlow Court	No	03/28/24	Completed point repair

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
217	2121 Tucker Industrial Road	No	05/31/24	Completed sewer rehabilitation and removed bypass
218	3045 Wadsworth Mill Place	No	02/21/25	Cleaned sewer mains, completed EPR
219	3172 Bobbie Lane	No	01/16/25	Construction completed in area, bypass pumps removed
220	1442 Canoochee Drive	No	10/15/24	Cleaned sewer mains
221	6682 Peachtree Industrial Blvd	No	05/01/24	Construction is complete in this area, bypass pumps have been removed
222	2417 Dawn Drive	No	02/04/25	Bypass pumps removed from area.
223	4109 Hideaway Drive	No	08/29/25	Construction complete in area, bypass pumps removed from site
224	3066 Buford Highway	No	05/24/24	Construction is complete, bypass pumps have been removed from site
225	5250 Snapfinger Park Drive	No		Cleaned sewer mains, CCTV complete, awaiting data for root cause analysis
226	3752 Cherry Ridge Blvd	No	07/13/24	Cleaned sewer mains of grease and debris. Completed EPR
227	4165 Hideaway Drive	No	08/29/25	Construction complete in area, bypass pumps removed from site
228	2547 Lithonia West Drive	No	08/06/24	Cleaned sewer mains of grease, completed EPR
229	6009 Memorial Drive	No	07/09/24	Cleaned sewer mains of grease
230	4027 Flakes Mill Road	No	09/26/25	cleaning of small diameter and trunk sewers complete
231	3902 Memorial College Ave	Yes	11/14/25	CIPP complete
232	3850 Memorial Drive	No	01/16/25	Construction complete in area, bypass pumps removed from site
233	1143 Banbury Cross	No	01/16/25	Construction complete in area, bypass pumps removed from site
234	1595 Moncrief Circle	No	06/18/25	EPR and CIPP complete
235	921 2nd Street	No		Cleaned sewer mains of debris, CCTV complete, awaiting data for root cause analysis
236	1579 Drayton Woods Drive	No	09/11/24	EPR Complete
237	3565 Lawrenceville Highway	No	07/01/25	EPR and CIPP complete
238	3908 Woburn Road	No	01/21/25	Cleaning and EPRs complete

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
239	3342 North Druid Hills Road	No	09/19/25	Repair of lateral and manhole complete
240	5009 Memorial Drive	No	12/05/24	Completed EPR
241	2473 East Club Drive	No		Cleaned sewer mains of grease, CCTV complete, EPRs being scheduled
242	5440 North Peachtree Road	No	12/09/24	EPR complete, verifying adequate fix
243	822 North Indian Creek	No	12/17/24	Cleaning/removal of blockage complete
244	2100 Winterspark Drive	No	06/12/25	Cleaning/removal of blockage and manhole rehab complete
245	2402 Tiffany Circle	No		CCTV complete, scheduling pipe rehab
246	4323 Winters Chapel Road	No	06/12/25	Cleaning/removal of blockage and manhole rehab complete
247	1431 Conway Road	Yes		Design for Interim Measures 3B storage complete.
248	2829 Dresden Drive	No	04/02/25	Cleaning of blockage complete
249	3052 Wells Street	No	08/01/25	EPR and cleaning complete
250	773 Shadow Lakes Drive	No	04/01/25	EPR Complete
251	3001 McCall Drive	No		Sewer rehabilitation planned
252	5100 East Ponce De Leon Avenue	No	04/01/25	Cleaning complete, FOG outreach to apt complex upstream on private sewers
253	1302 Mannbrook Drive	No	04/10/25	Creek crossing repair complete, removed bypass pumps
254	1529 Harbour Oaks Road	No	08/29/25	Construction complete in area, bypass pumps removed from site
255	400 Perimeter Center Terrace	No		CCTV complete, awaiting data for root cause analysis
256	3575 Oakvale Road	No		CCTV complete, awaiting data for root cause analysis
257	1421 Mockwell Court	No	05/26/25	Sewer rehabilitation complete
258	1471 Northeast Expressway	No		EPR complete, verifying adequate fix
259	1377 Hearst Drive	No		CCTV assigned
260	1335 Church Street	No		Performing root cause analysis
261	2595 Rockcliff Road	No		CCTV complete, awaiting data for root cause analysis
262	1659 Briarcliff Road	No		Crown of pipe patched, verifying adequate fix
263	1111 Rankin Street	No		CCTV complete, awaiting data for root cause analysis

Attachment B – Priority Fix List Status

PFL Site #	Address	Capacity Related	Date of Adequate Fix ⁸	Ongoing/Complete Work
264	2443 Hunting Valley Drive	No	09/02/25	EPR complete and bypass removed
265	3370 Panthersville Road	No		TISCIT complete, cleaning underway
266	1011 Lenox Valley	No		Performing root cause analysis
267	3294 Lansbury Village Drive	No		Performing root cause analysis
268	2542 Maclaren Circle	No		CCTV complete, awaiting data for root cause analysis
269	3251 Wake Robin Trail	No	11/18/25	CIPP complete, bypass removed
270	446 Clairemont Avenue	No		CCTV assigned

Part II Sanitary Sewer Overflow Trends Analysis

Executive Summary

As required by Section IX, Reporting Requirements 58(b) of the CD, a trends analysis is to be submitted on an annual basis, as follows:

“A trends analysis of the number, volume, average duration, and cause of the County’s Sanitary Sewer Overflows (SSOs) for the previous twenty-four (24) month period.”

This trends analysis includes the 24-month period of 2024 and 2025 but also includes data from 2023 for reference. 2017 is the first year the County implemented an updated SSO reporting process, which has been consistently applied through 2025. As required by the CD, the report addresses SSO types (spills, overflows, and building backups) as applied to the various data and trends. This analysis consists of the following sections:

- Section 1 – Classification of SSO Types and Causes
- Section 2 – Number and Volume of SSOs
- Section 3 – Average Duration of SSOs
- Section 4 – Causes of SSOs
- Section 5 – Other Trends

Beginning with the 3rd Quarter 2022 Quarterly Report, the County began to separate reporting of “SSOs by Others.” An SSO by Others is an SSO caused by a wastewater collection system that is owned and maintained by a utility outside of the County. From 2022 through 2025, 55 SSOs by Others were reported, 2 of them in 2025. Unless otherwise specified, all figures in Section II of this report will exclude data from SSOs by Others.

Of the SSOs occurring in the County, and not caused by others, during 2025, 39 were wet weather SSOs. The County determined that while there were no Severe Natural Condition events in 2025, there was one storm equivalent to a 2-year storm on February 12-13, 2025.

The County has identified that many of these wet weather SSOs are due to capacity limitations within the large-diameter trunks and have completed the design to address these limitations and provide additional capacity. In 2025, 18 of the wet weather SSOs occurred within Snapfinger Basin which has planned capacity upgrades designed. Other sewer rehabilitation and smaller-diameter capacity projects have and will continue to be completed in the interim.

Overall, the number of SSOs per year has decreased by over 50 percent since the CD was lodged in 2012. For maintenance-related SSOs, this is largely attributable to the County’s MMS program including sewer cleaning, the FOG program, and extensive public education campaigns. Figure ES-1 shows the number of SSOs from 2023 to 2025. A higher number of SSOs were experienced in 2024 compared to 2023 and 2025 which can be attributed to a higher number of significant rain events resulting in an increase in I/I-related SSOs.

Figure ES-1 Reported SSOs per Year (2023–2025)



Figure ES-2 shows the number of spills, or discharges of wastewater, that reach waters of the United States or the State. The number of spills, excluding spills by others, increased from 252 in 2023 to a peak of 362 in 2024, again, attributed to the increase in significant wet weather events, before ending 2025 at 150 spills.

Figure ES-2 Total Spills by Year (2023–2025)


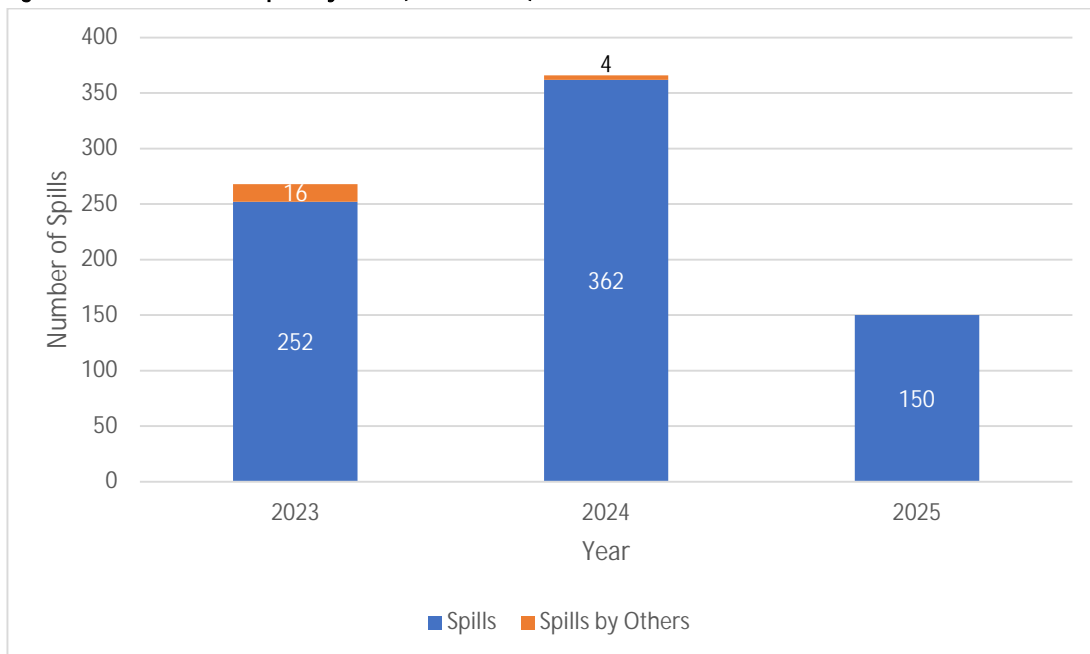


Figure ES-3 shows the total annual reported SSO volumes for 2023 through 2025. The largest contributors to spill volume are structural SSOs involving breaks on large diameter sewer trunks and wet weather-caused SSOs. As stated previously, 2024 experienced a number of significant wet weather events, including Hurricane Helene.

Figure ES-3 **Reported Volumes of SSOs by Year (2023–2025)**

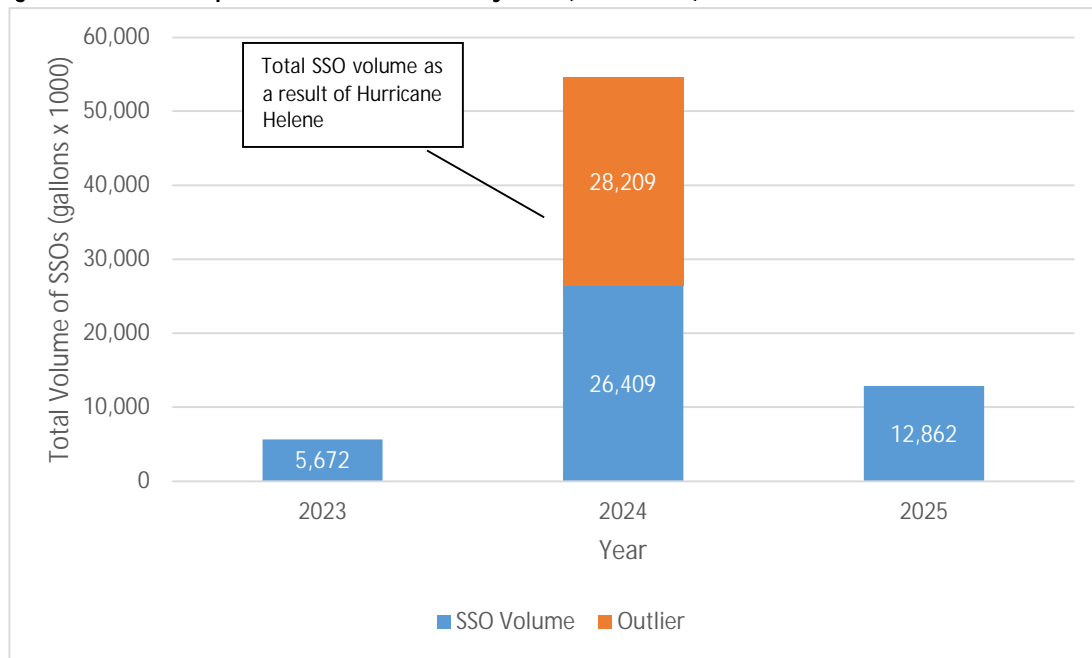


As shown on Figure ES-4, the number of spills attributable to the shown causes decreased from 2024 to 2025.

Furthermore, as the County maintains an extensive flow monitoring network, continues its efforts to conduct sewer condition assessment, and continues to implement MMS programs, the County can more readily identify SSOs. With a flow monitoring network of more than 300 flow meters throughout the County that provides data that can be reviewed on a daily, weekly, and monthly basis, any sudden changes in flow behavior that may indicate a possible SSO are called in for further investigation. This has resulted in prevention of potential SSOs. In 2025, the flow monitoring team detected and prevented seven potential SSOs. As an example, on March 21, 2025 when performing maintenance on a flow monitor, the crew noticed the manhole was starting to hold flow. A call was made to dispatch to investigate. CCTV of the line showed a cross bore from another utility. A point repair was completed on the sewer main to return to useful capacity.

Sewer condition assessment work identifies defects that can contribute to SSOs. Since 2016, as part of the MMS program, DWM increased the number of inspections and put resources in the field in remote places, such as along streams and in ravines that are generally out of sight. If SSOs were found, DWM subsequently reported the findings appropriately.

DWM's increased stream sampling effort also continues to help identify SSOs that would have previously remained unknown. Source tracking from elevated fecal counts in stream samples identified five SSOs that DWM was able to locate and address.

Figure ES-4 Total Spills by Year by Cause Category (2023–2025)

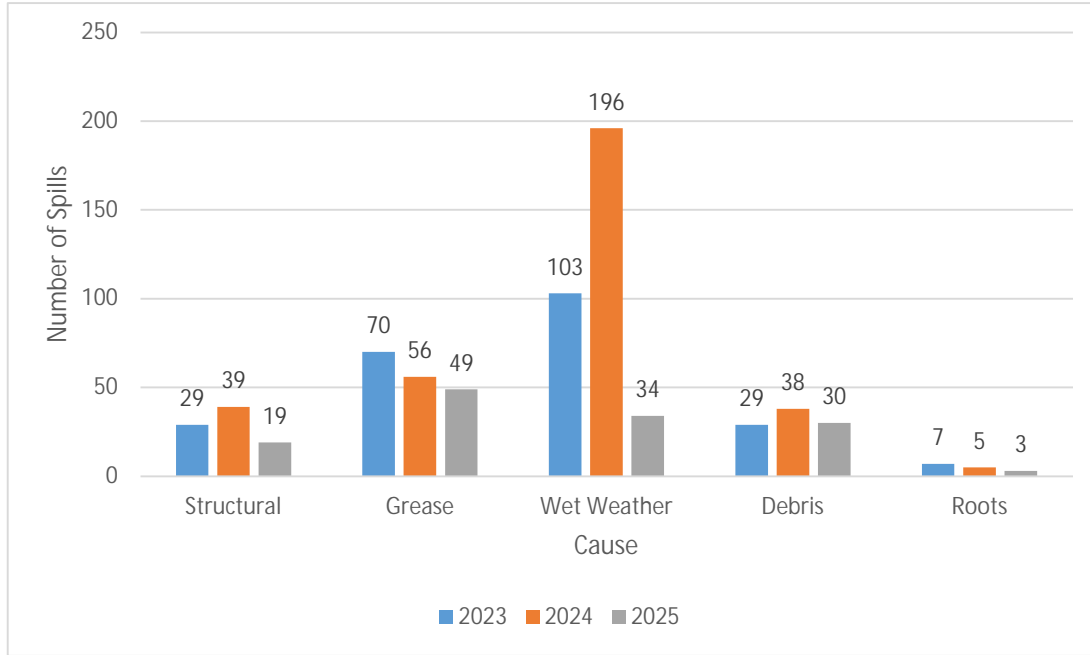

Notes:

Cause Categories may include more than one cause.

Some spills appear in more than one Cause Category.

Other causes for spills not shown in this figure include pump failure, vandalism, contractor-related, etc.

1. Classification of SSO Types and Causes


The CD requires a trend analysis of the prior 24-month period. Although 2017 was the first year the County implemented an updated SSO reporting process that has been consistently applied through 2025, this report focuses on trends from 2023 through 2025.

DWM categorizes each SSO that occurs as one of three types as defined in the CD. This initial categorization is based on multiple factors, including details provided by the reporting party, details provided by County response crews, and reports from County laboratories. As details of each SSO are learned, an SSO might be re-categorized accordingly. Definitions from the CD of each type of SSO are as follows:

- **Spill:** a discharge of wastewater from the WCTS, or from a wastewater treatment facility caused by problems in the WCTS, that reaches waters of the United States or the State, including a prohibited bypass, but not including other discharges from a point source that is specified in the National Pollutant Discharge Elimination System permits.
- **Overflow:** a release of wastewater from the WCTS, or from a wastewater treatment facility caused by problems in the WCTS, that does not reach waters of the United States or the State.
- **Building Backup:** a wastewater backup into a building that is caused by blockages, malfunctions, or flow conditions in the WCTS; however, provided that a wastewater backup into a building that is caused by a blockage or other malfunction of a private lateral, or other piping or conveyance system that the County does not own or operate, is not a building backup.

Figure 1-1 shows the distribution of SSOs by type for 2025 as compared to 2024. Spills account for the majority of the SSOs followed by overflows then building backups. Beginning in the 3rd Quarter 2022 Report, the County reported SSOs by Others separately. SSOs by Others are SSOs that occur from County laterals, but the root cause is attributed to sewer mains owned and maintained by other utilities. As a result of ongoing coordination with City of Atlanta, SSOs within the County as a result of capacity issues on Atlanta owned sewer mains are now being reported by the City.

Figure 1-1 SSOs by Type (2024–2025)

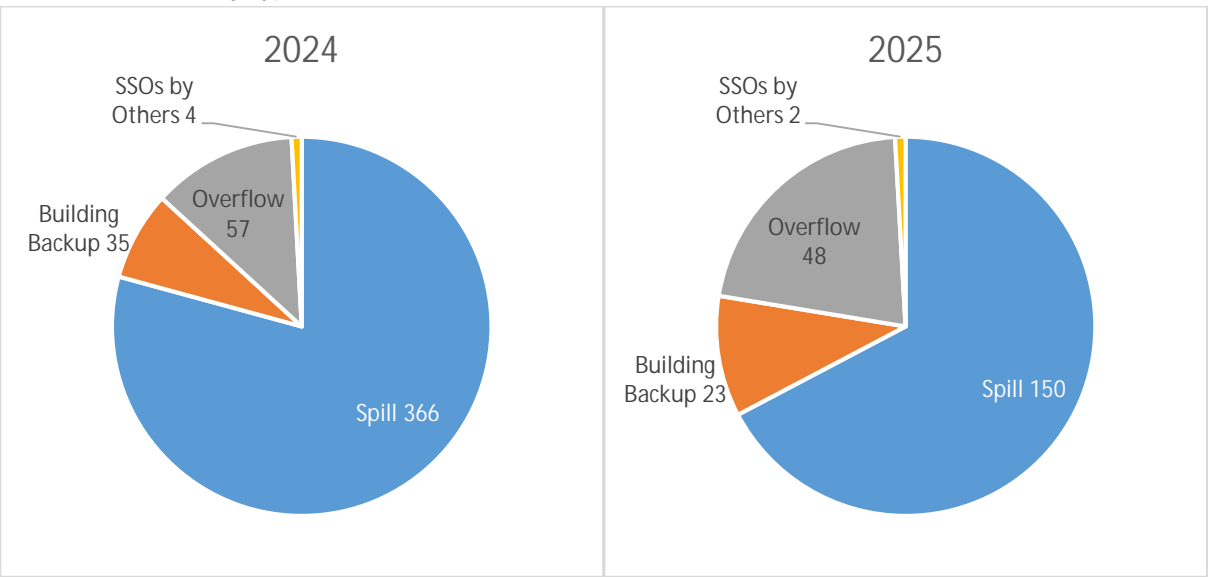

In addition to categorizing SSOs based on type, the County investigates the root cause of SSOs and classifies the events accordingly. Table 1-1 lists the types of causes used by DWM for the period of 2017 to 2025. This investigation and classification includes a review of the results of assessment tools, such as CCTV, and includes consideration of whether other sections of the WCTS might be vulnerable to a similar

SSO event. To identify and prevent future SSOs, a portion of this analysis focuses on causes determined to be maintenance-related. For this trends analysis, the following terms are defined:

- Maintenance-Related: an SSO caused by grease, roots, debris, or any combination thereof.
- Other: an SSO caused by anything other than grease, roots, debris, or any combination thereof.

Table 1-1 SSO Causes Used by DWM

Cause Code	Cause Title	Description
BRK LN/STR	Broken line/structure	Broken pipe, manhole, force main, or other appurtenance.
CC	County contractor	Caused by a contractor performing work for the County.
CRK BRK	Creek crossing break	Structural failure of sewer infrastructure at a creek crossing.
DB	Debris	Solids that have collected in a pipe or manhole.
GR	Grease	Build-up of grease in a pipe or manhole.
GRDB	Grease and debris	Combination of grease and solids build-up in a pipe or manhole.
GRRT	Grease and roots	Combination of grease build-up and root intrusion in a pipe or manhole.
GRRTDB	Grease, roots, and debris	Combination of grease and solids build-up and root intrusion in a pipe or manhole.
I&I	Infiltration and Inflow	Occurs when I/I enters the system and uses existing capacity, not necessarily associated with a wet weather event.
LFT STN FLR	Lift station failure	Failure at a lift station.
MH	Manhole	Caused by structural defect at or in manhole.
OTH	Other	Use of this code requires a detailed description.
OUTSIDE CON	Outside contractor	Caused by a contractor not performing work for the County.
PMP FLR	Pump failure	Caused by failure during bypass pumping.
RT	Roots	Intrusion of roots into a pipe or manhole.
RTDB	Roots and debris	Combination of root intrusion and solids build-up in a pipe or manhole.
STORM	Storm	Caused by a storm. Includes wet weather capacity, failures at lift stations resulting from lightning strikes or storm-induced power outages, and maintenance-related SSO during storm events.
TREE	Tree (fallen)	Damage caused by falling trees.
UNK	Unknown	Used when no clear cause can be identified. The in-depth data review conducted in 2016 identified additional SSOs where the cause could not be determined retroactively. For those instances, the UNK code was used.
VAND	Vandalism	Intentional damage caused by vandals.

2. Number and Volume of SSOs

As shown on Figure 2-1, when excluding SSOs by Others, the number of SSOs per year decreased by 48 percent from 2024 to 2025. 2024 was a year of increased severe wet weather events that resulted in more I/I SSOs than average. Comparing 2025 to 2023 which was more similar in annual rainfall still showed a 28% decrease in SSOs. Overall, the number of SSOs has decreased by more than 50% since the CD was lodged in 2012. 2025 has the lowest number of SSOs reported since the beginning of the CD, including 2016, a drought year. There is an overall decreasing trend in the number of SSOs, particularly dry weather SSOs, since 2012, which can be attributed to the County's MMS programs including sewer cleaning, root control, the FOG program, and extensive public education campaigns. Several program improvements have allowed the County to identify and respond to SSOs more readily. These improvements include expansion of the County's flow monitoring network, further progress of sewer system investigation activities, new stream sampling protocols to detect spills, and implementation of the Cityworks work order management system to track identification and response to SSOs.

Figure 2-1 Reported SSOs per Year (2023–2025)



Figure 2-2 shows annual rainfall for the same period of record (2023–2025). In previous reports, the County would utilize the NOAA Rainfall Scorecard for Atlanta, which utilizes a rain gauge at Hartsfield Jackson International Airport. In conducting the SSO trends analysis, further evaluation was conducted to review USGS rain gauges that were located within the County to understand the effects of localized rain events. Utilizing USGS rain gauge 2203900, located at South River and Flakes Mill Road, located near the Snapfinger AWTF and in closer proximity to many of the wet weather SSOs was determined to be more applicable to the rainfall analysis. Total annual rainfall can vary by 5 – 6 inches between the NOAA and USGS rain gauges, with monthly variations as great as 2.5 inches.

Utilizing the rain gauges, total rainfall for 2025 decreased by 15 - 22 inches from 2024 levels. Annual rainfall levels of 41-46 inches are less than the average annual rainfall for the metro Atlanta area (~50 inches). There were 9 wet weather events greater than 1 inch total rainfall in 2025 compared to 16 in 2024. While there were no Severe Natural Condition events in 2025, there was one event that was equivalent to a 2-year storm on February 12-13, 2025.

Figure 2-2 Annual Precipitation (inches) (2023–2025)


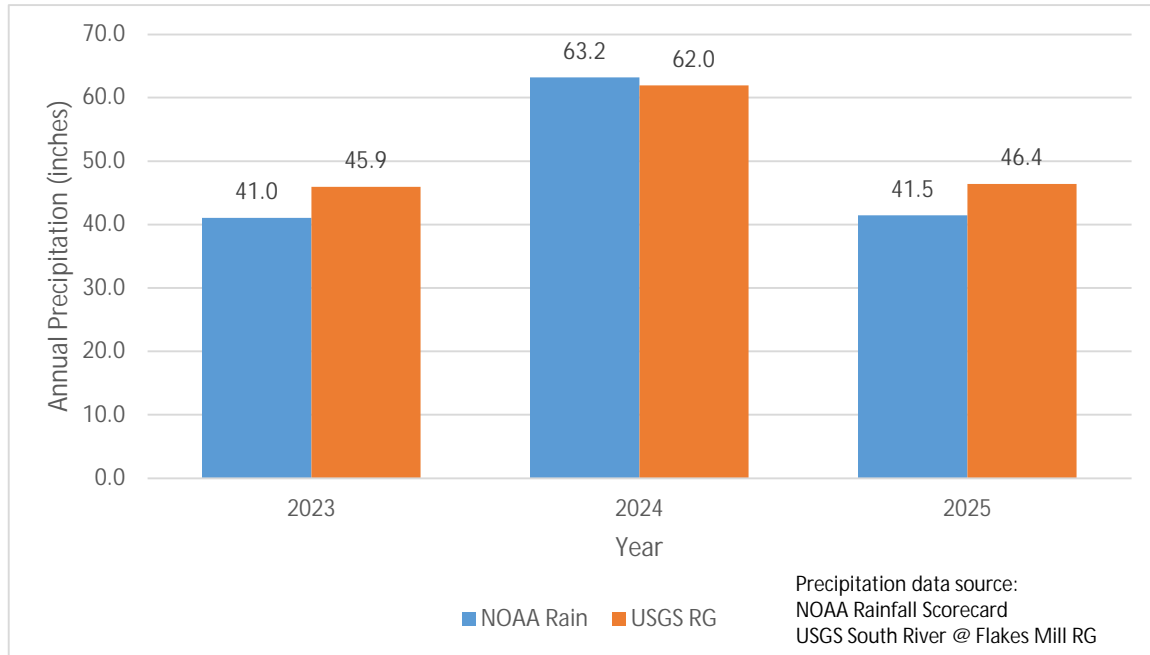


Figure 2-3 presents the total volume (gallons) of SSOs for 2023–2025. There was less rain observed in 2025 with one 2-year storm observed. Over 50% of the total SSO volume, 7.7 MG, occurred due to I/I from that event. While cleaning and FOG program enforcement have decreased maintenance-related SSOs overall, wet-weather-related SSOs are expected to decrease as the County begins construction on large-capacity projects.


Figure 2-3 Reported Volume of SSOs per Year (2023–2025)

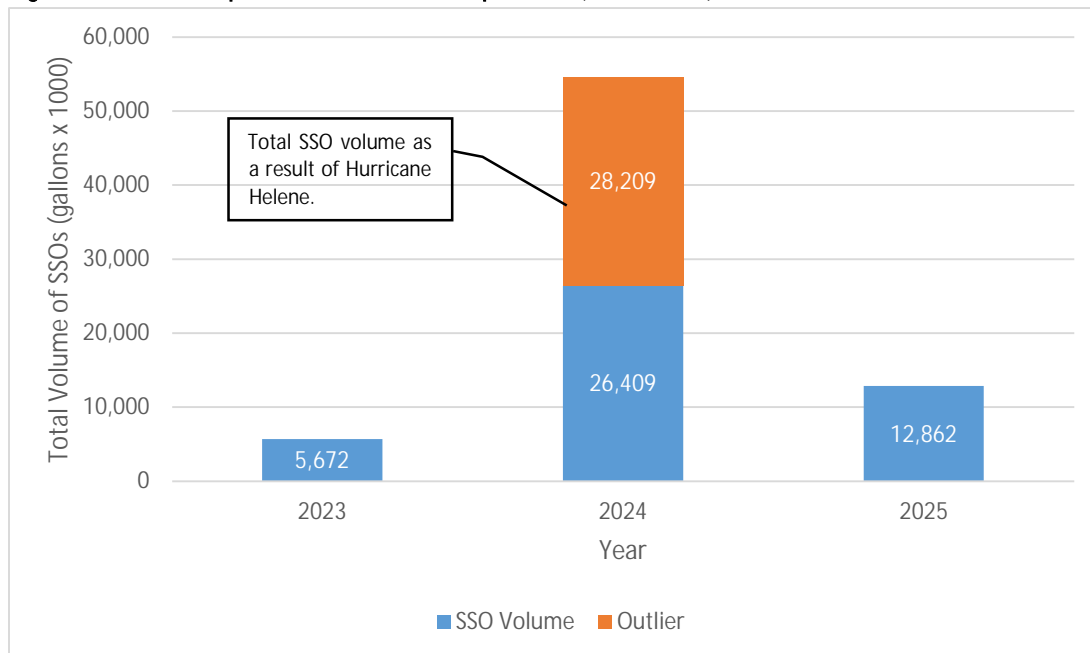

Figures 2-4 and 2-5 show the number of maintenance-related SSOs and the associated annual volumes, respectively, from 2023 through 2025. From a peak of 238 SSOs in 2014 to 126 SSOs in 2025, DWM has reduced maintenance-related SSOs by 47 percent through a steady downward trend. In 2022, the County began to review the details of SSOs with a cause of unknown. If the work order comments indicate the

SSO is due to an unknown blockage as opposed to an unknown cause altogether, it is now reported as a maintenance issue.


Figure 2-4 Maintenance-Related SSOs per Year (2023–2025)

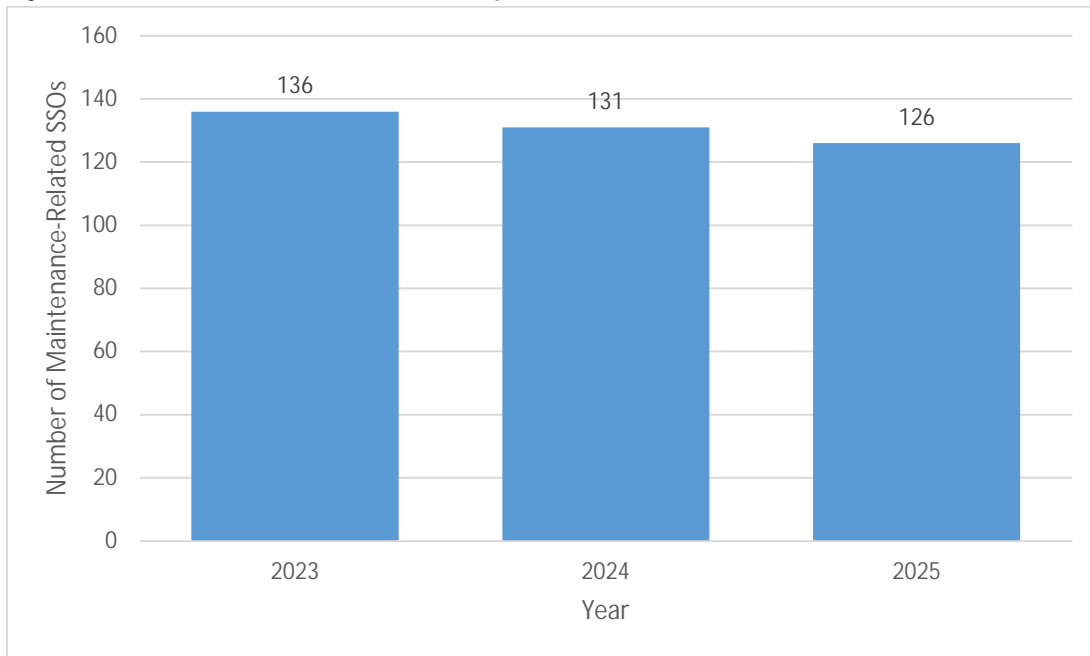

Note: Maintenance-related SSOs are caused by grease, roots, debris, or any combination thereof.

The volume of maintenance-related SSOs for 2025 decreased from 2024. On average, maintenance related SSOs from 2025 are 7,000 gallons per SSO. Some maintenance related SSOs exceed that volume due to the size of the sewer main and quantity of flow or due to an extended duration in locating the source of the SSO. DWM believes decreases in the general trend of maintenance related SSO is attributable to the County’s implementation of MMS programs, such as sewer cleaning, root control, Cityworks, and the effectiveness of the FOG Management Program and public education campaigns.

Figure 2-5 Volume of Maintenance-Related SSOs per Year (2023–2025)

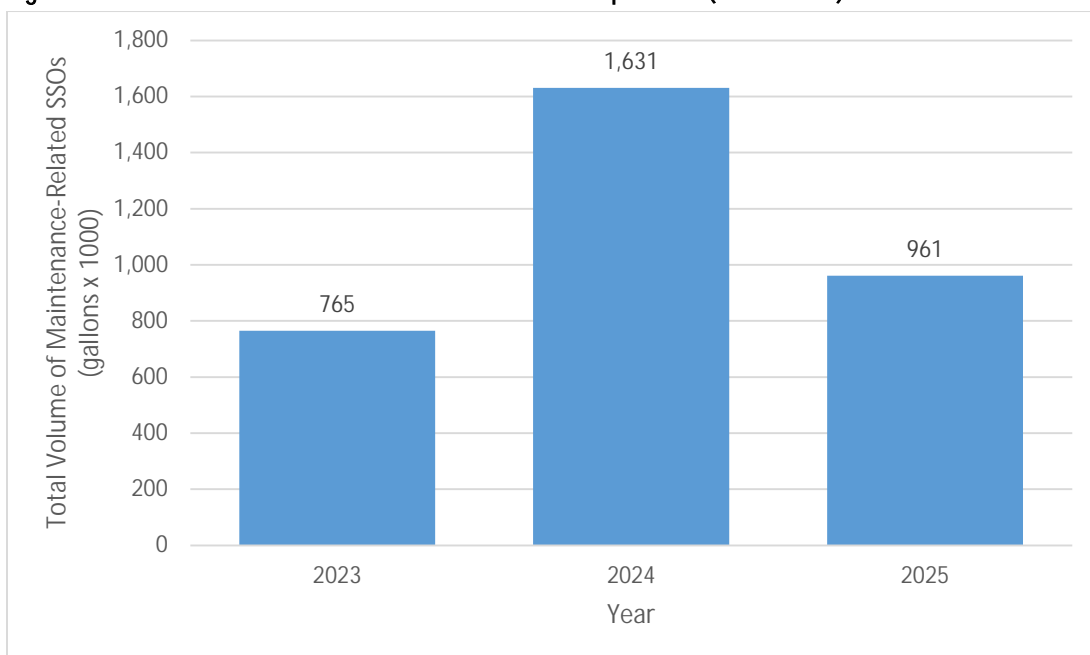


DWM's continued focus on its comprehensive cleaning program, chemical root control, and easement clearing has resulted in addressing the number and volume of maintenance-related SSOs in 2025. Because the assessment of the PASARP areas was substantially completed in 2017, a new focus on rehabilitation was seen in 2018 as DWM procured two design-build rehabilitation contracts, issued Task Orders to engineering firms with existing contracts for the design of four additional rehabilitation packages, and also started rehabilitation construction in the PASARP areas. In subsequent years, additional contracts have continued making significant strides in rehabilitation but also in design and construction of capacity relief projects. While addressing the structural integrity of the sewer assets, rehabilitation will address and reduce sources of I/I to help minimize SSOs that occur because of wet weather.

3. Average Duration of SSOs

Duration of SSOs are calculated from the time the SSO was reported until it is resolved. This parameter depends on how the SSO was identified, how quickly the source can be located and accessed, and the cause of the SSO. The average SSO duration from 2023 through 2025 was approximately 6.8 hours, when removing one outlying SSO from September 11, 2024 as shown on Figure 3-1.

Figure 3-1 Average SSO Duration by Year (2022–2024)

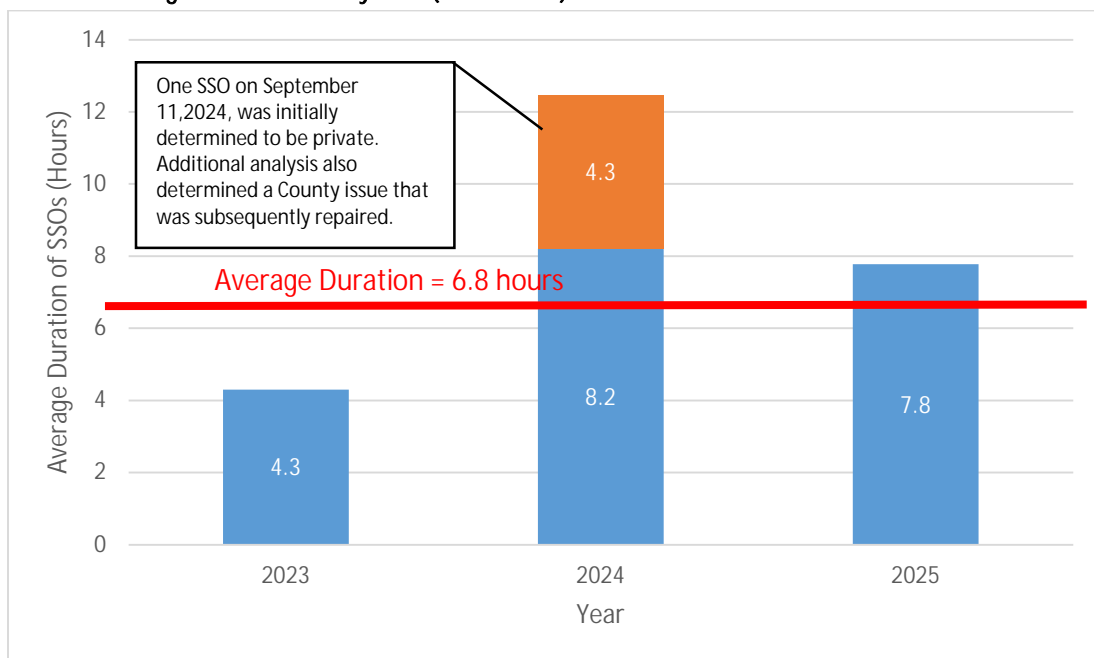

While receiving calls is the primary source of SSO reporting, as noted previously, DWM also locates spills using in-house programs, including flow monitoring and stream sampling. As data is collected that indicates a possible SSO, whether through a sudden, significant change in metered flows or an increase in fecal count in waterways, DWM investigates through site visits and creek walks. In 2024, DWM identified five SSOs from stream sampling. The duration of a spill also heavily depends on the flow restoration actions needed to address the SSO. Evaluating the duration of SSOs is more effectively done by grouping causes that have the same general flow restoration action. Table 3-1 lists all causes noted in Table 1-1 and maps them to a broader group.

Table 3-1 Mapping Cause to Cause Groups


Cause	Group
BRK LN/STR	Structural
CC	Contractor
CRK BRK	Structural
DB	Maintenance
GR	Maintenance
GRDB	Maintenance
GRRT	Maintenance
GRRTDB	Maintenance
I/I ^a	Wet Weather
LFT STN FLR	Pump Failure

Cause	Group
MH	Structural
OTH	Other
OUTSIDE CON	Contractor
PMP FLR	Pump Failure
RT	Maintenance
RTDB	Maintenance
STORM	Wet Weather
TREE	Structural
UNK	Unknown/Maintenance
VAND	Vandalism

^a All I/I SSOs recorded to date were wet-weather-related.

Figure 3-2 presents average durations for all SSOs from 2023 through 2025. Three causes had durations that were greater than average: wet weather structural, and other.


Figure 3-2 Average SSO Duration by Cause (2023–2025)

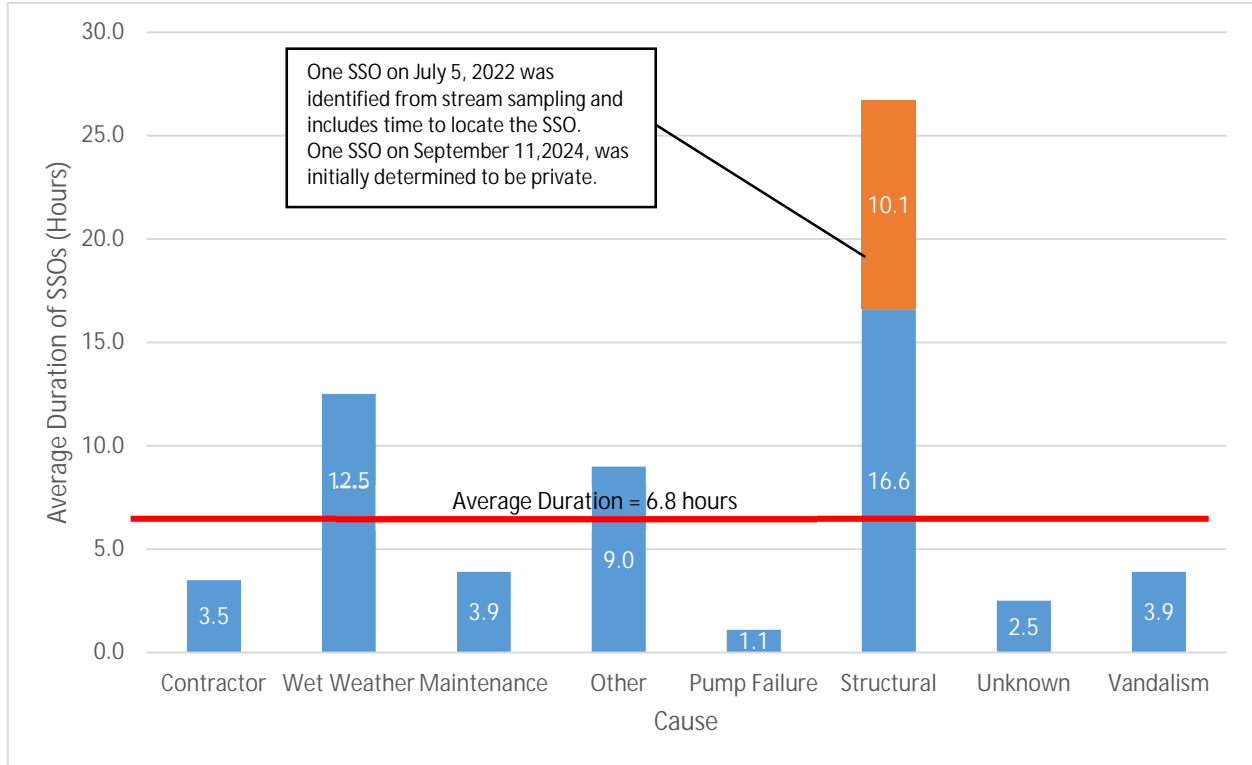

4. Causes of SSOs

Maintenance-related SSOs, including grease, roots, and debris, decreased from 2012 to 2025 by 47 percent, a result, in part, of increased sewer cleaning and the County's commercial FOG Management Program and Public Education Programs. In reviewing data from the past 3 years, blockages continue to account for more SSOs than any other cause (39 percent) and only represent the third greatest volume (5 percent) of all SSO causes (refer to Figure 4-1). The cause with the greatest volume is wet weather, and the County is continuing to take steps to address impacts from storm-related events. Specifically, the County has undertaken follow-up and corrective action for private I/I and stormwater connections to the sanitary sewer in the Priority Areas. In 2025, 930 cleanout caps were replaced by DWM in the field. The continuation of these programs, along with the rehabilitation construction that is now underway, will begin to eliminate sources of I/I within the sewer system and provide additional capacity to help reduce the SSOs that occur because of wet weather.

Figure 4-1 SSOs by Count, Volume, and Cause (2023–2025)

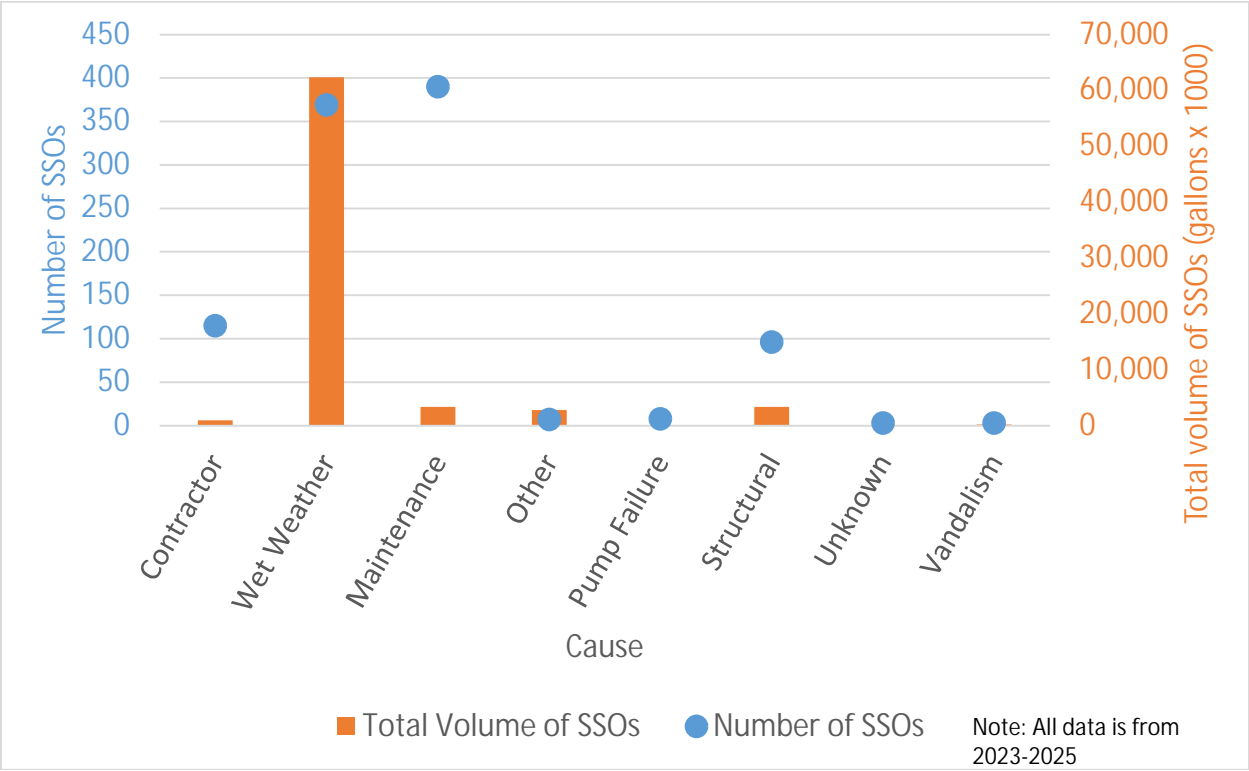

Selected causes can be grouped into categories that help assess the effectiveness of DWM’s efforts to reduce SSOs. These broader categories are grease, structural, wet weather, and debris. Table 4-1 lists the causes assigned to each category. As shown on Figure 4-2, there has been a decrease in structural and wet weather SSOs, and grease, root and debris SSOs have remained steady compared to 2024 levels.

Table 4-1 Mapping Cause to Cause Categories


Cause	Grease	Structural	Wet Weather	Debris
BRK LN/STR		STRUC		
CC				
CRK BRK		STRUC		
CRK BRN		STRUC		
DB				DB

Table 4-1 Mapping Cause to Cause Categories

Cause	Grease	Structural	Wet Weather	Debris
GR	GR			
GRDB	GR			DB
GRRT	GR	STRUC		
GRRTDB	GR	STRUC		DB
I&I ^a			WET WEATHER	
LFT STN FLR				
MH				
OTH				
OUTSIDE CON				
PMP FLR				
RT		STRUC		
RTDB		STRUC		DB
STORM			WET WEATHER	
TREE				
UNK				
VAND				

^a All I/I SSOs recorded to date were wet-weather-related.


Figure 4-2 SSOs by Year by Cause Category (2023–2025)

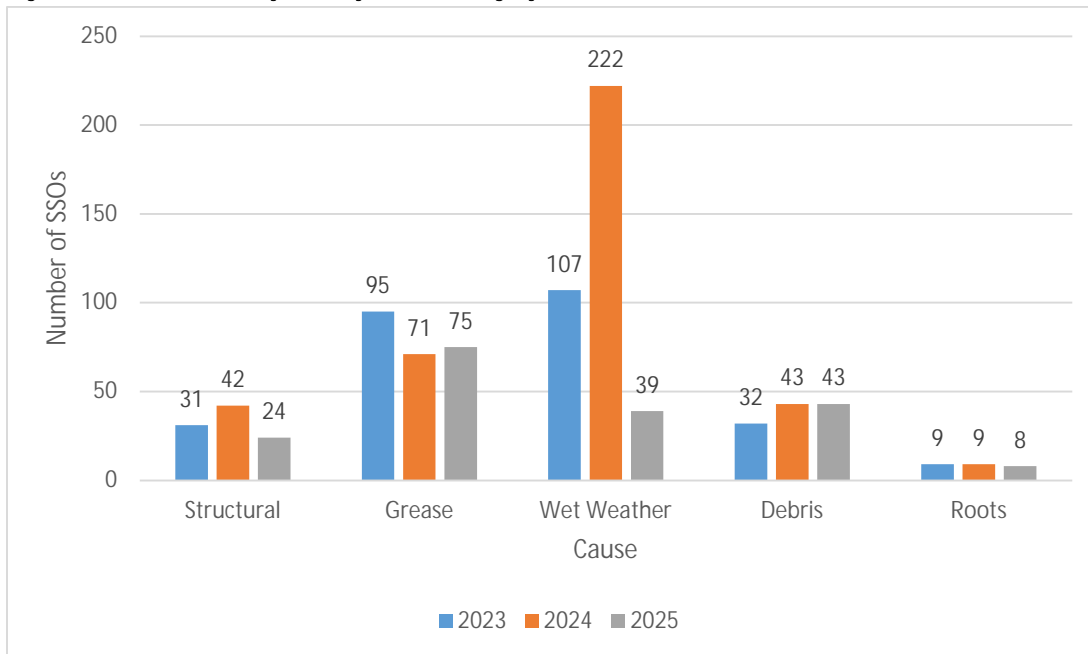

Notes:
Cause Categories may include more than one cause. Some SSOs appear in more than one Cause Category.
Other causes for spills not shown in this figure include pump failure, vandalism, contractor-related, etc.

These same cause categories, when applied specifically to spills, show similar trends (refer to Figure 4-3).


Figure 4-3 Spills by Year by Cause Category (2023–2025)

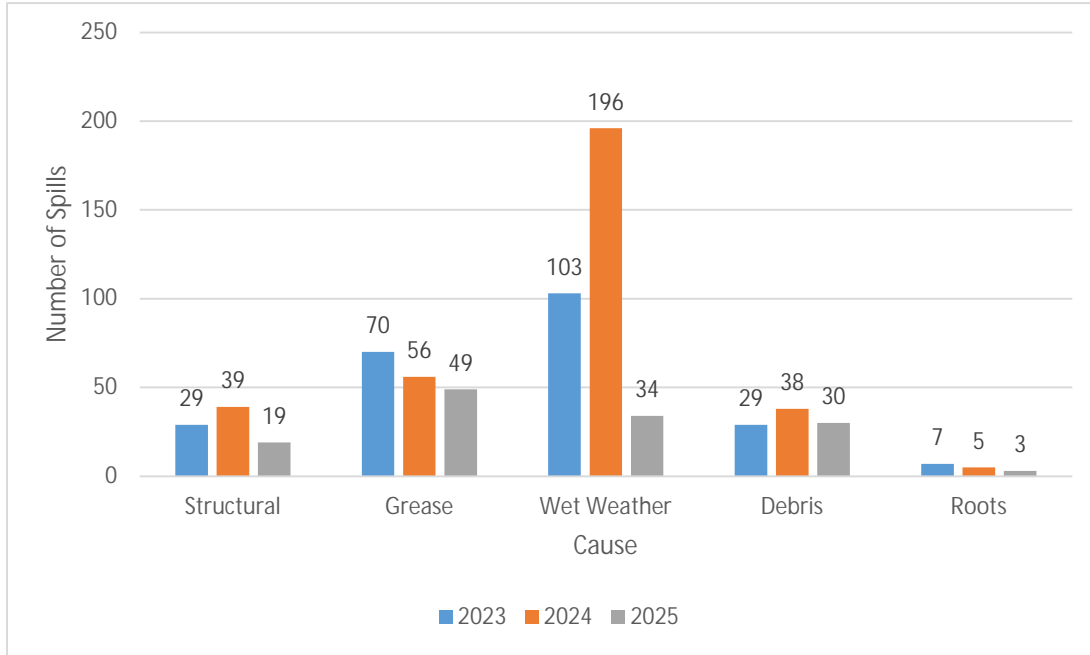

Note: Cause Categories may include more than one cause. Some SSOs appear in more than one Cause Category. Other causes for spills not shown in this figure include pump failure, vandalism, contractor-related, etc.


Figure 4-4 presents the number of spills by year. The number of total spills per year decreased from 2023 to 2025. This is heavily influenced by the number and type of rain events over the course of the year causing wet weather spills. Sewer rehabilitation and capacity relief projects have continued under a number of projects to reduce wet weather SSOs. In 2025, pipe upsizing projects completed at a number of repeat SSO sites including 1440 Sowell Estate, 2060 Keheley Drive, 2562 Tilly Mill Rd, 307 2nd Avenue/607 3rd Avenue, Brookfield Lane/Cobb Branch Drive, and 3911/3924 Roman Court have reduced the number and volume of wet weather SSOs.

Figure 4-4 Spills by Year (2023–2025)

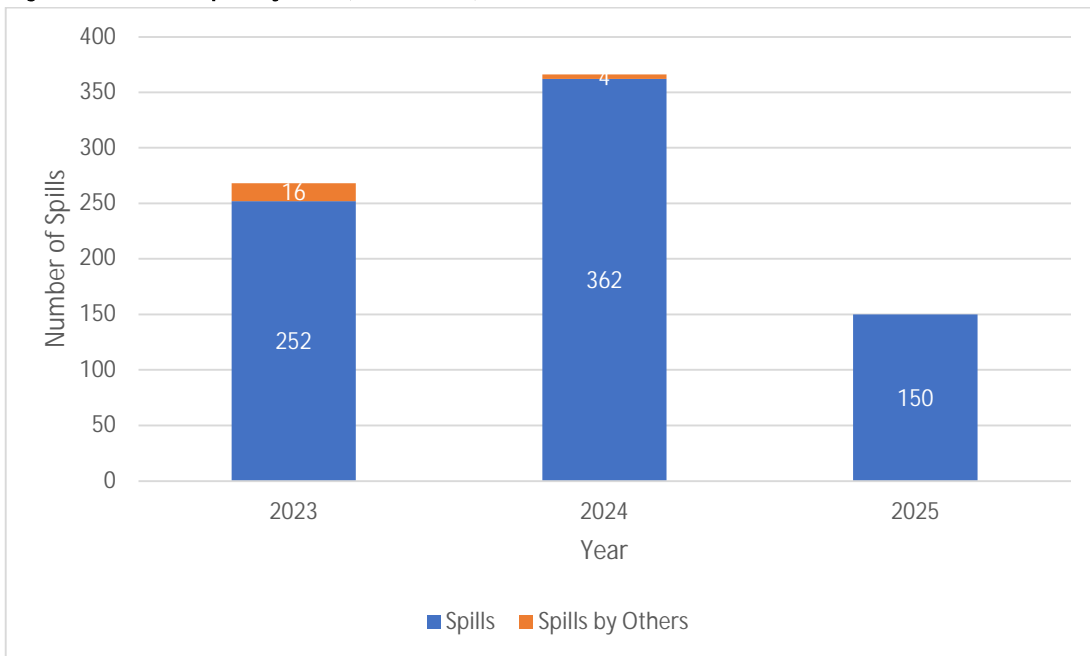

Overall, spills decreased between 2024 and 2025. Figure 4-5 shows a month-to-month comparison of spills from 2024 and 2025. In 2025, February saw the most spills due to the February 12-13, 2025 2 year storm event.

Figure 4-5 Spills by Month (2024–2025)

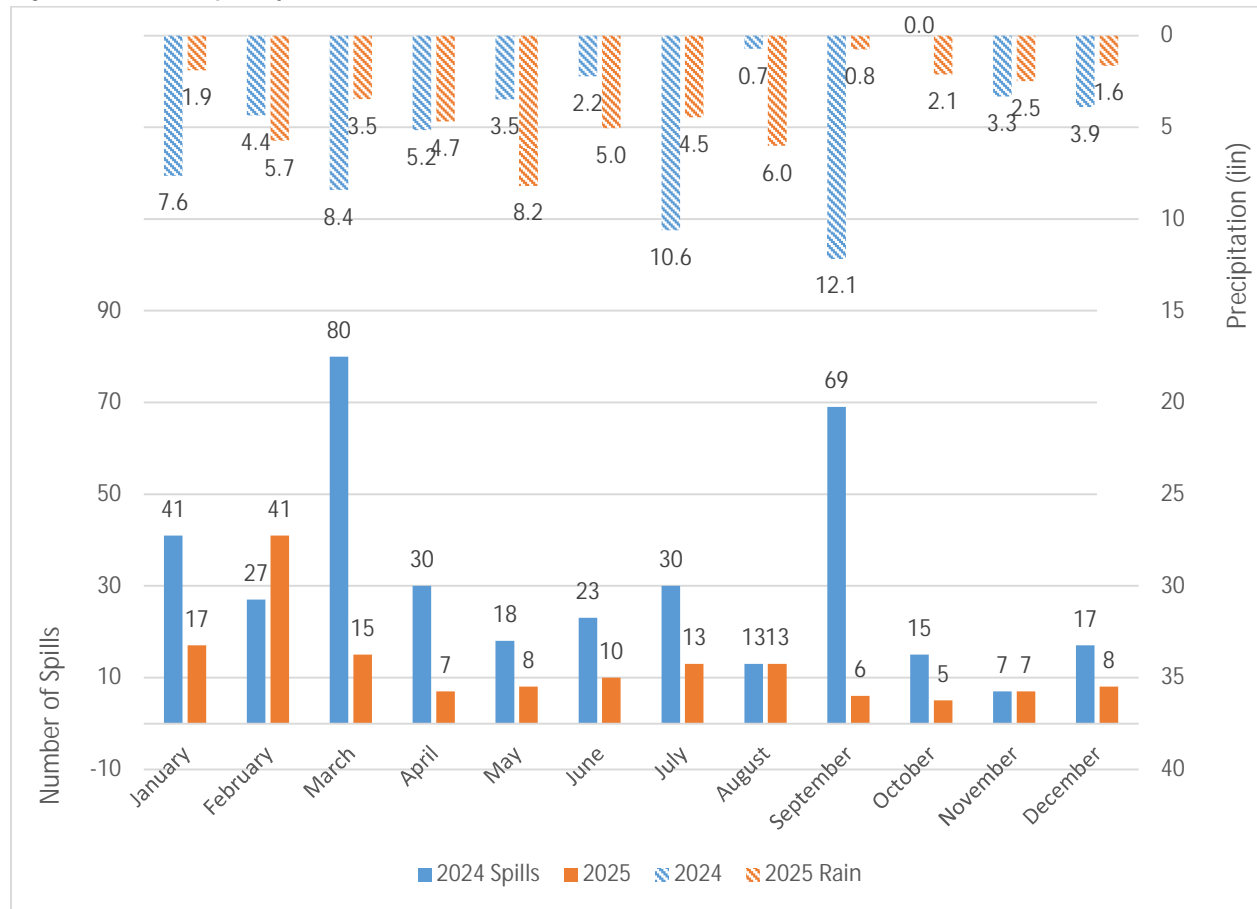

5. Other Trends

DWM evaluated other potential trends including those based on pipe size and rainfall.

Pipe Size

The most common pipe diameter in the collection system is 8 inches, as shown on Figure 5-1. Pipes with a diameter of 8 inches account for 85 percent of the total number of pipes and 83 percent of the total length of pipe. Likewise, most spills are associated with pipes of 8 inches in diameter (Figure 5-2).

Figure 5-1 Sewer Gravity Main Pipe Count and Length by Diameter


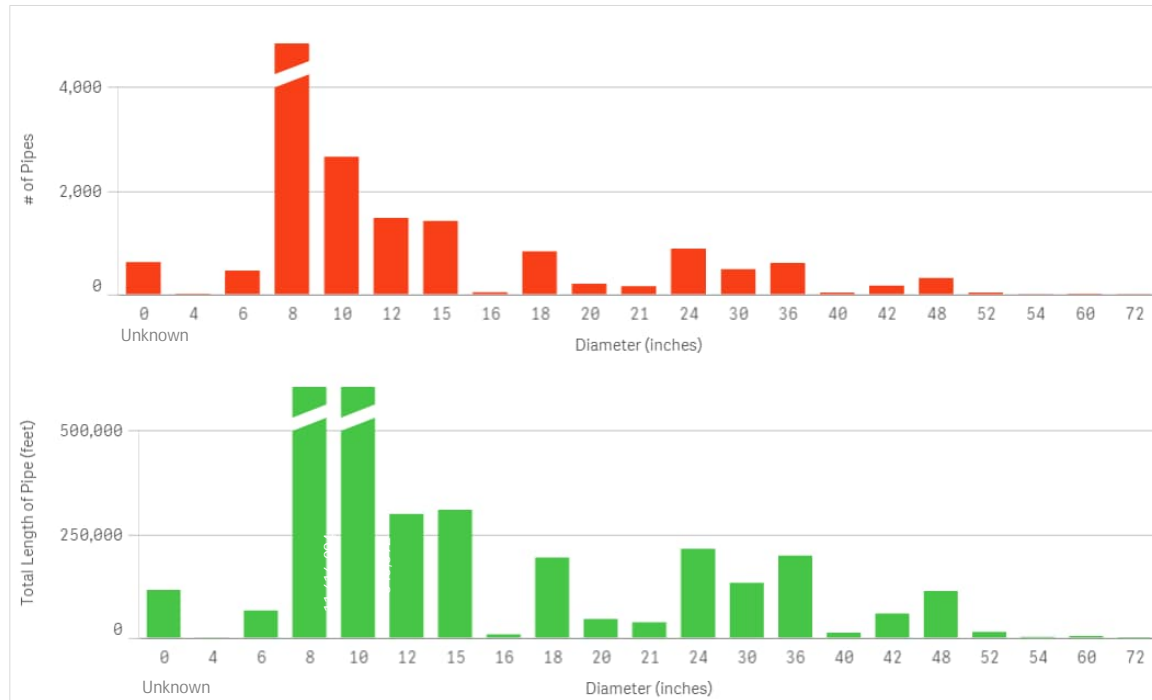



Figure 5-2 Spills by Year by Pipe Size (Inches) (2023–2025)

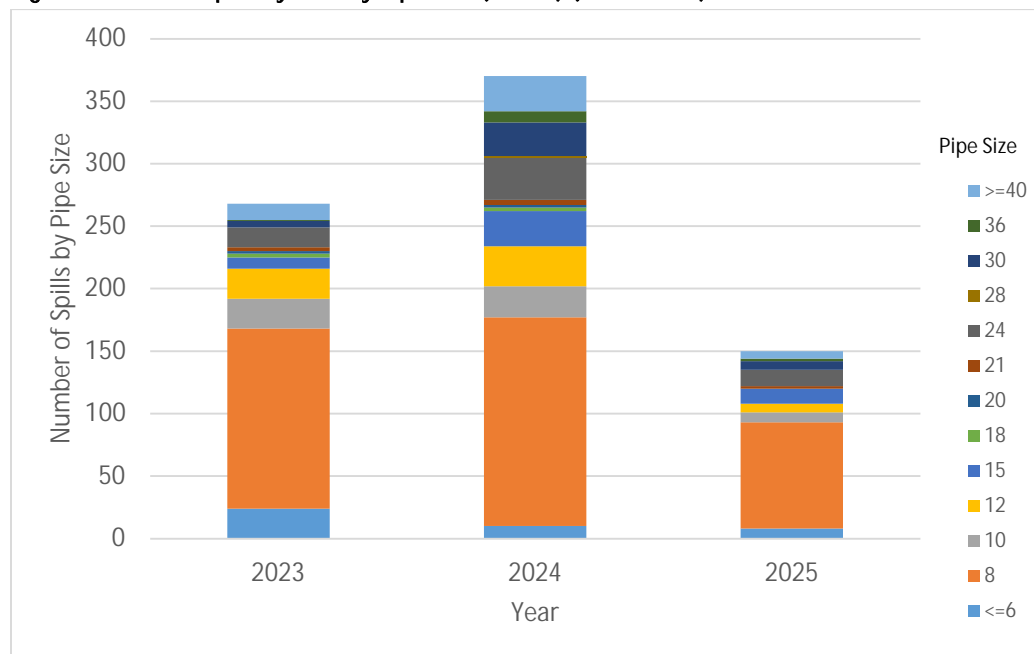

Notes: Only spills have an associated pipe size linked to an SSO, so only spills are included in this figure.

Figure 5-3 shows the volume of spills by pipe size. There is correlation between pipe size and volume of SSO, as larger pipes have greater capacity, generally convey more flow, and in cases of structural repairs, can take longer to restore.

Figure 5-3 Spill Volume by Year by Pipe Size (2023–2025)

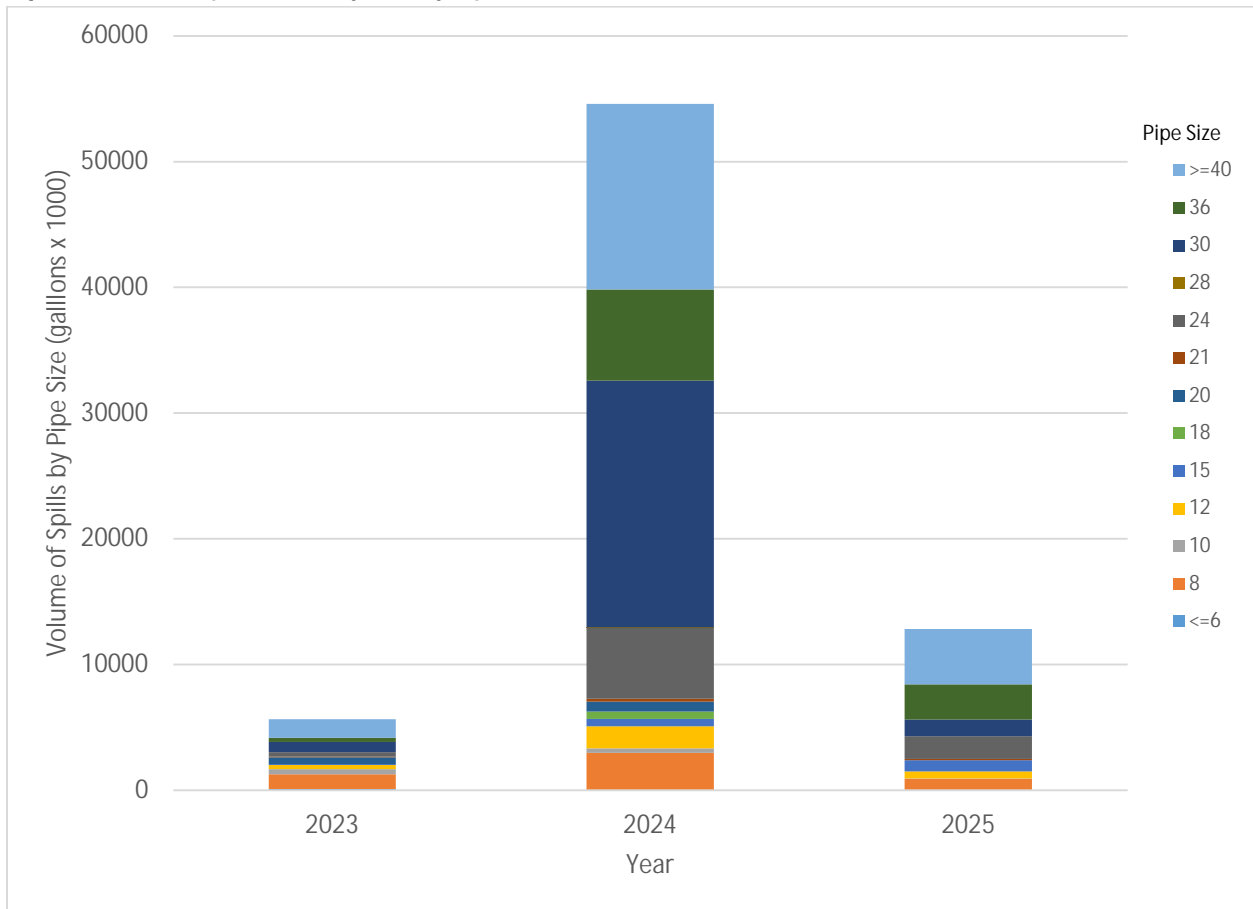


Notes:

Only spills have an associated pipe size linked to an SSO, so only spills are included in this figure. Pipe diameter was not always recorded; thus, some are blank or N/A.

Rainfall

The difference in rainfall intensity is reflected in the data for SSOs and spills caused by wet weather. In 2023, 103 spills were attributed to wet weather (39 occurred on 2 wet weather events that exceeded 2-year recurrence levels) and in 2024, 196 spills were attributed to wet weather (54 occurred during Hurricane Helene and an additional 77 during the two other Severe Natural Condition events). In 2025 34 spills were attributed to wet weather (25 occurred on 1 wet weather event equal to a 2-year recurrence level). The volume for spills caused by wet weather was approximately 3.7 million gallons in 2023, 50.3 million gallons in 2024 (28.2 MG during Hurricane Helene and another 14.6 MG from the other two Severe Natural Condition events) and 8.3 million gallons in 2025. Figure 5-4 shows rainfall and SSO volume by month from 2023 through 2025.

Figure 5-4 Monthly Precipitation and Wet-Weather-Induced SSO Volume (2023–2025)

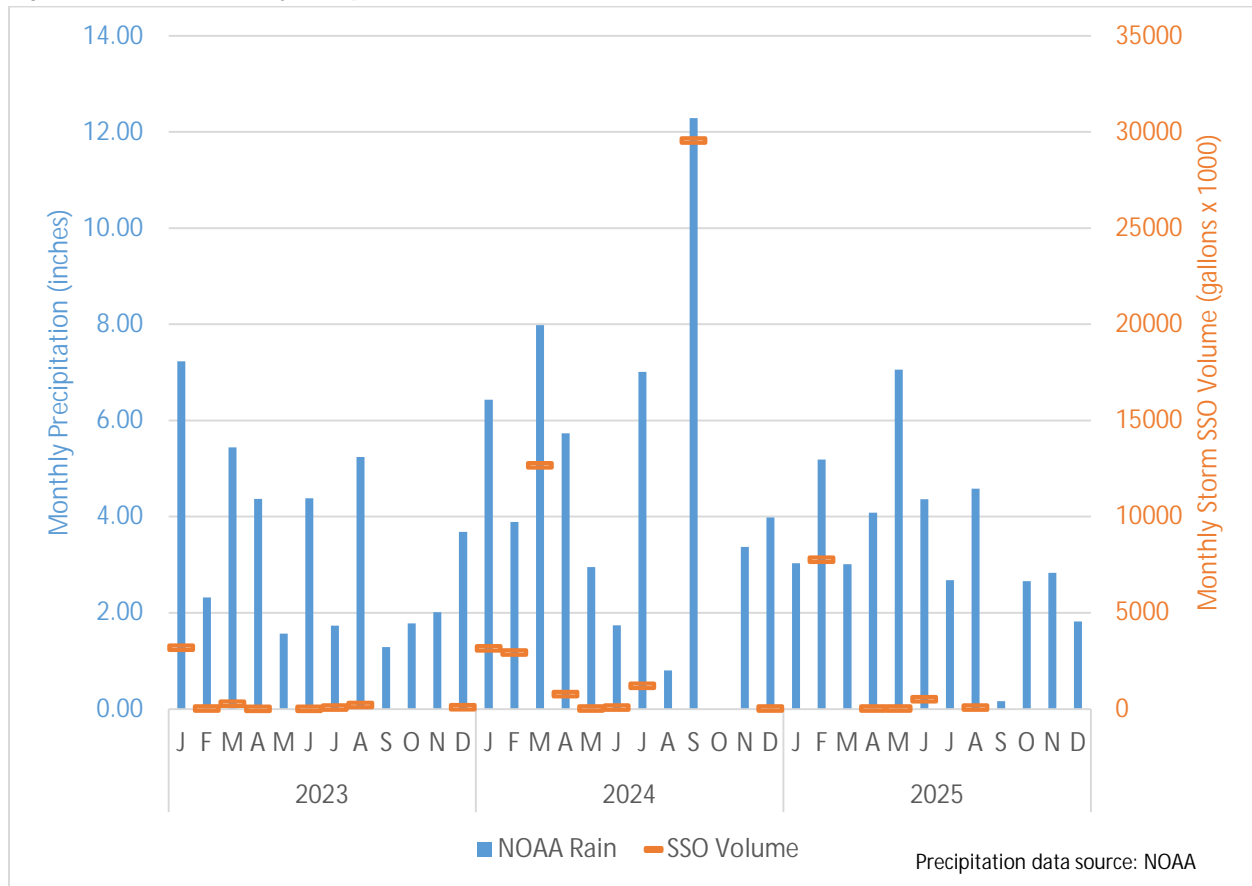


Note: Only spills with a cause of STORM or I/I are represented on this figure.

Repeat SSOs

DWM reviewed SSOs in their spatial context to identify repeat SSO locations. These locations were recorded and prioritized for further investigation to define solutions to minimize future recurrence of SSOs.


DWM defined 500-foot-radius areas with repeat SSOs and tallied the repeat SSO locations by sewershed (refer to Figure 5-5). For 2025, the total number of repeat SSOs was 92. North Fork Peachtree Creek and South Fork Peachtree Creek had the greatest number of repeat SSO locations. The majority of these SSOs are maintenance related in North Fork Peachtree Creek and maintenance and structural related in South Fork Peachtree Creek. Focused cleaning and implementation of the Find and Fix Program is aimed at reducing these repeat SSOs.

Figure 5-5 Number of Locations with Repeat SSOs by Sewershed (2025)

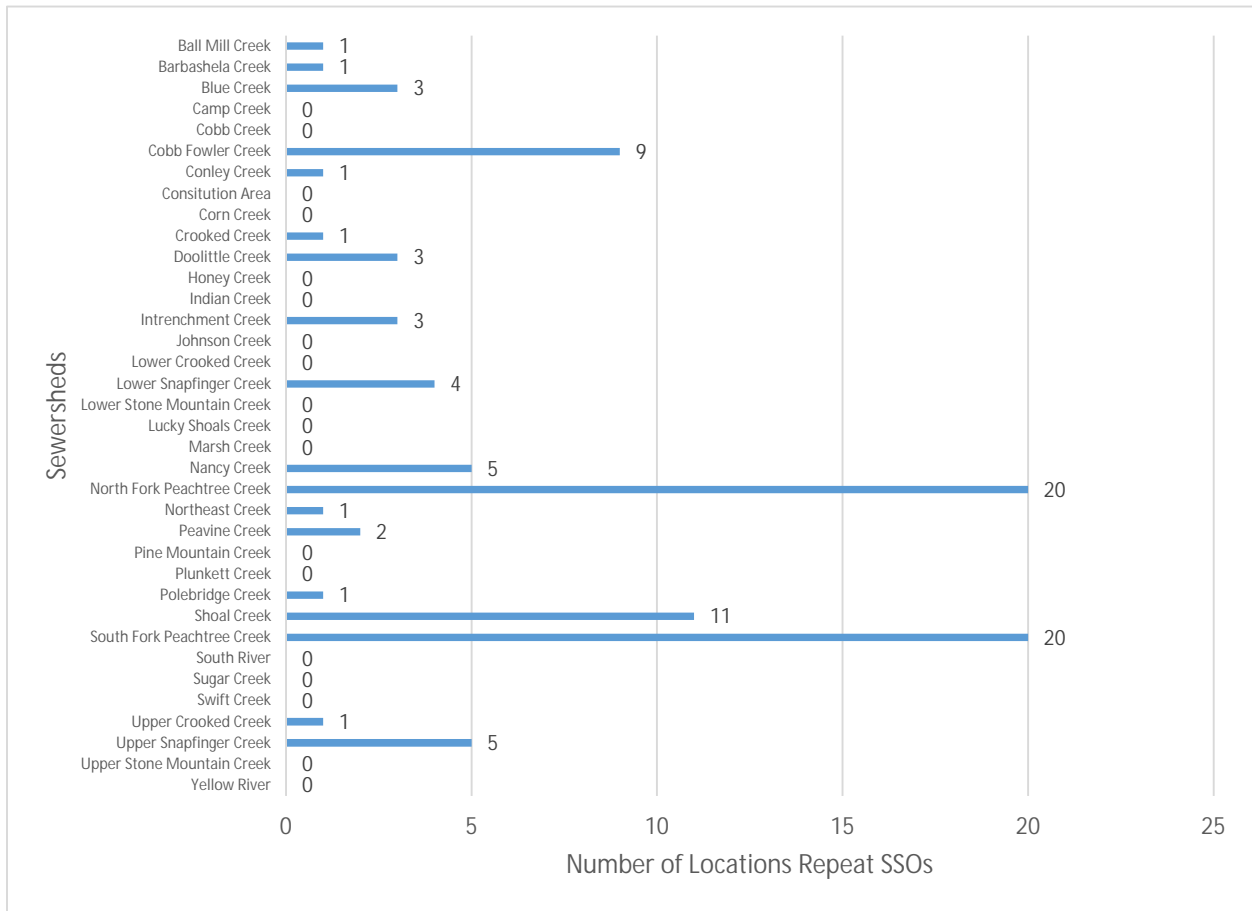

The most common cause of repeat SSOs in 2025 was wet weather (refer to Figure 5-6). Wet-weather-related, repeat SSOs have decreased 2023 to 2025 due to decrease in severe weather events and completion of a number of capacity relief projects. As planned rehabilitation measures are constructed to reduce I/I sources and provide capacity in the system, wet-weather SSOs are expected to continue to decrease. DWM has identified historical repeat SSOs and has developed remediation plans to address these issues.


Figure 5-6 Number of Repeat SSOs by Cause (2023–2025)

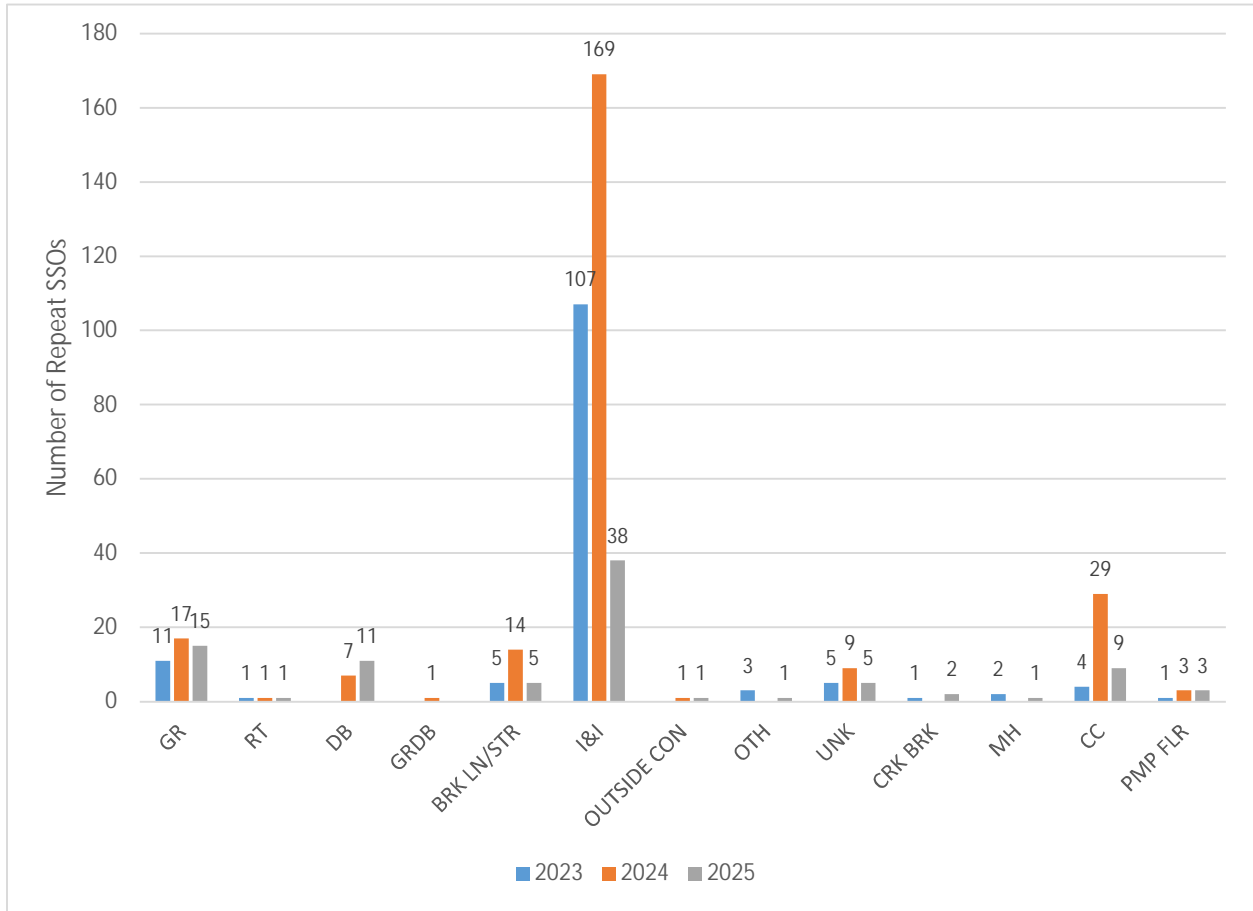

Note: All I/I SSOs recorded to date were wet-weather-related.


Similarly, DWM analyzed only those SSOs that are categorized as spills. From 2024 to 2025, repeat spills decreased. North Fork Peachtree Creek, South Fork Peachtree Creek, and Shoal Creek had the greatest number of repeat spill locations in 2025 (refer to Figure 5-7).

Figure 5-7 Number of Locations with Repeat Spills by Sewershed (2025)

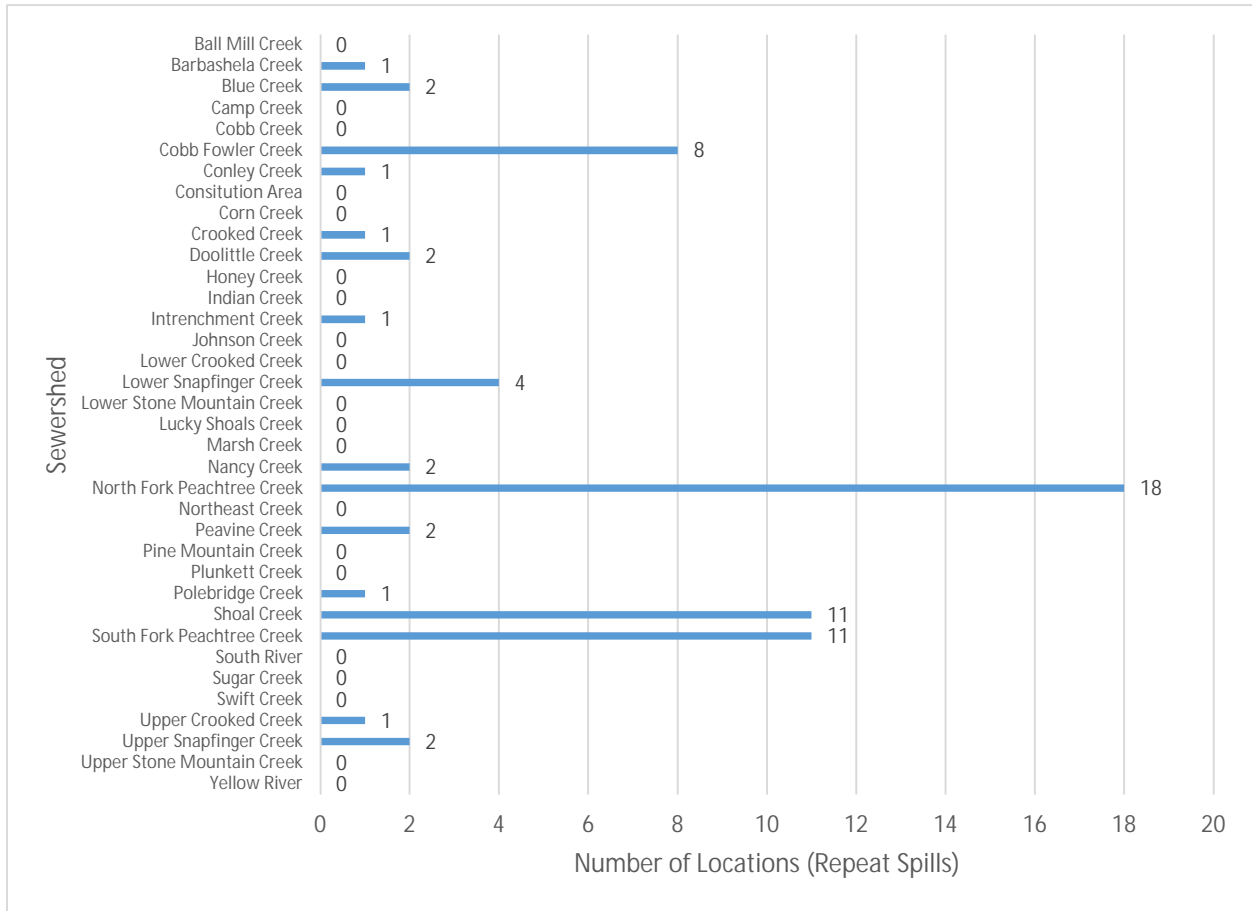

The most common cause of repeat spills is wet weather (refer to Figure 5-8). Wet-weather-related repeat spills increased from 2022 to 2024. As rehabilitation measures are constructed to reduce I/I sources and provide capacity in the system, wet weather SSOs are expected to decrease.

Figure 5-8 Number of Repeat Spills by Cause (2023 – 2025)

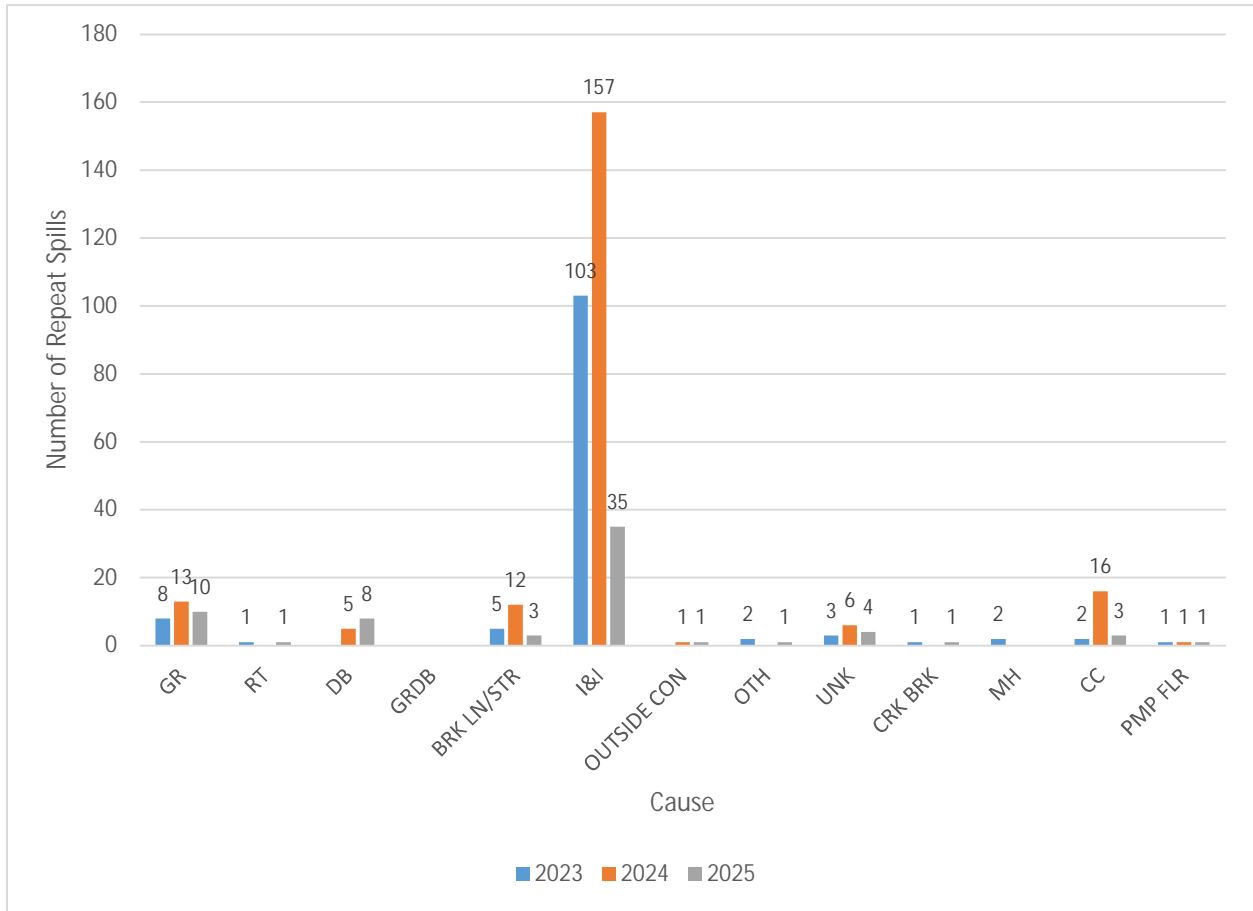

Note: All I/I SSOs recorded to date were wet-weather-related.

The spatial distribution of repeat SSOs and repeat spills are shown on Figures 5-9 and 5-10, respectively.

Figure 5-9 Repeat SSOs


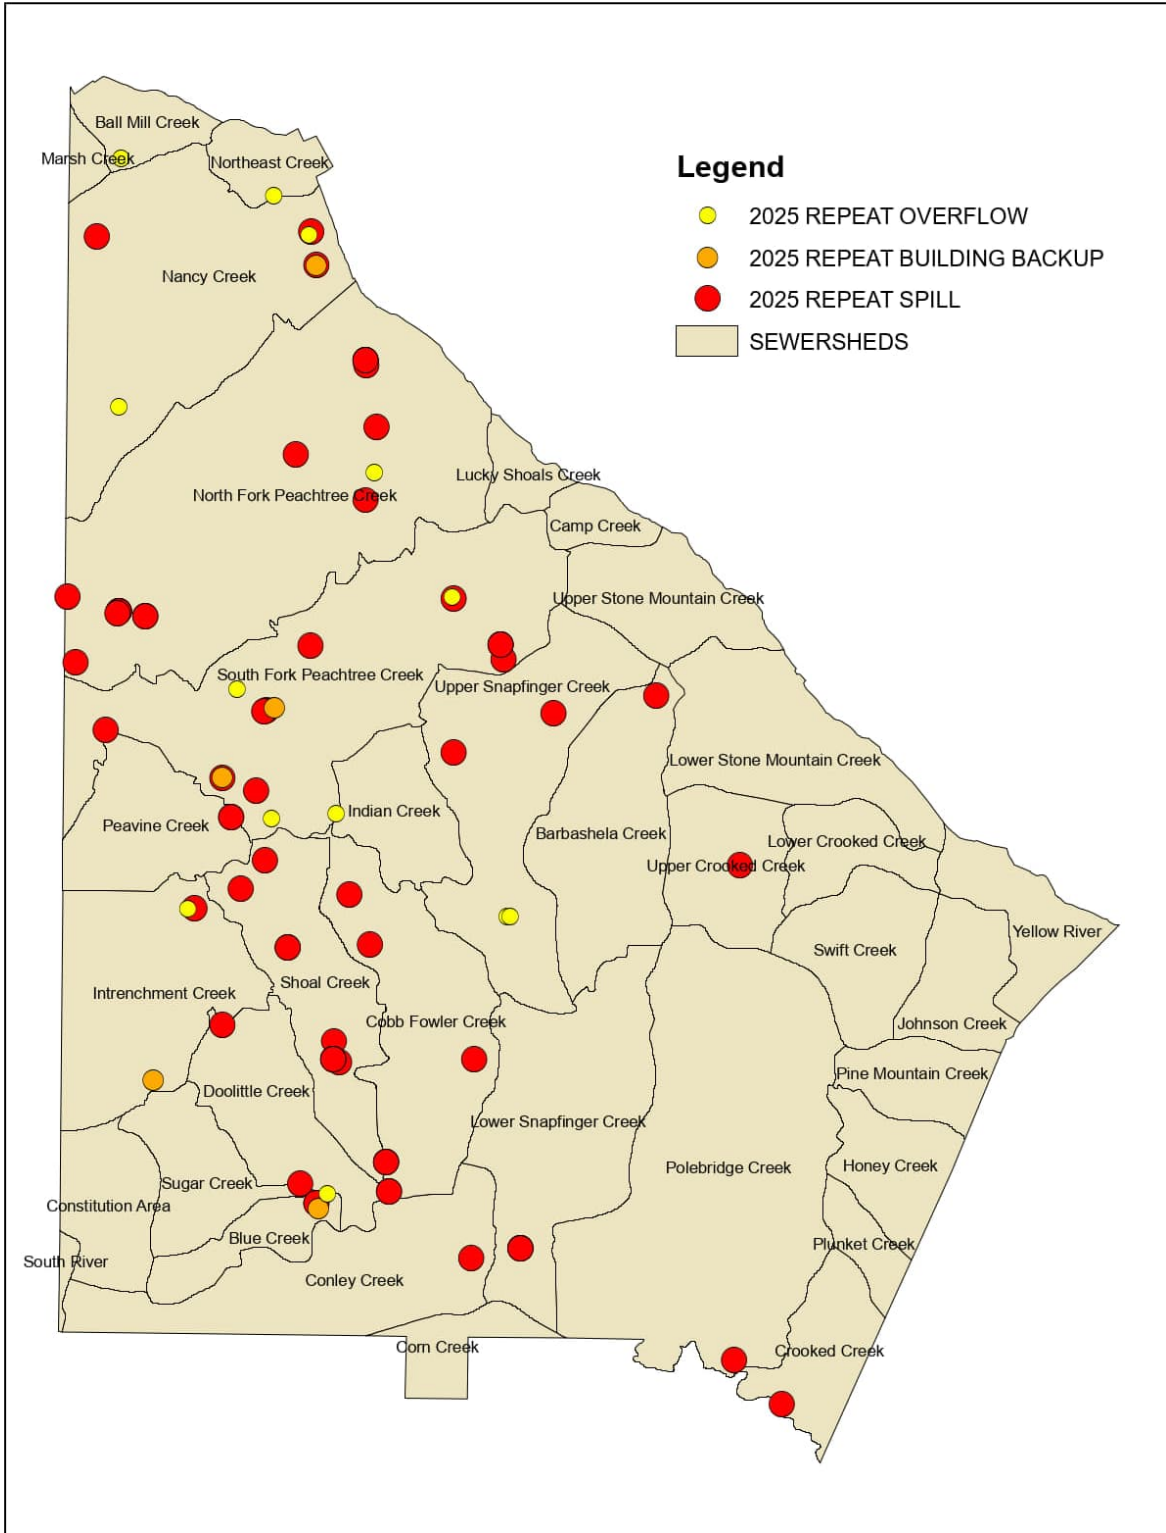


Figure 5-10 Repeat Spills

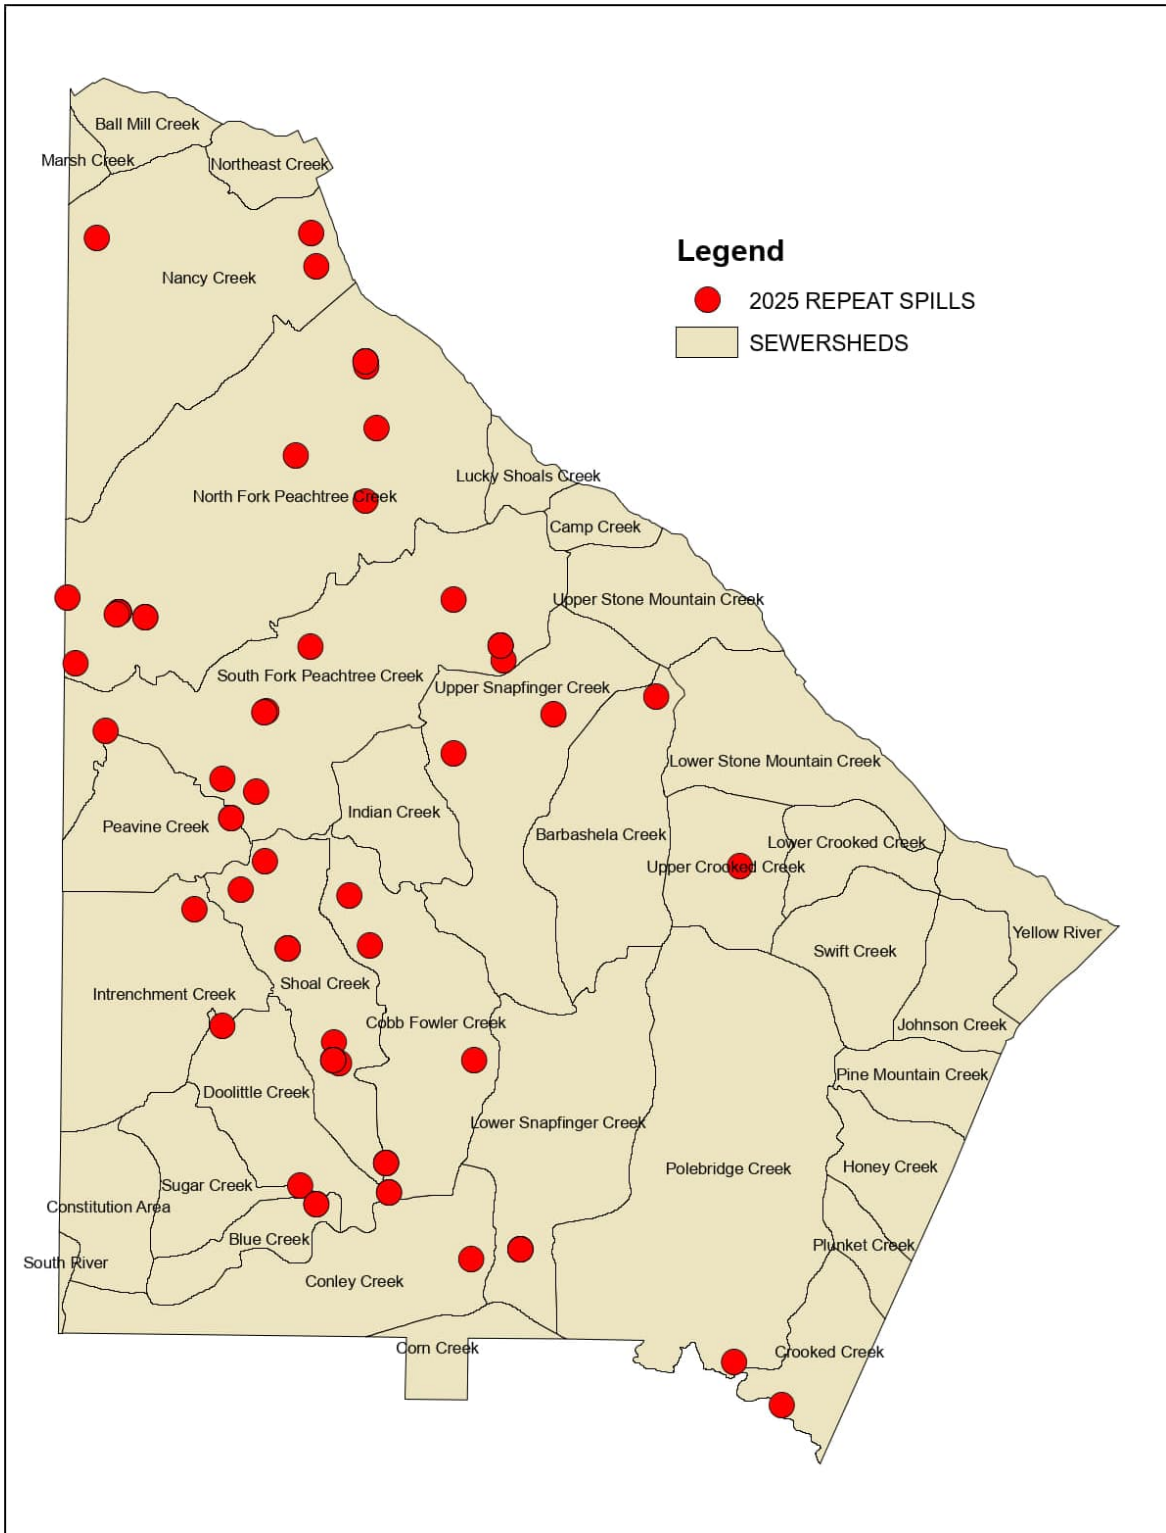

6. Summary

A summary of the trend analysis presented in this report is provided below:

- The number of SSOs per year decreased this year. Of the overall SSO trends for 2025:
 - Debris SSOs remained steady. The County transitioned to new small diameter sewer cleaning contractors at the end of 2025. While these contractors will continue to focus on the CARLS list and proactive cleaning, the assignments will be more focused based on data from the previous cleaning contract.
 - Wet weather SSOs decreased compared to 2024, due to decrease in severe wet weather events and completion of a number of capacity relief projects.
 - Grease SSOs increased slightly, which may be attributed to transition of small diameter sewer contracts.
 - Structural SSOs decreased compared to 2024 as the County continues to rehabilitate its system.
- Compared to 2024, spills decreased in 2025, from 362 spills to 150 spills. This decrease is attributed to a drier year in 2025, particularly compared to the impacts of Hurricane Helene and other severe natural conditions in 2024, as well as completion of capacity relief projects. 2025 had one event equivalent to a 2 year design storm on February 12-13, 2025 which resulted in 22 spills. The volume of spills, also decreased due to fewer wet weather events. Of the 12.8 MG of spills in 2025, more than 50%, 7.7MG occurred during the February 12-13 event.
- The average SSO duration for the last 3 years is approximately 6.8 hours (refer to Figure 3-1), up from 5.8 hours in 2024. Above-average durations are caused by the following:
 - I/I – SSOs can be contained but will not return to the system until capacity becomes available.
 - Structural – Longest duration because of the time needed to locate the spill, bypass the failure, and perform the repair.
 - Vandalism – Time needed to locate the issue; often includes atypical blockages in the system that cannot be removed during normal cleaning of the line.
 - Source Tracking – Spills can first be identified when lab tests of stream samples indicate high levels of fecal. The start of the spill is when the sample is taken. Next steps include lab testing, then walking the waterway upstream from the sampling site until the location of the spill is identified. Once dispatch is called and first responders address the spill, days can pass.
- SSOs resulting from maintenance issues (including grease, debris, and roots) accounted for 38 percent of the SSOs occurring from 2023 to 2025. During this same period, maintenance-related SSOs accounted for 5 percent of the estimated volume of SSOs (refer to Figure 4-1). Since the CD program was implemented in 2012, maintenance-related SSOs have decreased by 48 percent.
- Higher total annual or even monthly rainfall amounts does not always correlate to a higher number or larger volume of SSOs. SSO volume and frequency is not singularly because of the amount of rainfall for the month but also depends on antecedent conditions as well as how localized the rainfall event was. Reviewing additional USGS rain gauges located in the County compared to the NOAA rain gauge at Hartsfield Jackson International Airport, indicate that the County often experiences localized wet weather events.
- In 2025, there were 89 locations of repeat SSOs and 66 locations of repeat spills during the year (refer to Figure 5-5).
- The main cause of repeat SSOs in 2025 was wet weather (refer to Figure 5-6).
