



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Overall.dwg Plotted on: Mar 24, 2026 - 1:57pm

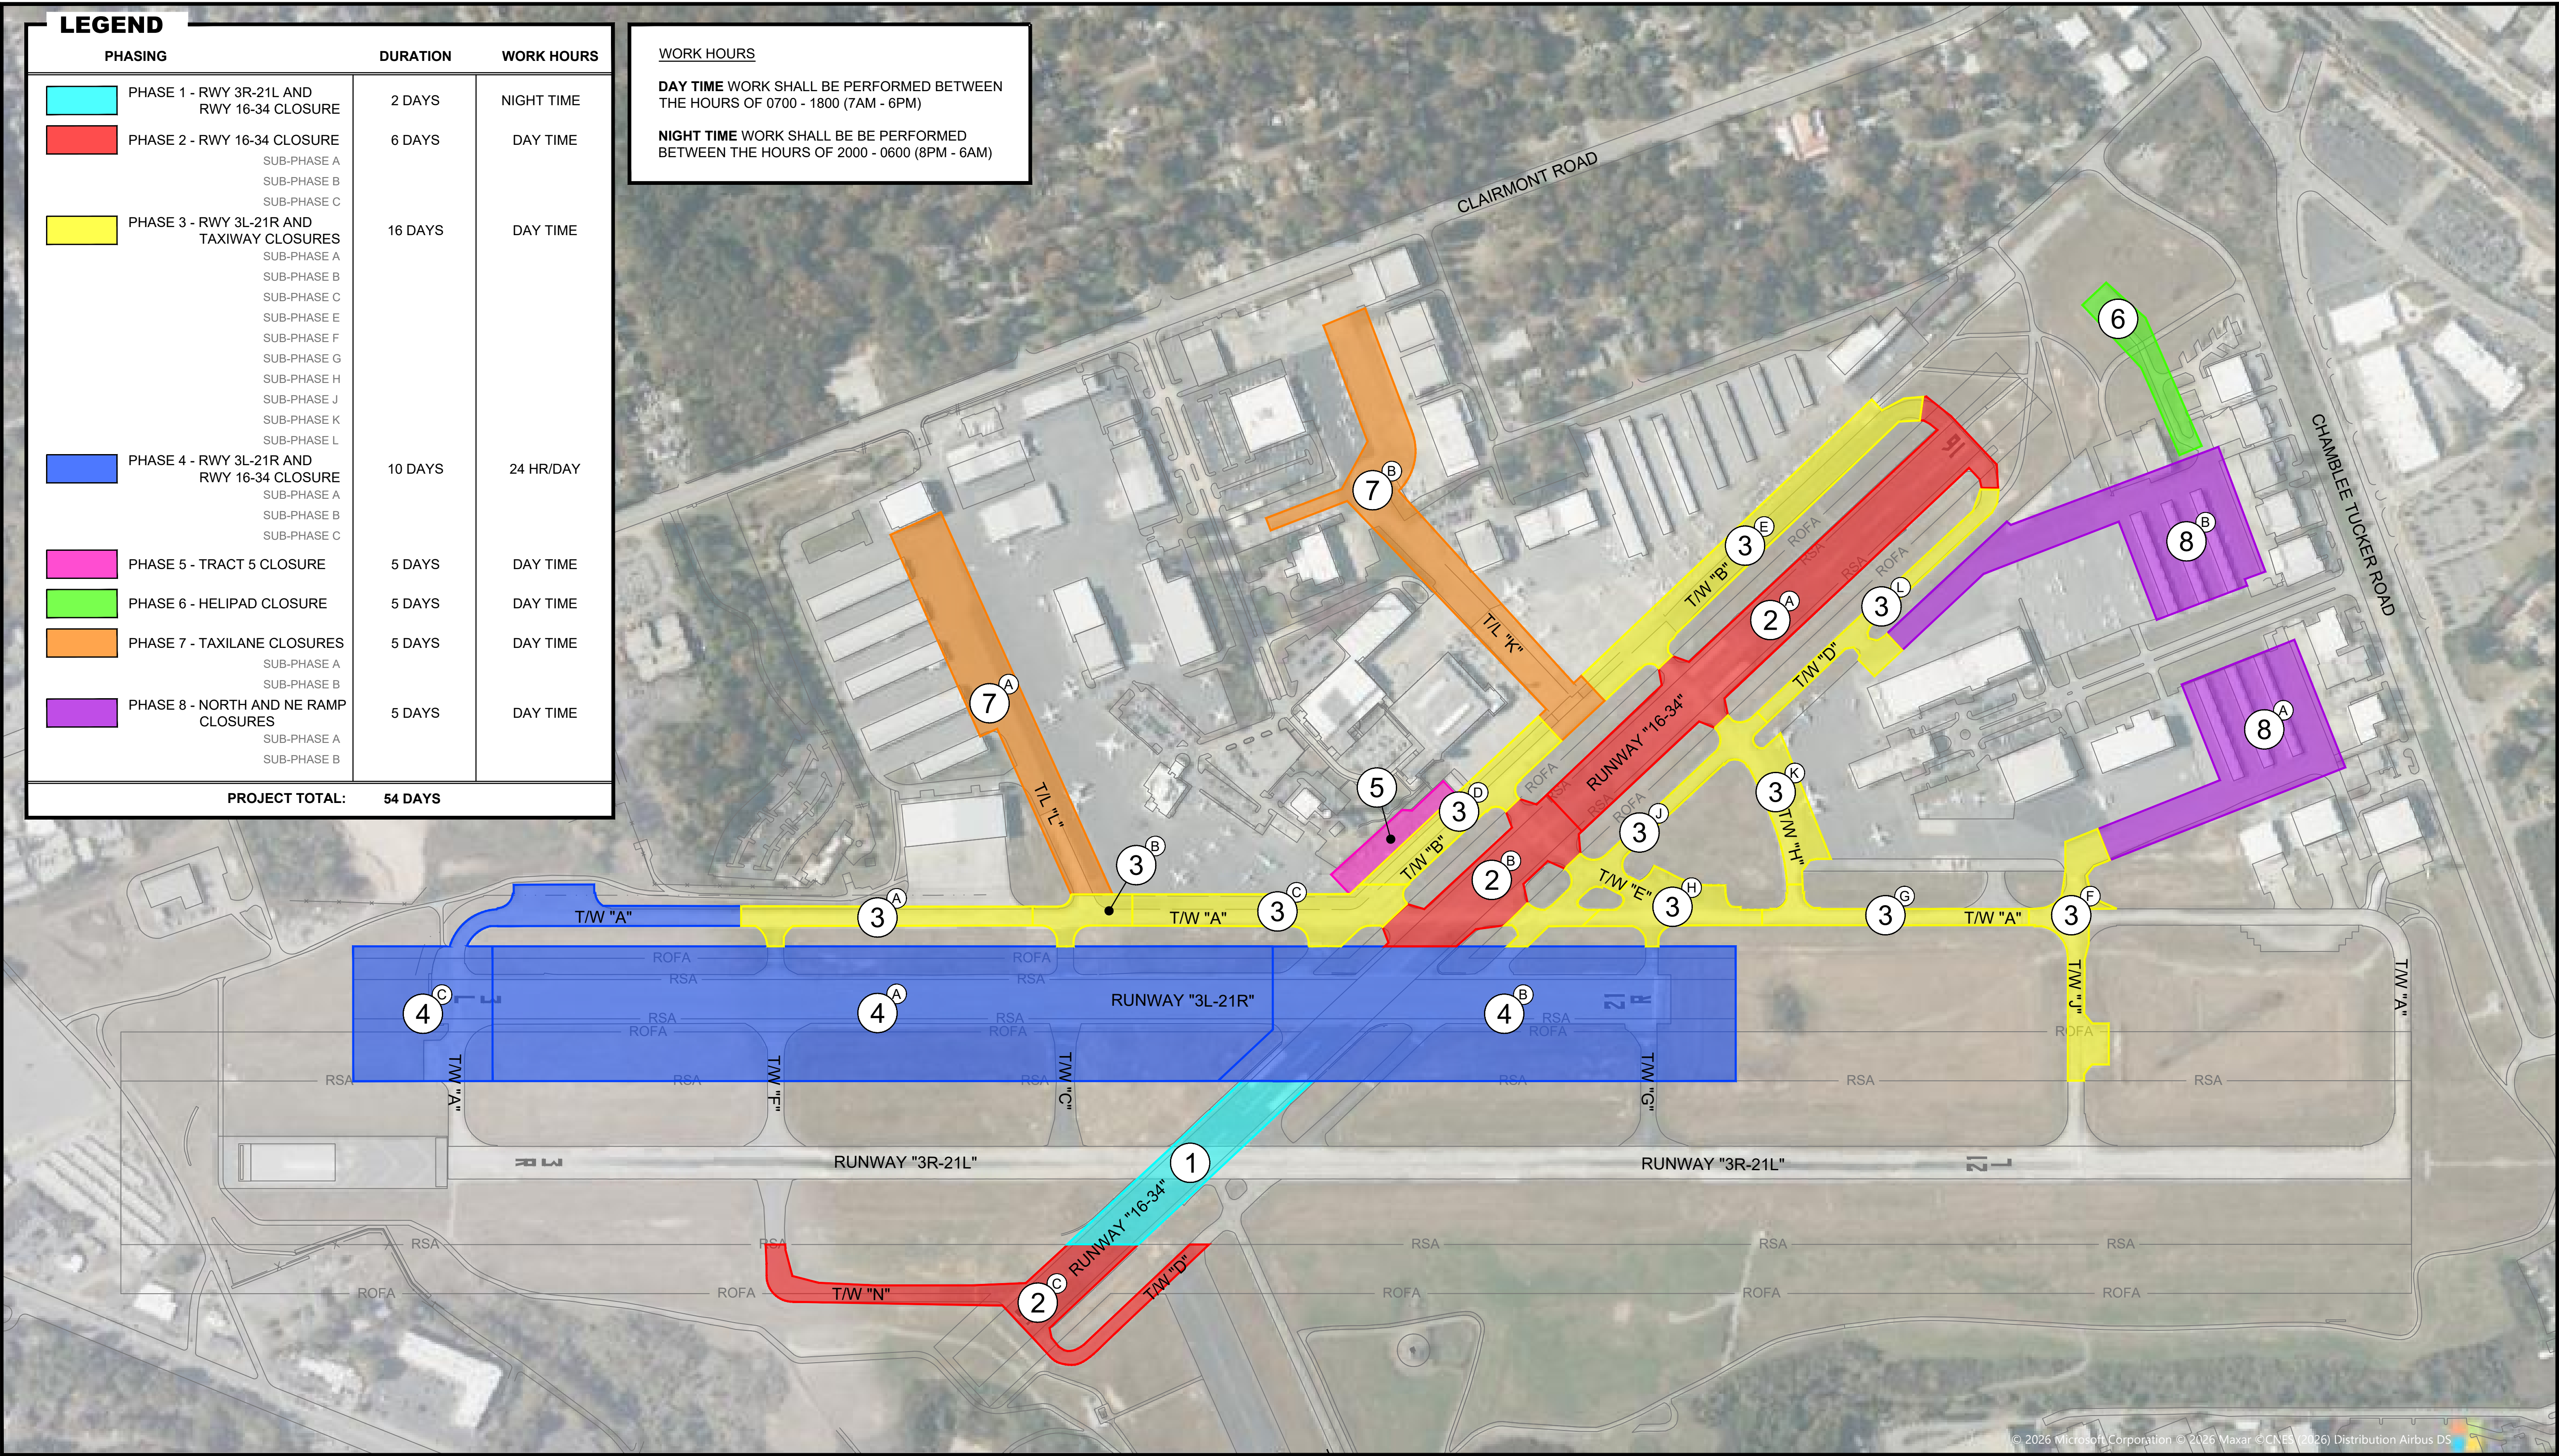

Y:\Airports\PDk\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:57pm

LEGEND


PHASE 1 - 2 DAYS (NIGHT TIME)

- BARRICADE
↔ AIR TRAFFIC
✕ RUNWAY CLOSURE


AIRFIELD CLOSURES:

- RUNWAY 3R-21L
- RUNWAY 16-34

WORK HOURS 2200 - 0600

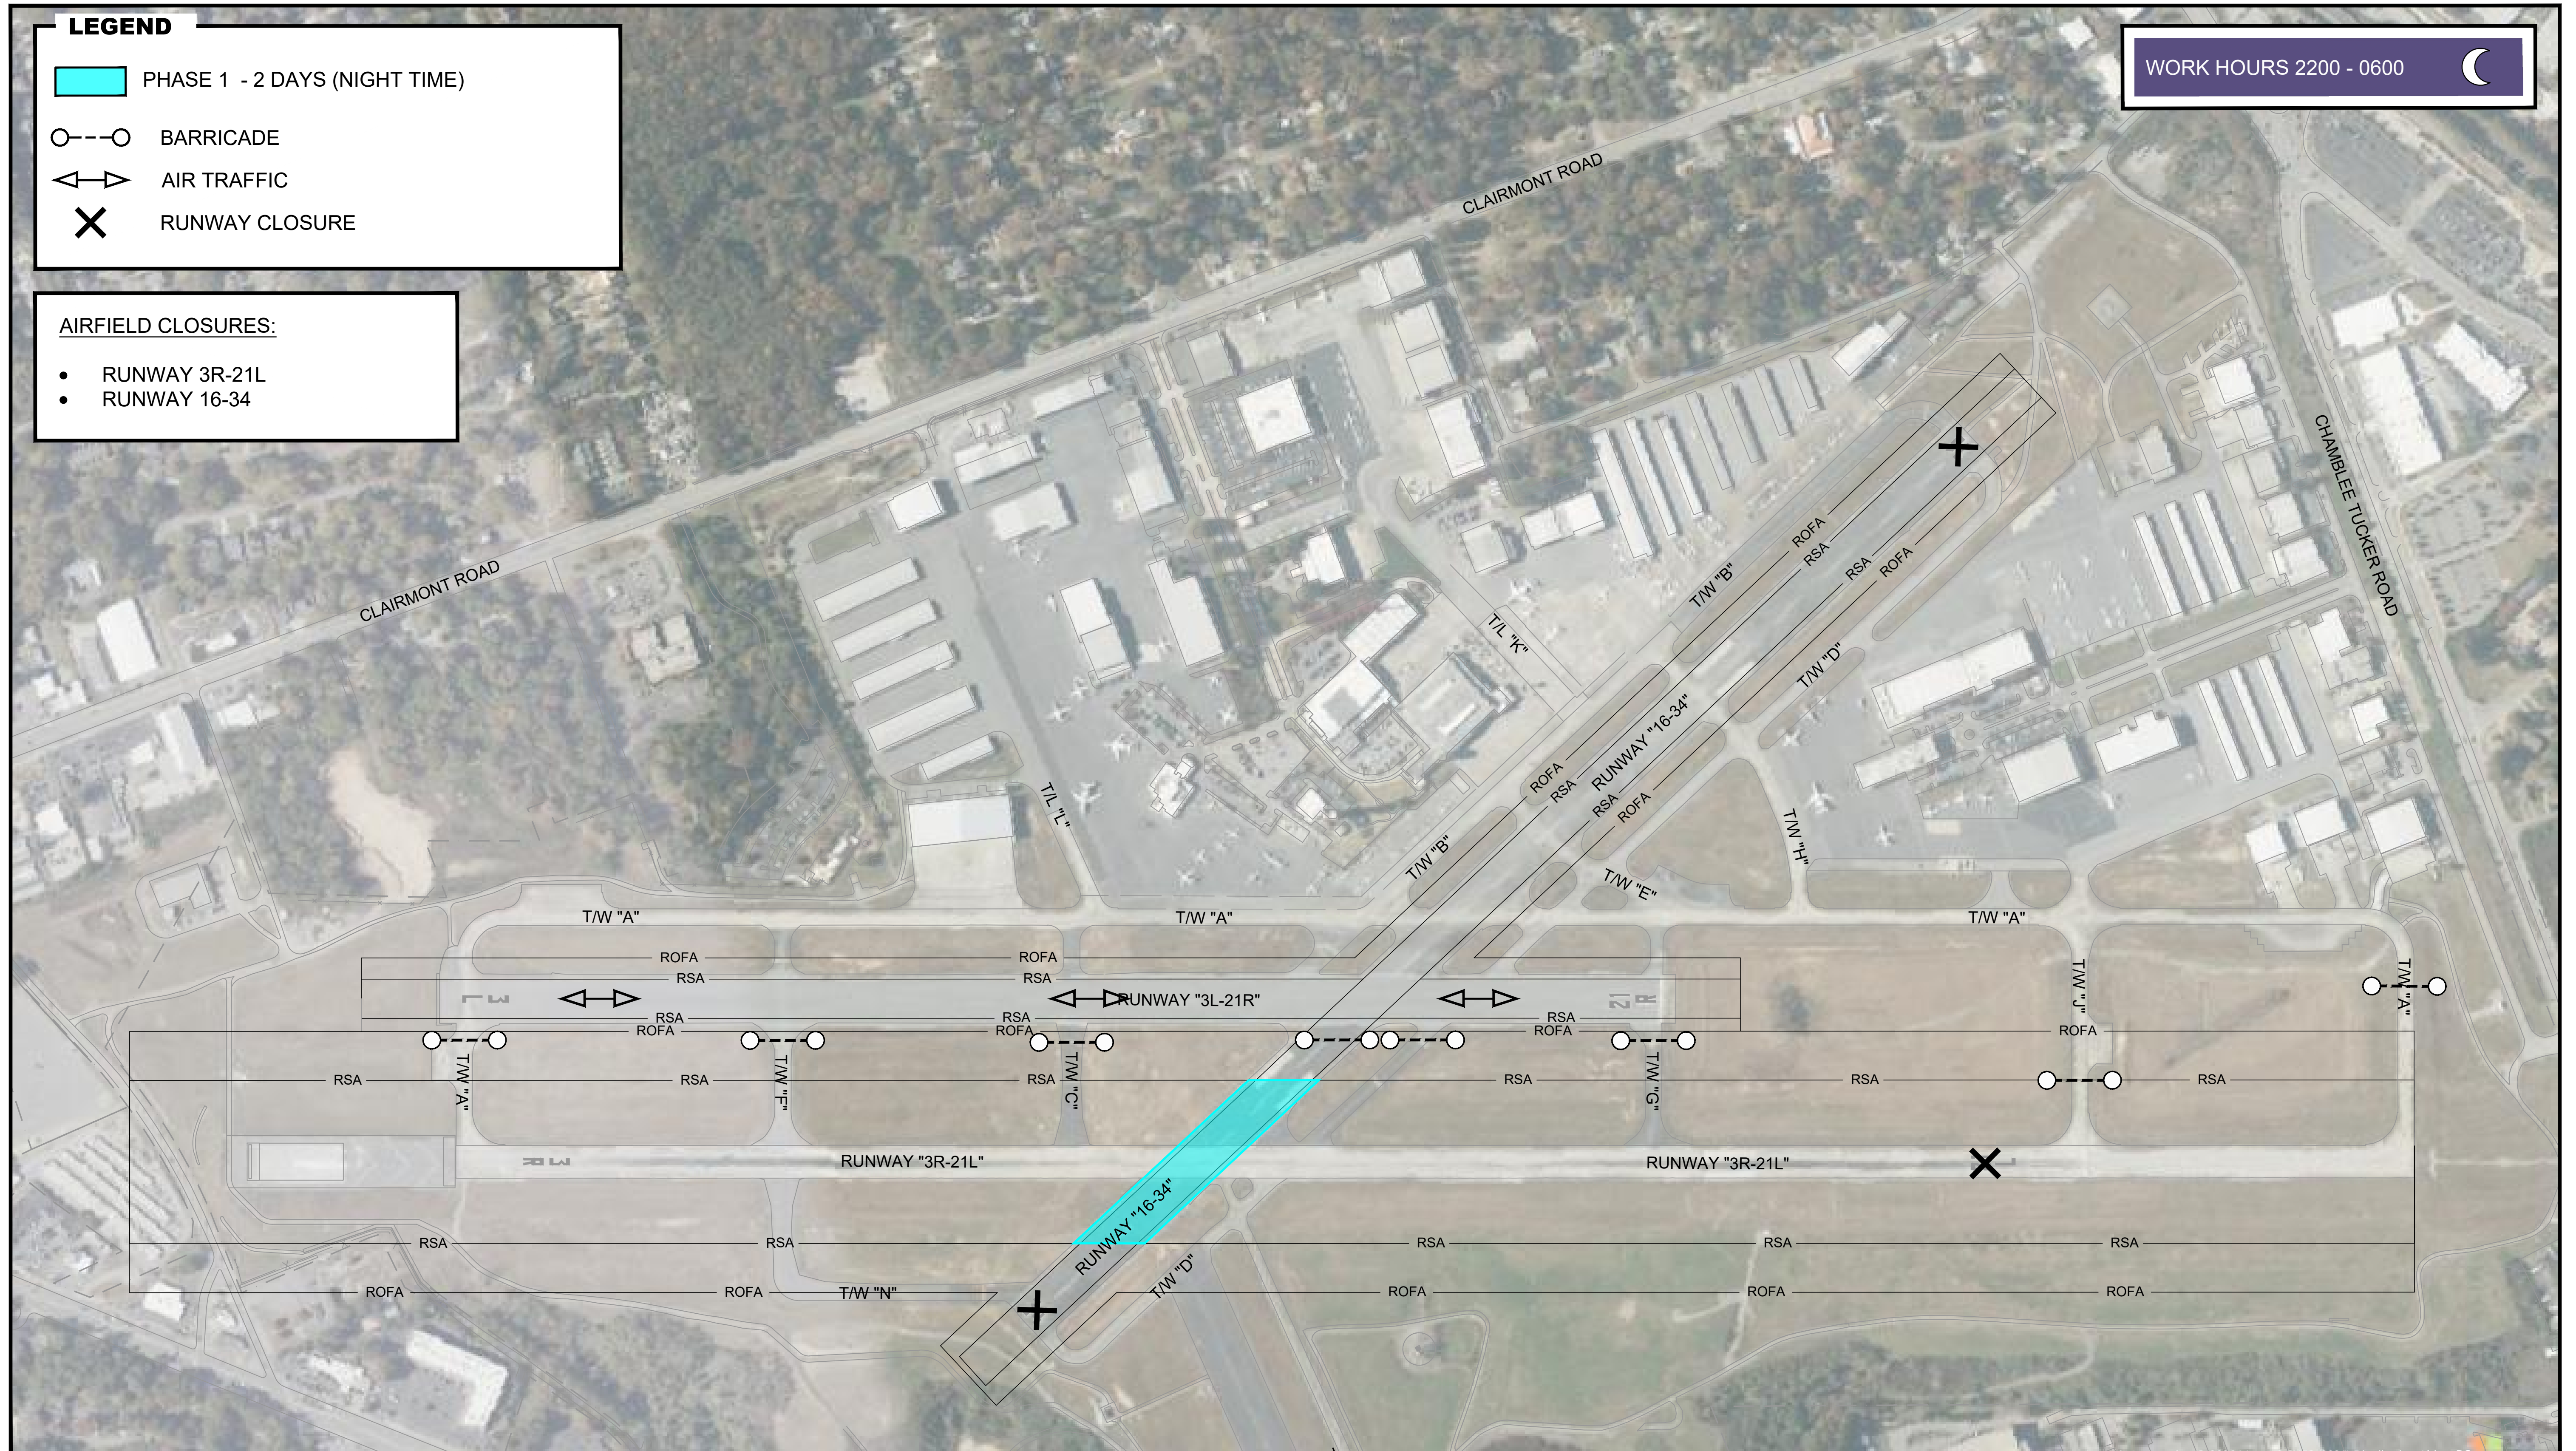

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 1

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:57pm

LEGEND

- PHASE 2A - 6 DAYS* (DAY TIME)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE



AIRFIELD CLOSURES:

- RUNWAY 16-34
- TAXIWAY H (PARTIAL)


*PHASE 2A IS A SUBPHASE OF PHASE 2. PHASE 2A DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

2A + 2B + 2C = 6 DAYS TOTAL

WORK HOURS 0700 - 1800

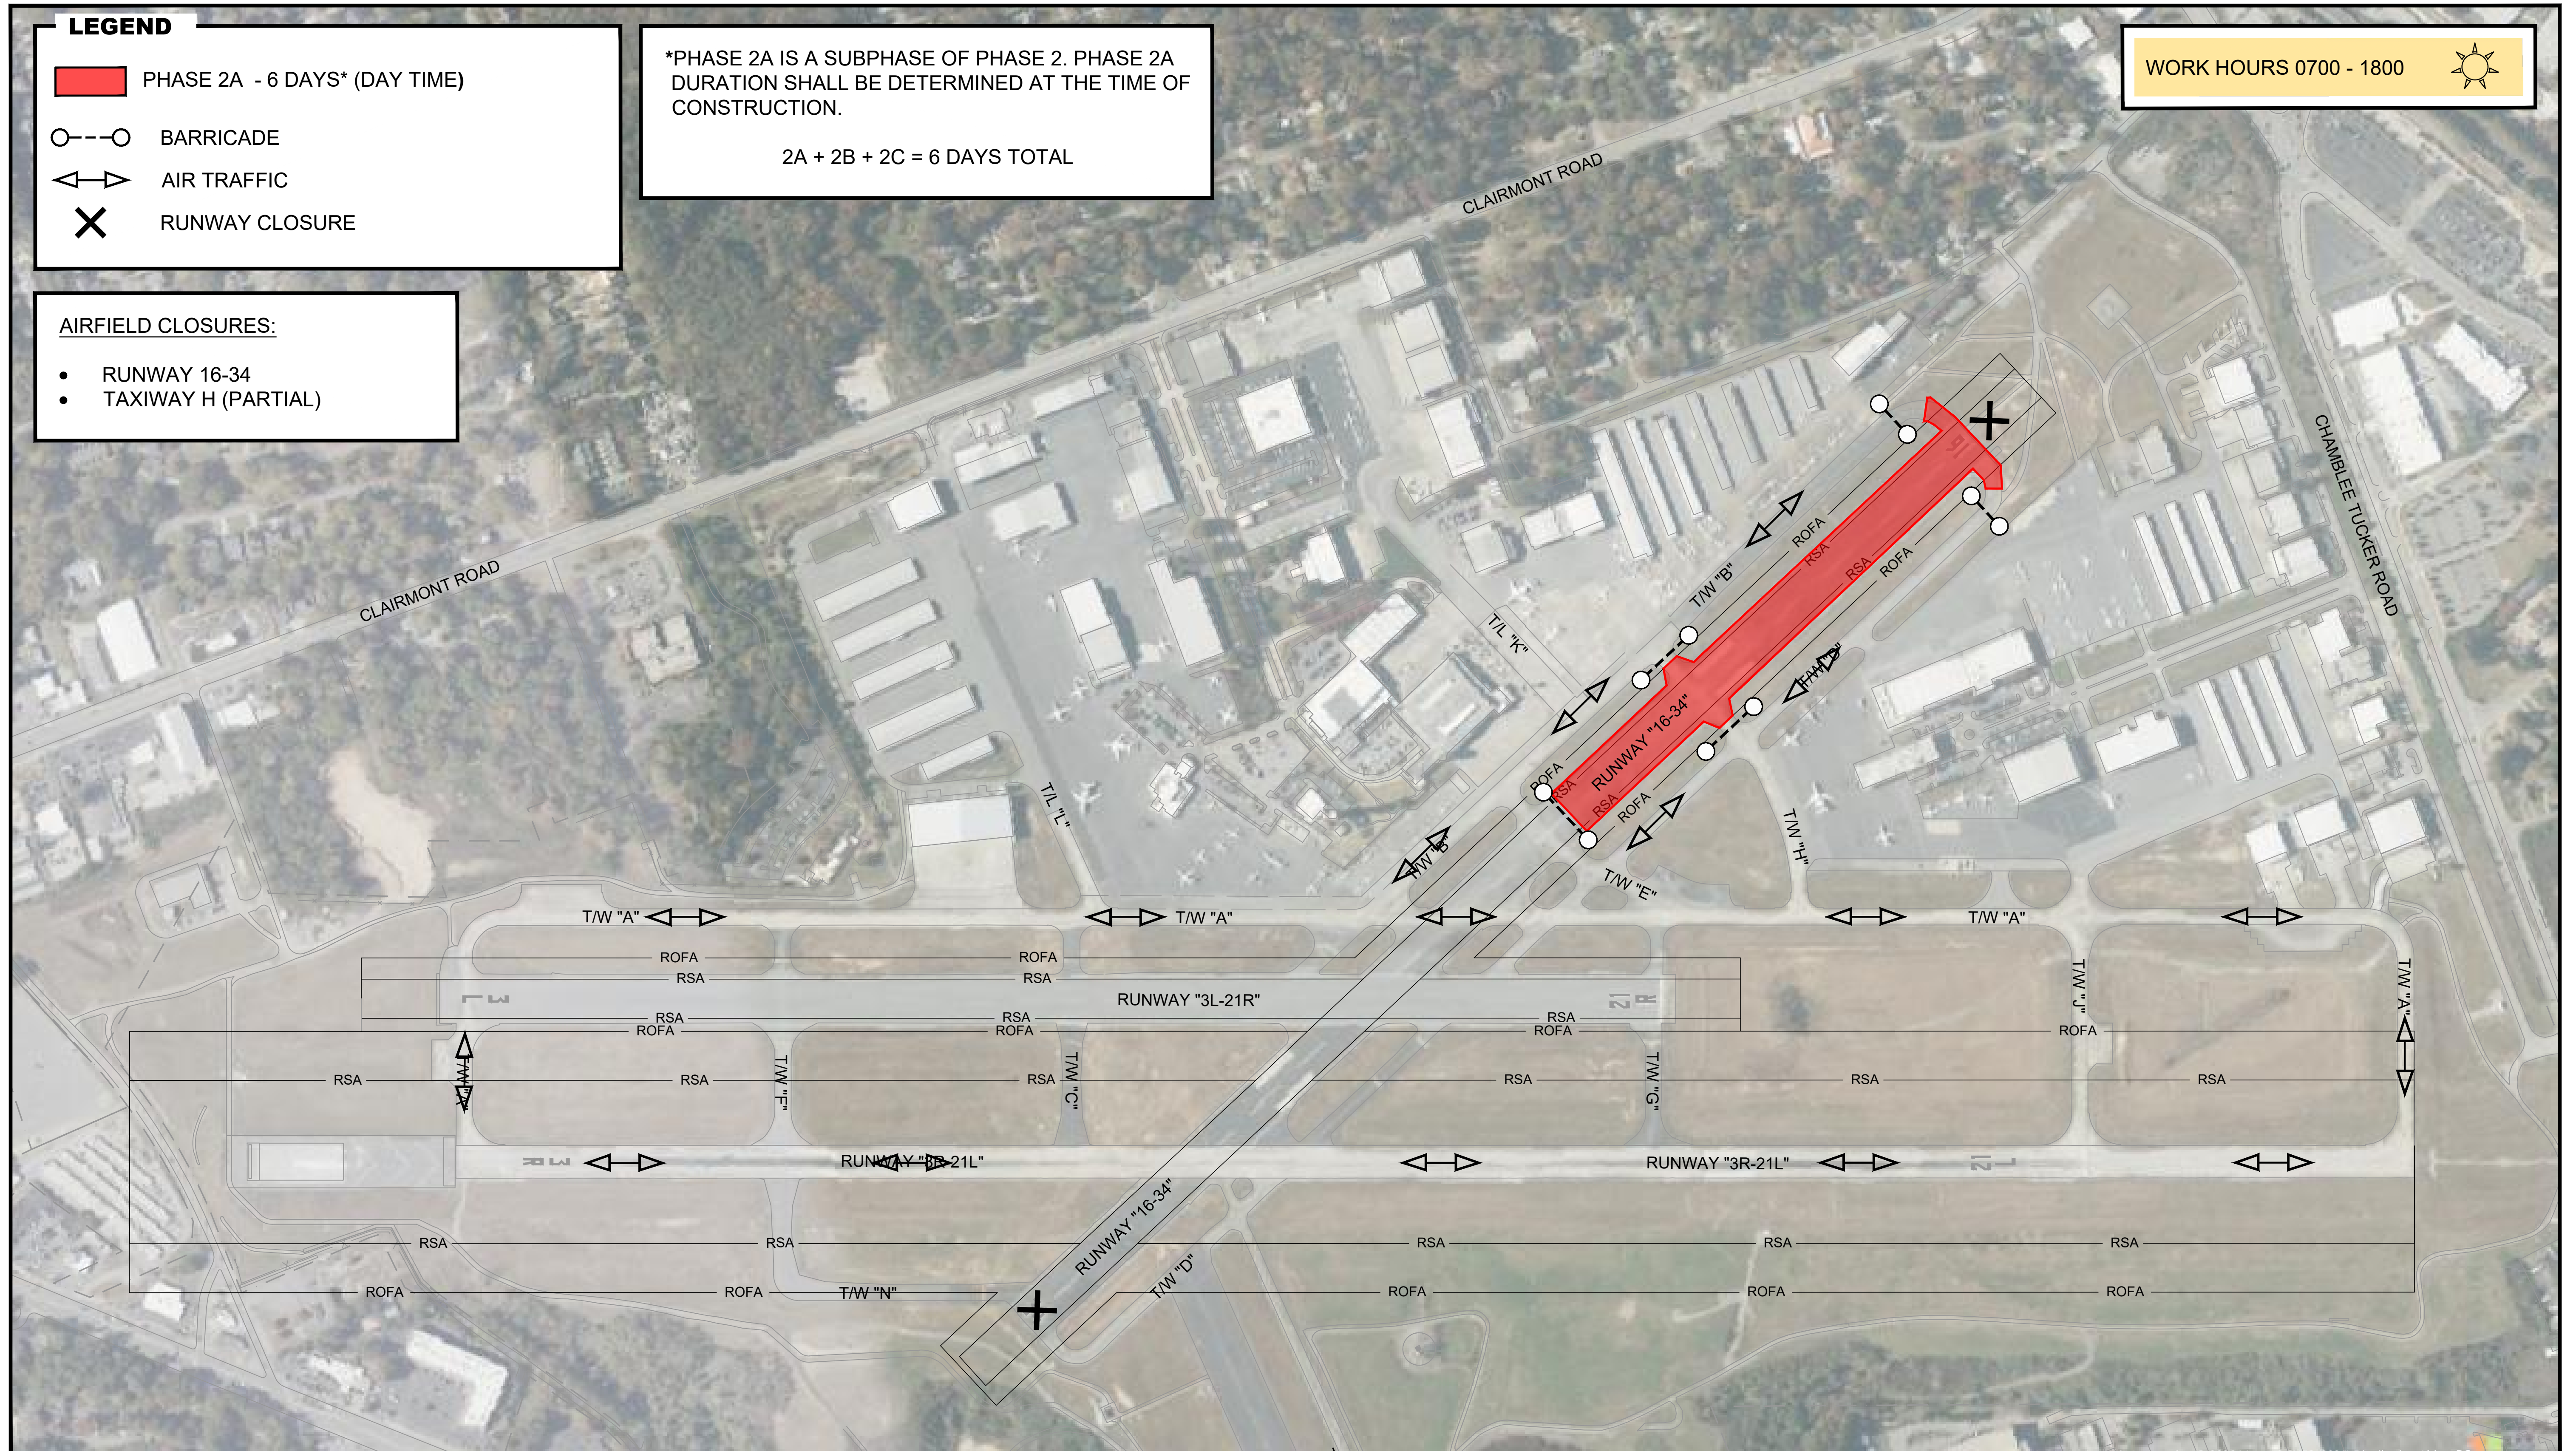

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 2A

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

- PHASE 2B - 6 DAYS* (DAY TIME)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE



AIRFIELD CLOSURES:

- RUNWAY 16-34
- TAXIWAY A (PARTIAL)
- TAXIWAY E (PARTIAL)


*PHASE 2B IS A SUBPHASE OF PHASE 2. PHASE 2B DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

$2A + 2B + 2C = 6 \text{ DAYS TOTAL}$

WORK HOURS 0700 - 1800

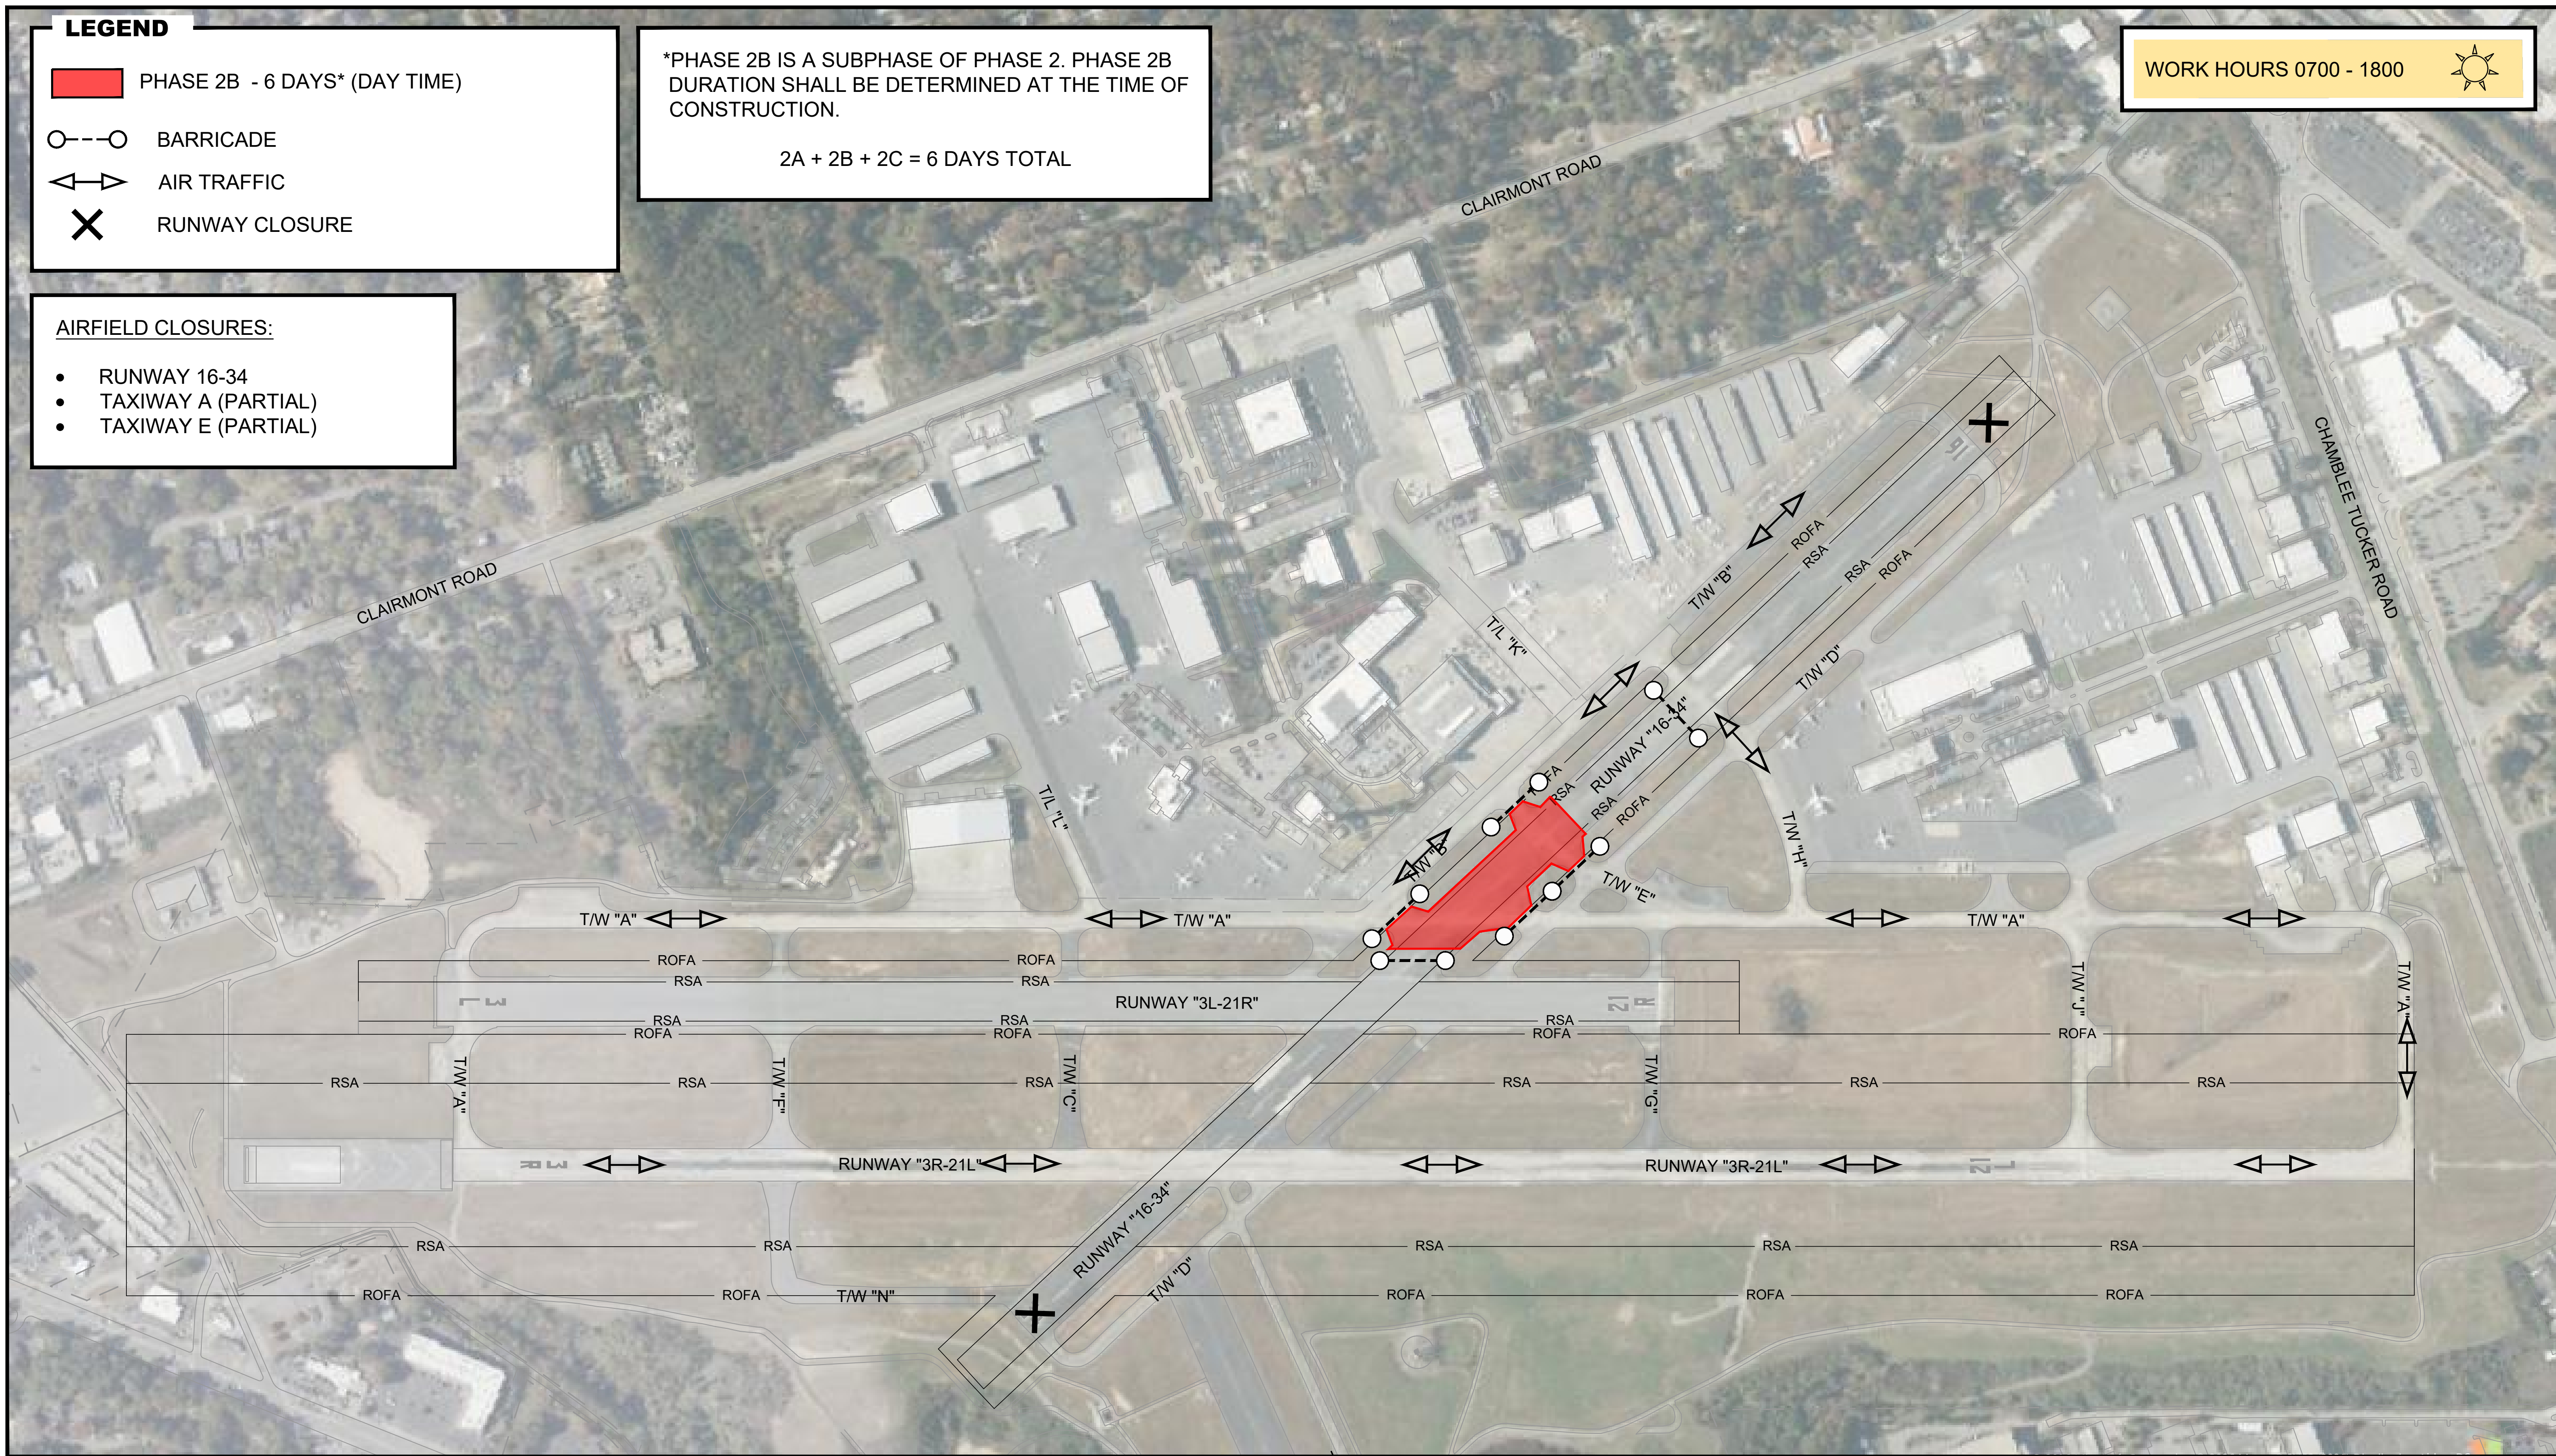

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 2B

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

- PHASE 2C - 6 DAYS* (DAY TIME)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE



AIRFIELD CLOSURES:

- RUNWAY 16-34
- TAXIWAY N


*PHASE 2C IS A SUBPHASE OF PHASE 2. PHASE 2C DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

$$2A + 2B + 2C = 6 \text{ DAYS TOTAL}$$

WORK HOURS 0700 - 1800

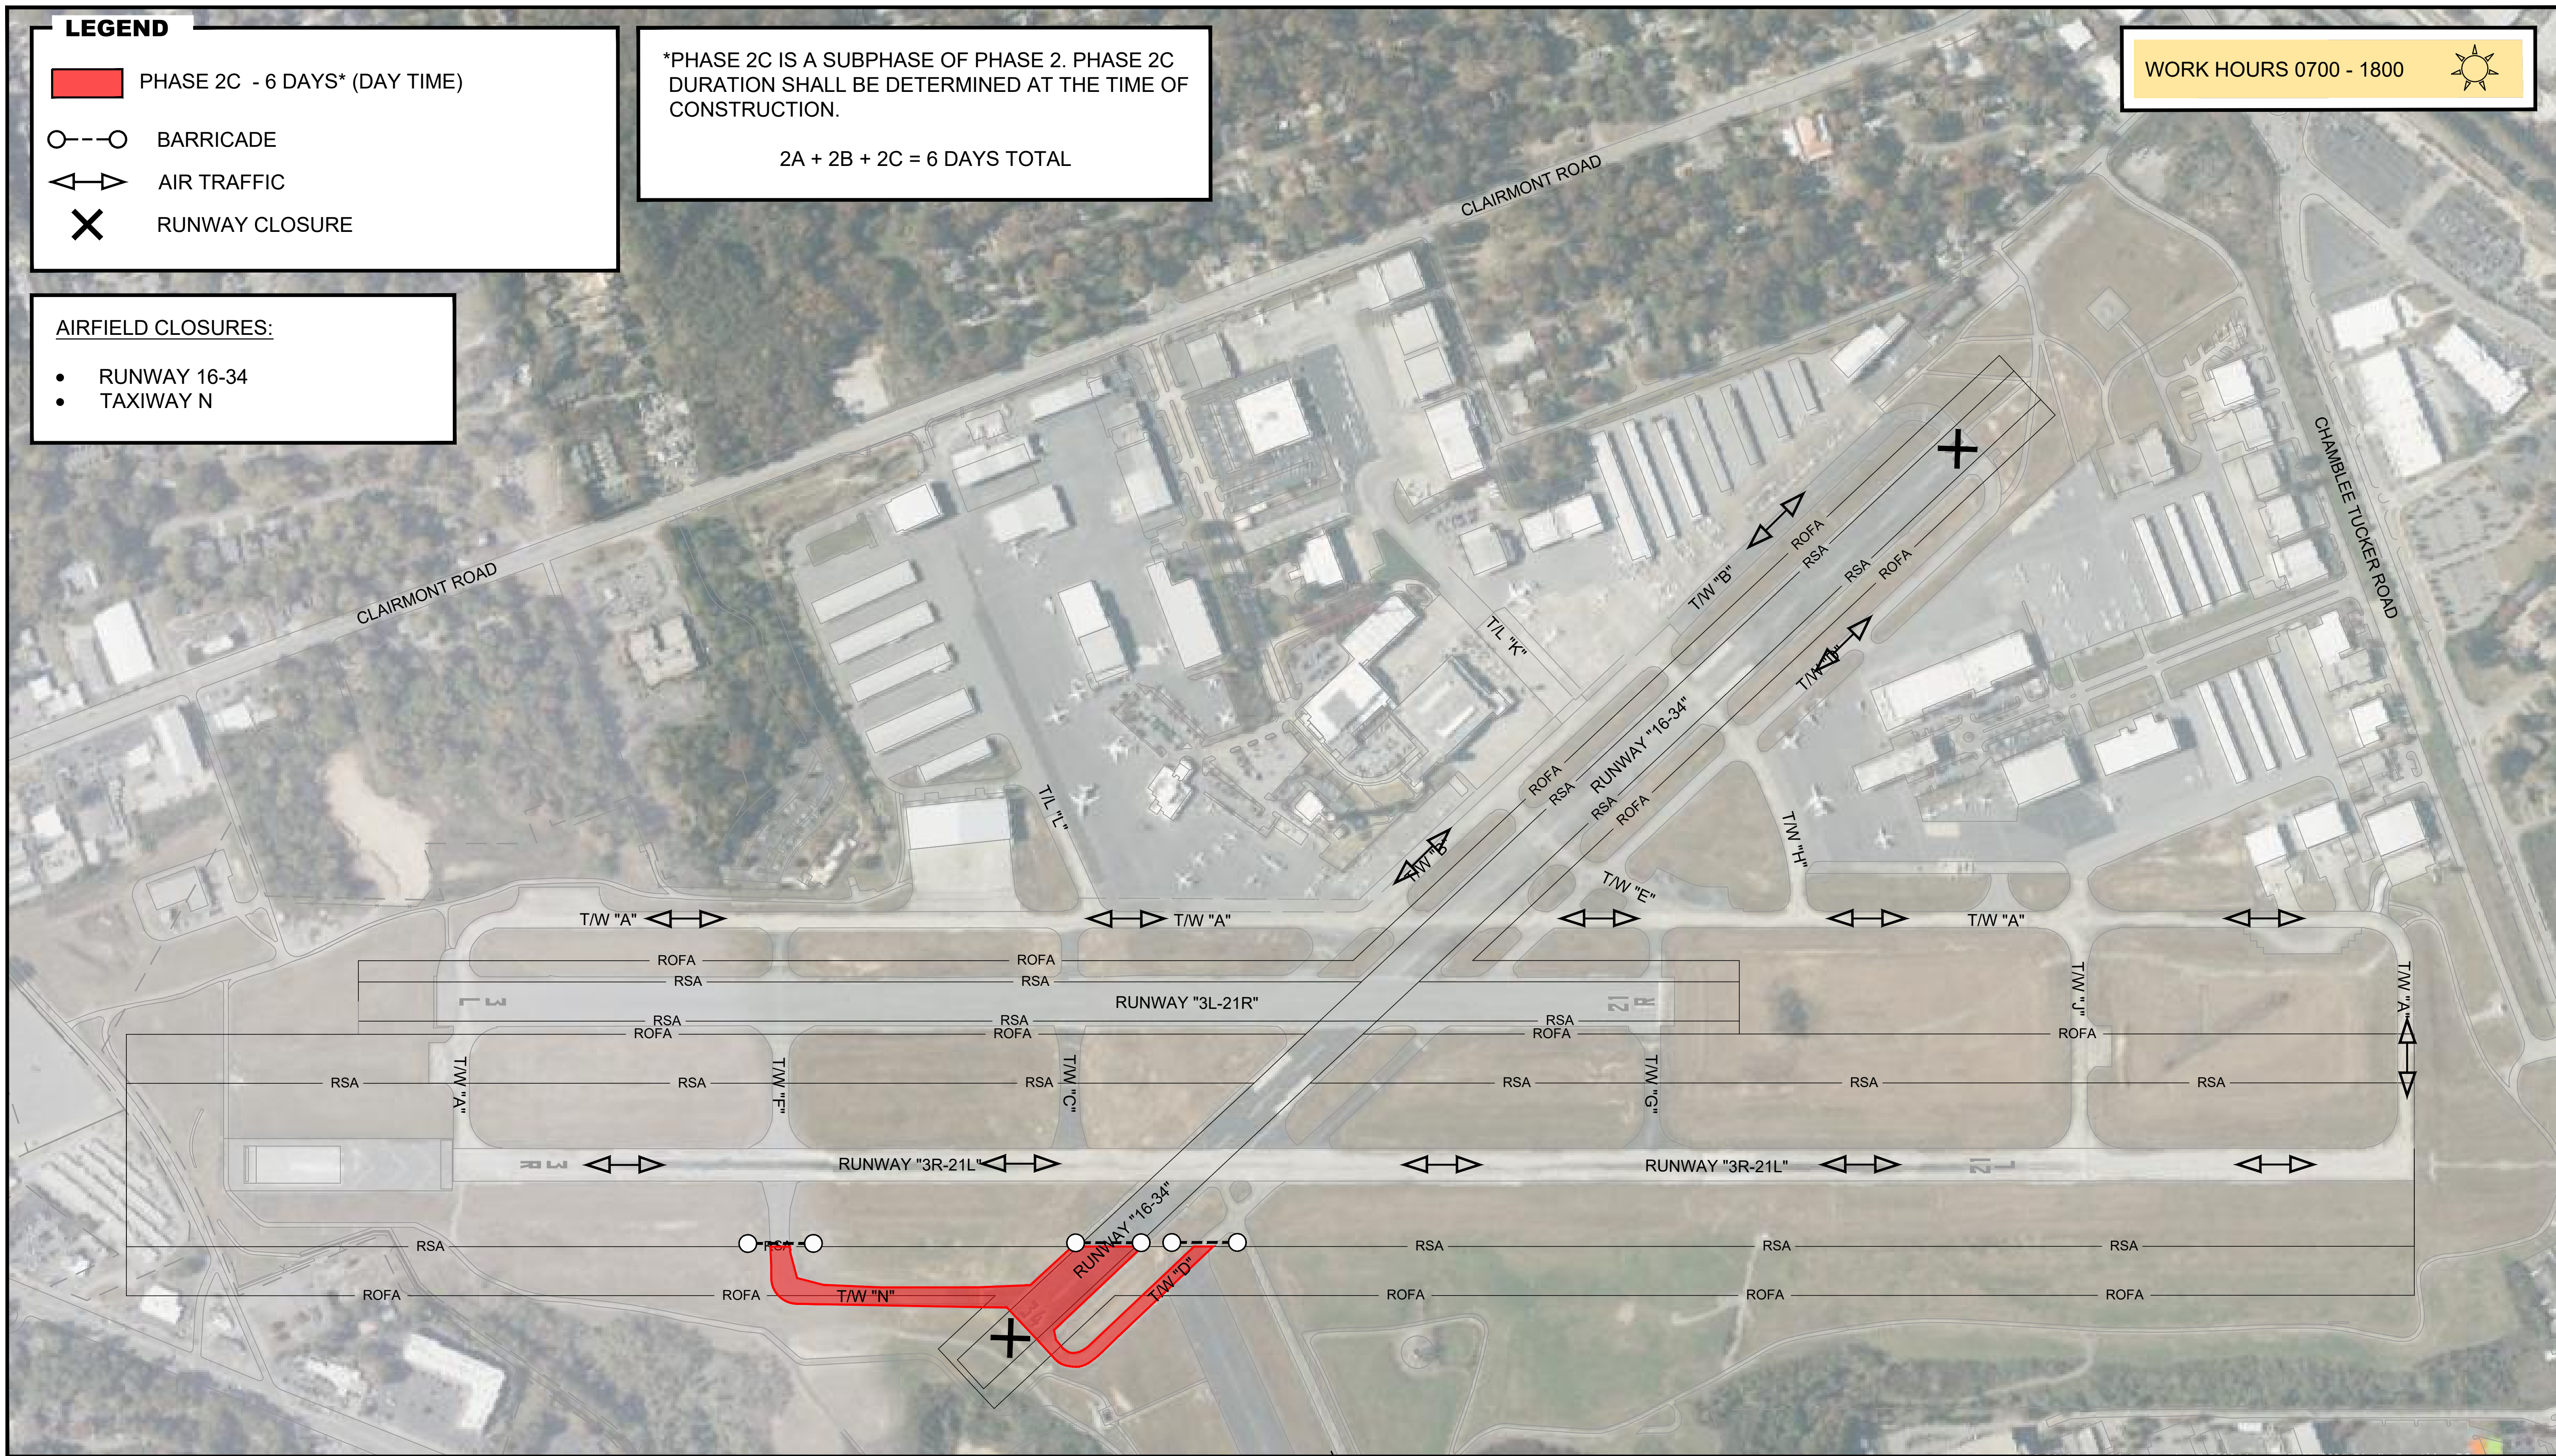

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 2C


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

 PHASE 3A - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- TAXIWAY A (PARTIAL)


*PHASE 3A IS A SUBPHASE OF PHASE 3. PHASE 3A DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800

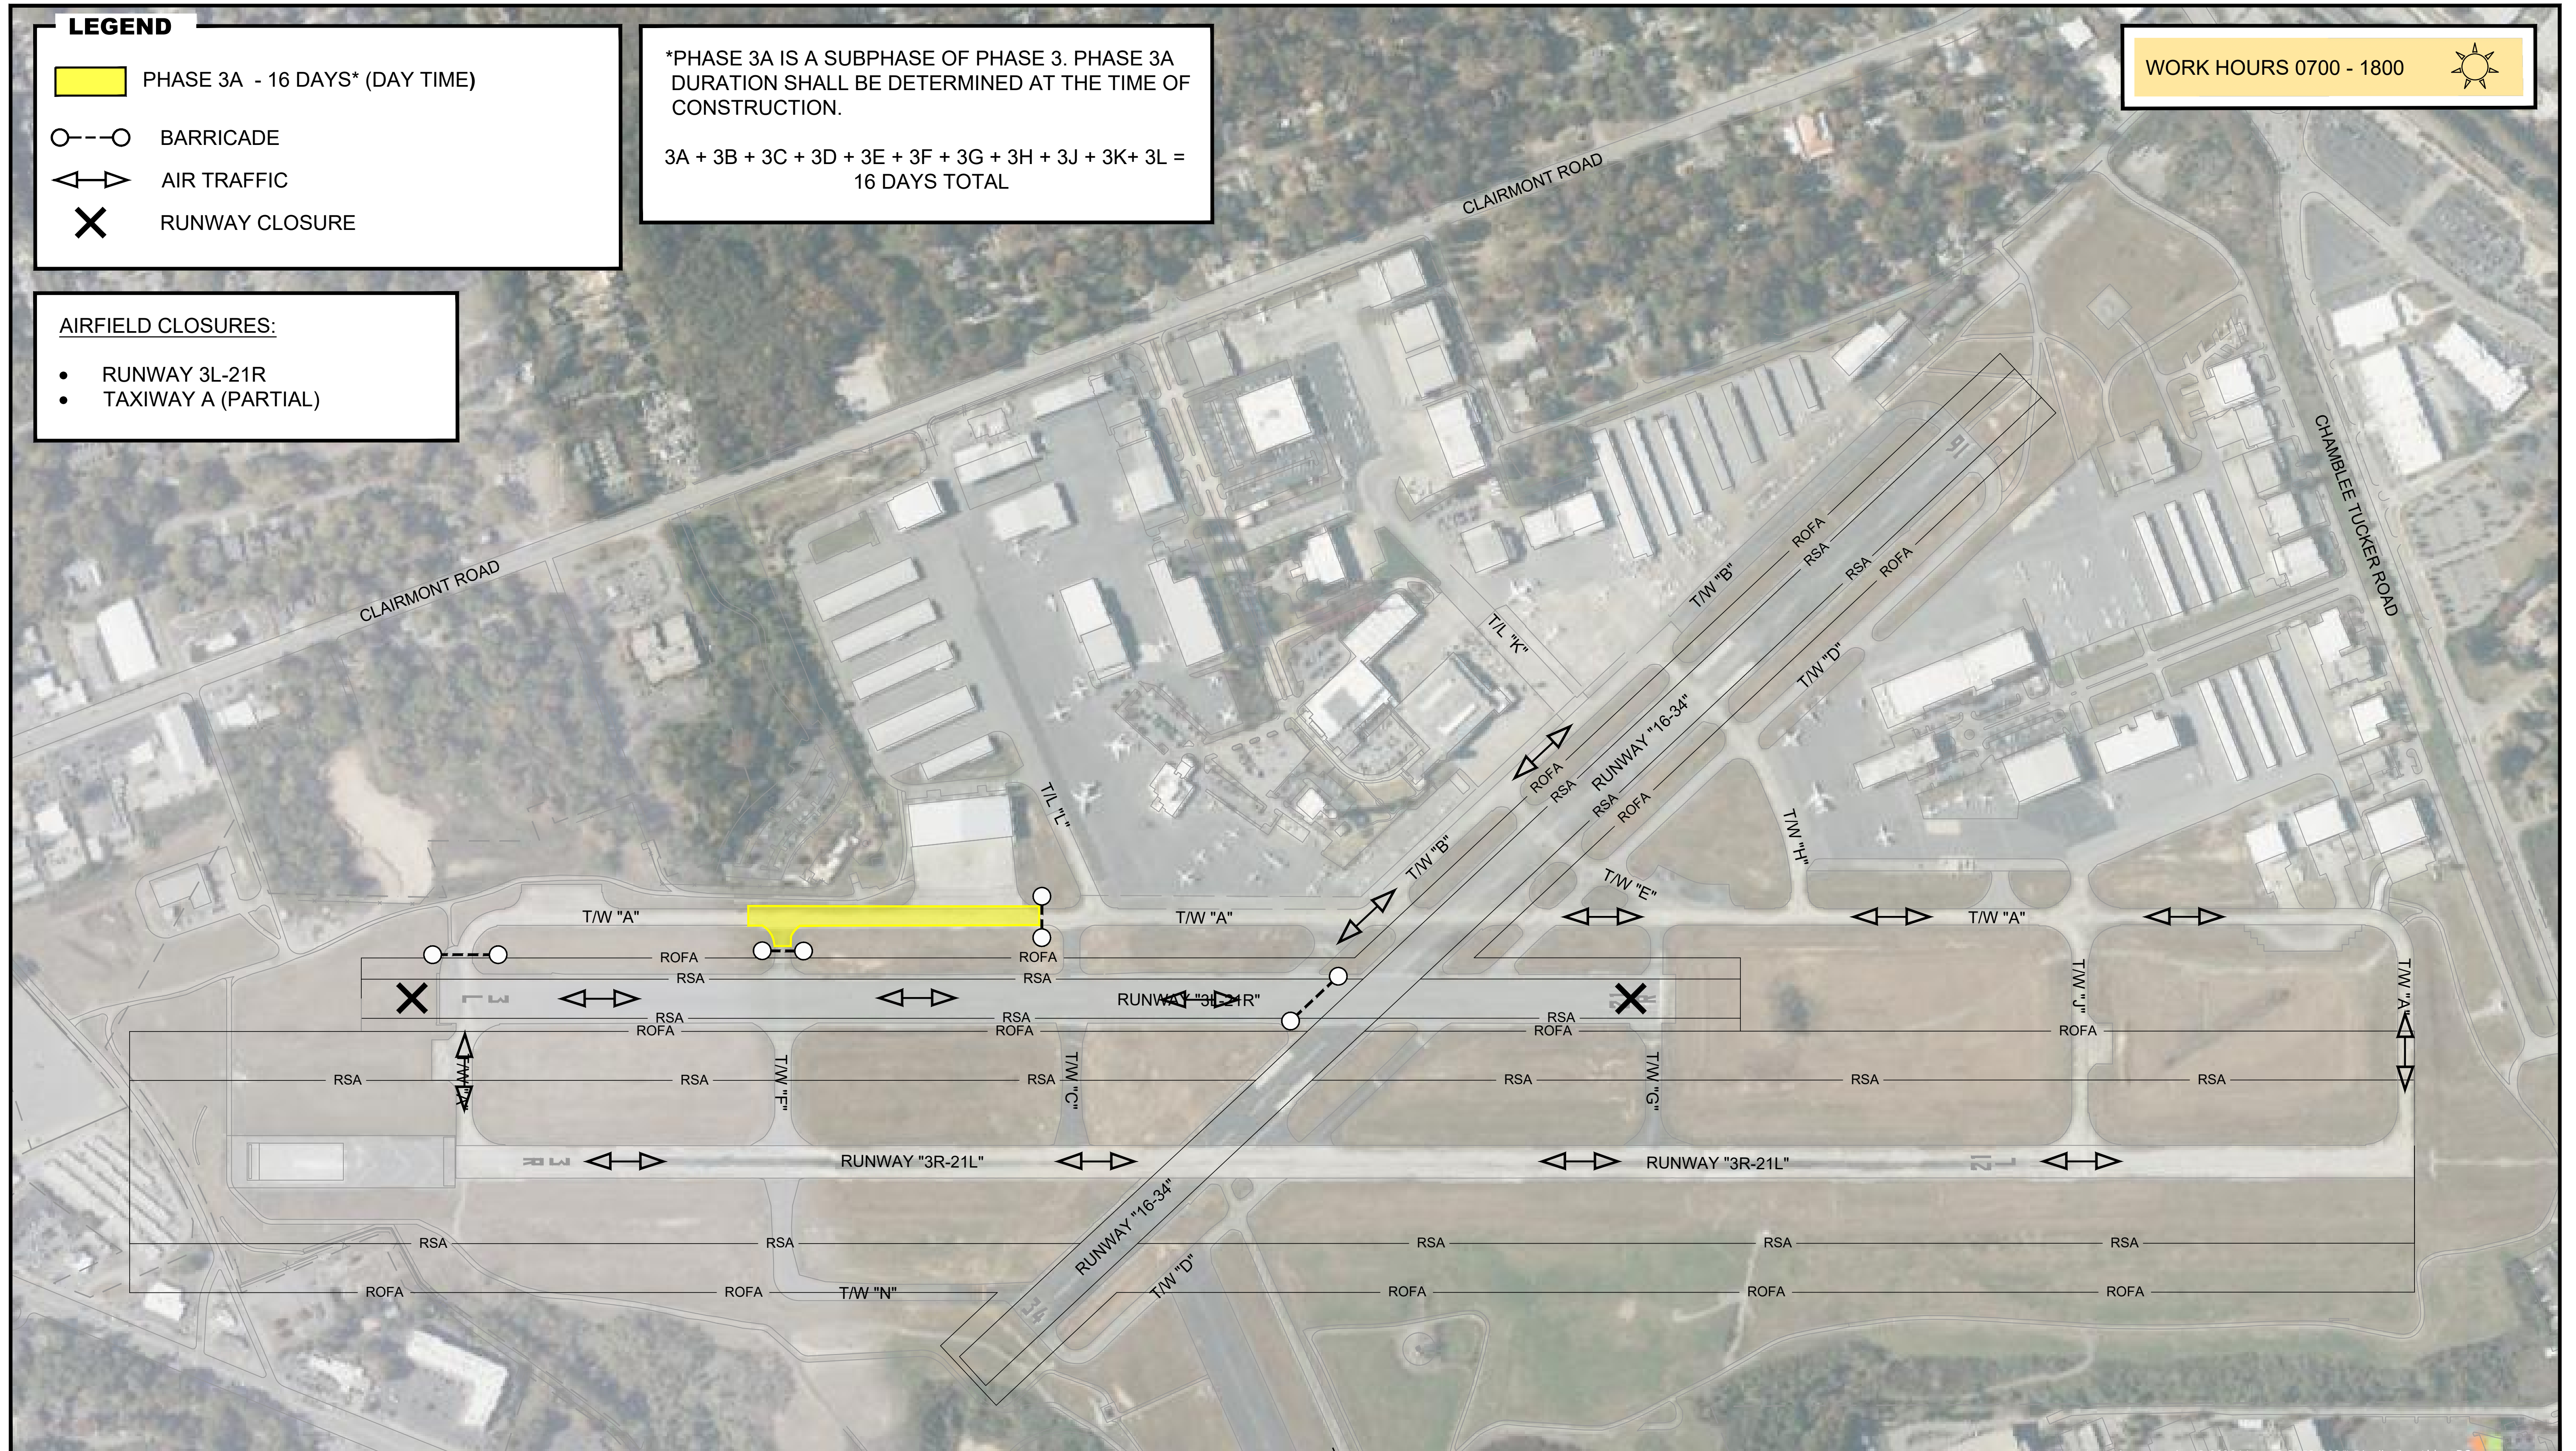

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3A


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

 PHASE 3B - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE


AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- TAXIWAY A (PARTIAL)


*PHASE 3B IS A SUBPHASE OF PHASE 3. PHASE 3B DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800



Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3B


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

 PHASE 3C - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- RUNWAY 16-34
- TAXIWAY A (PARTIAL)
- TAXIWAY B (PARTIAL)


*PHASE 3C IS A SUBPHASE OF PHASE 3. PHASE 3C DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L =
16 DAYS TOTAL

WORK HOURS 0700 - 1800

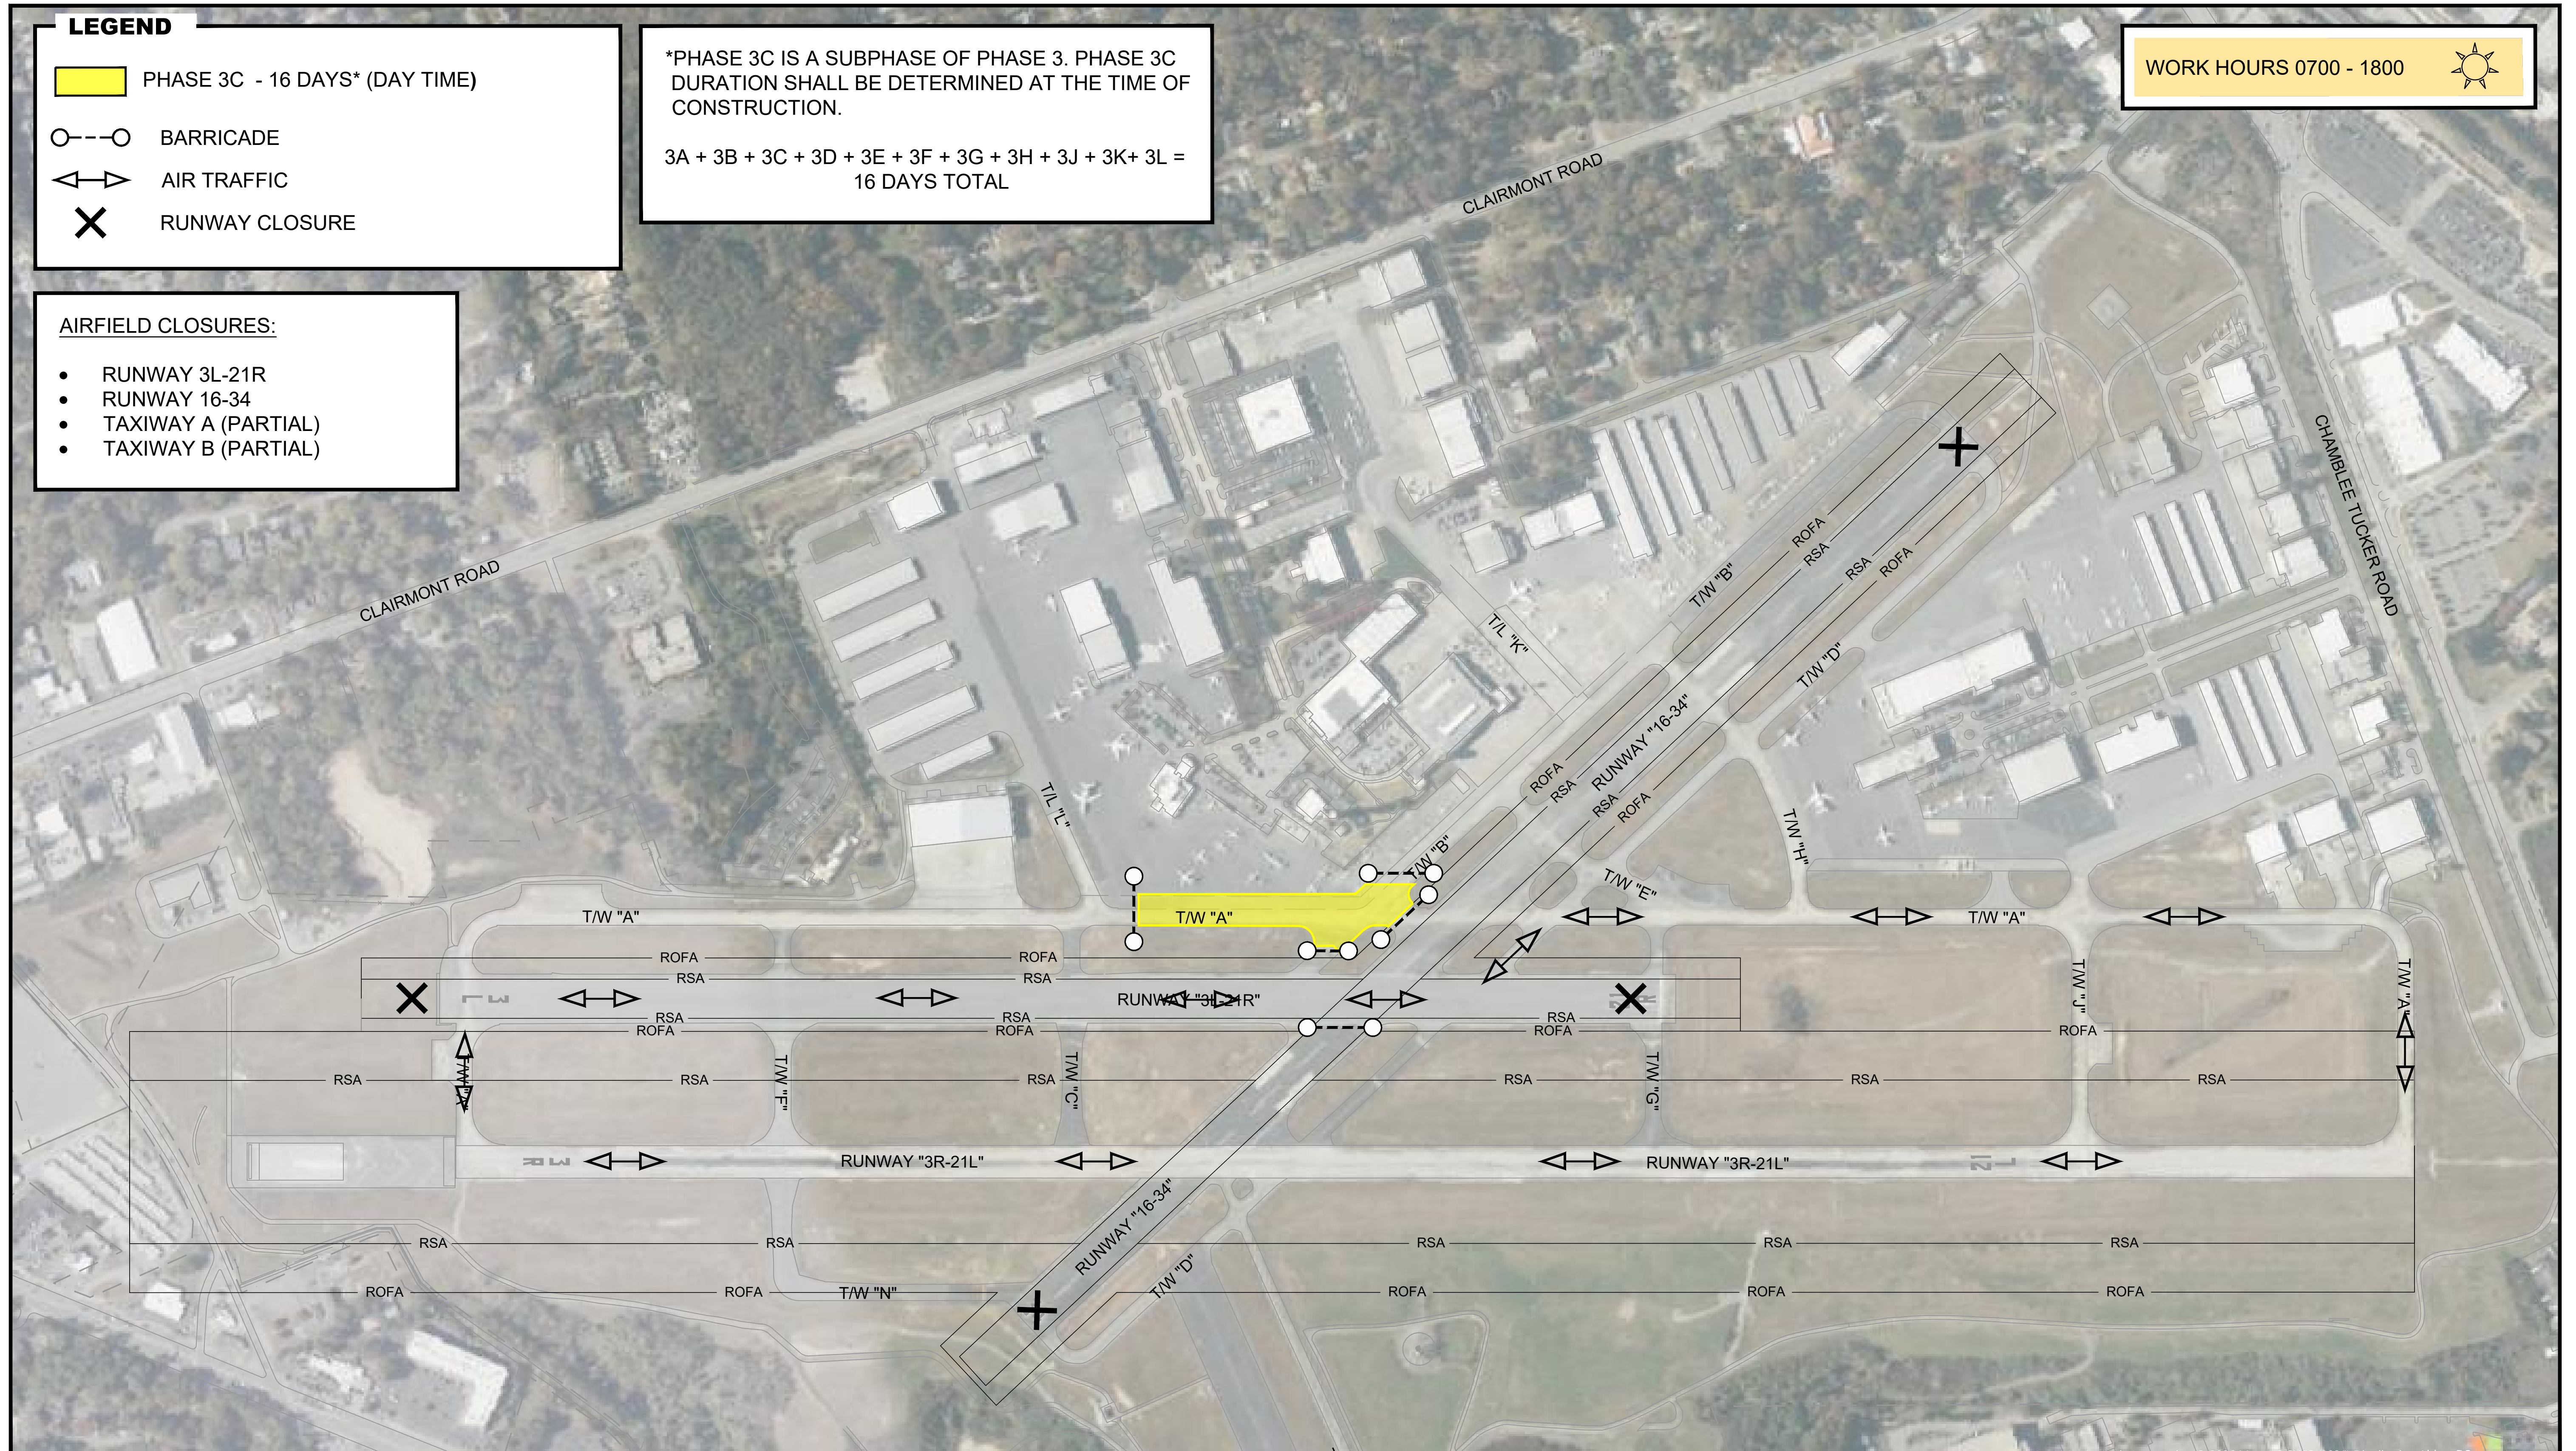

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3C


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:58pm

LEGEND

 PHASE 3D - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY B (PARTIAL)


*PHASE 3D IS A SUBPHASE OF PHASE 3. PHASE 3D DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L =
16 DAYS TOTAL

WORK HOURS 0700 - 1800

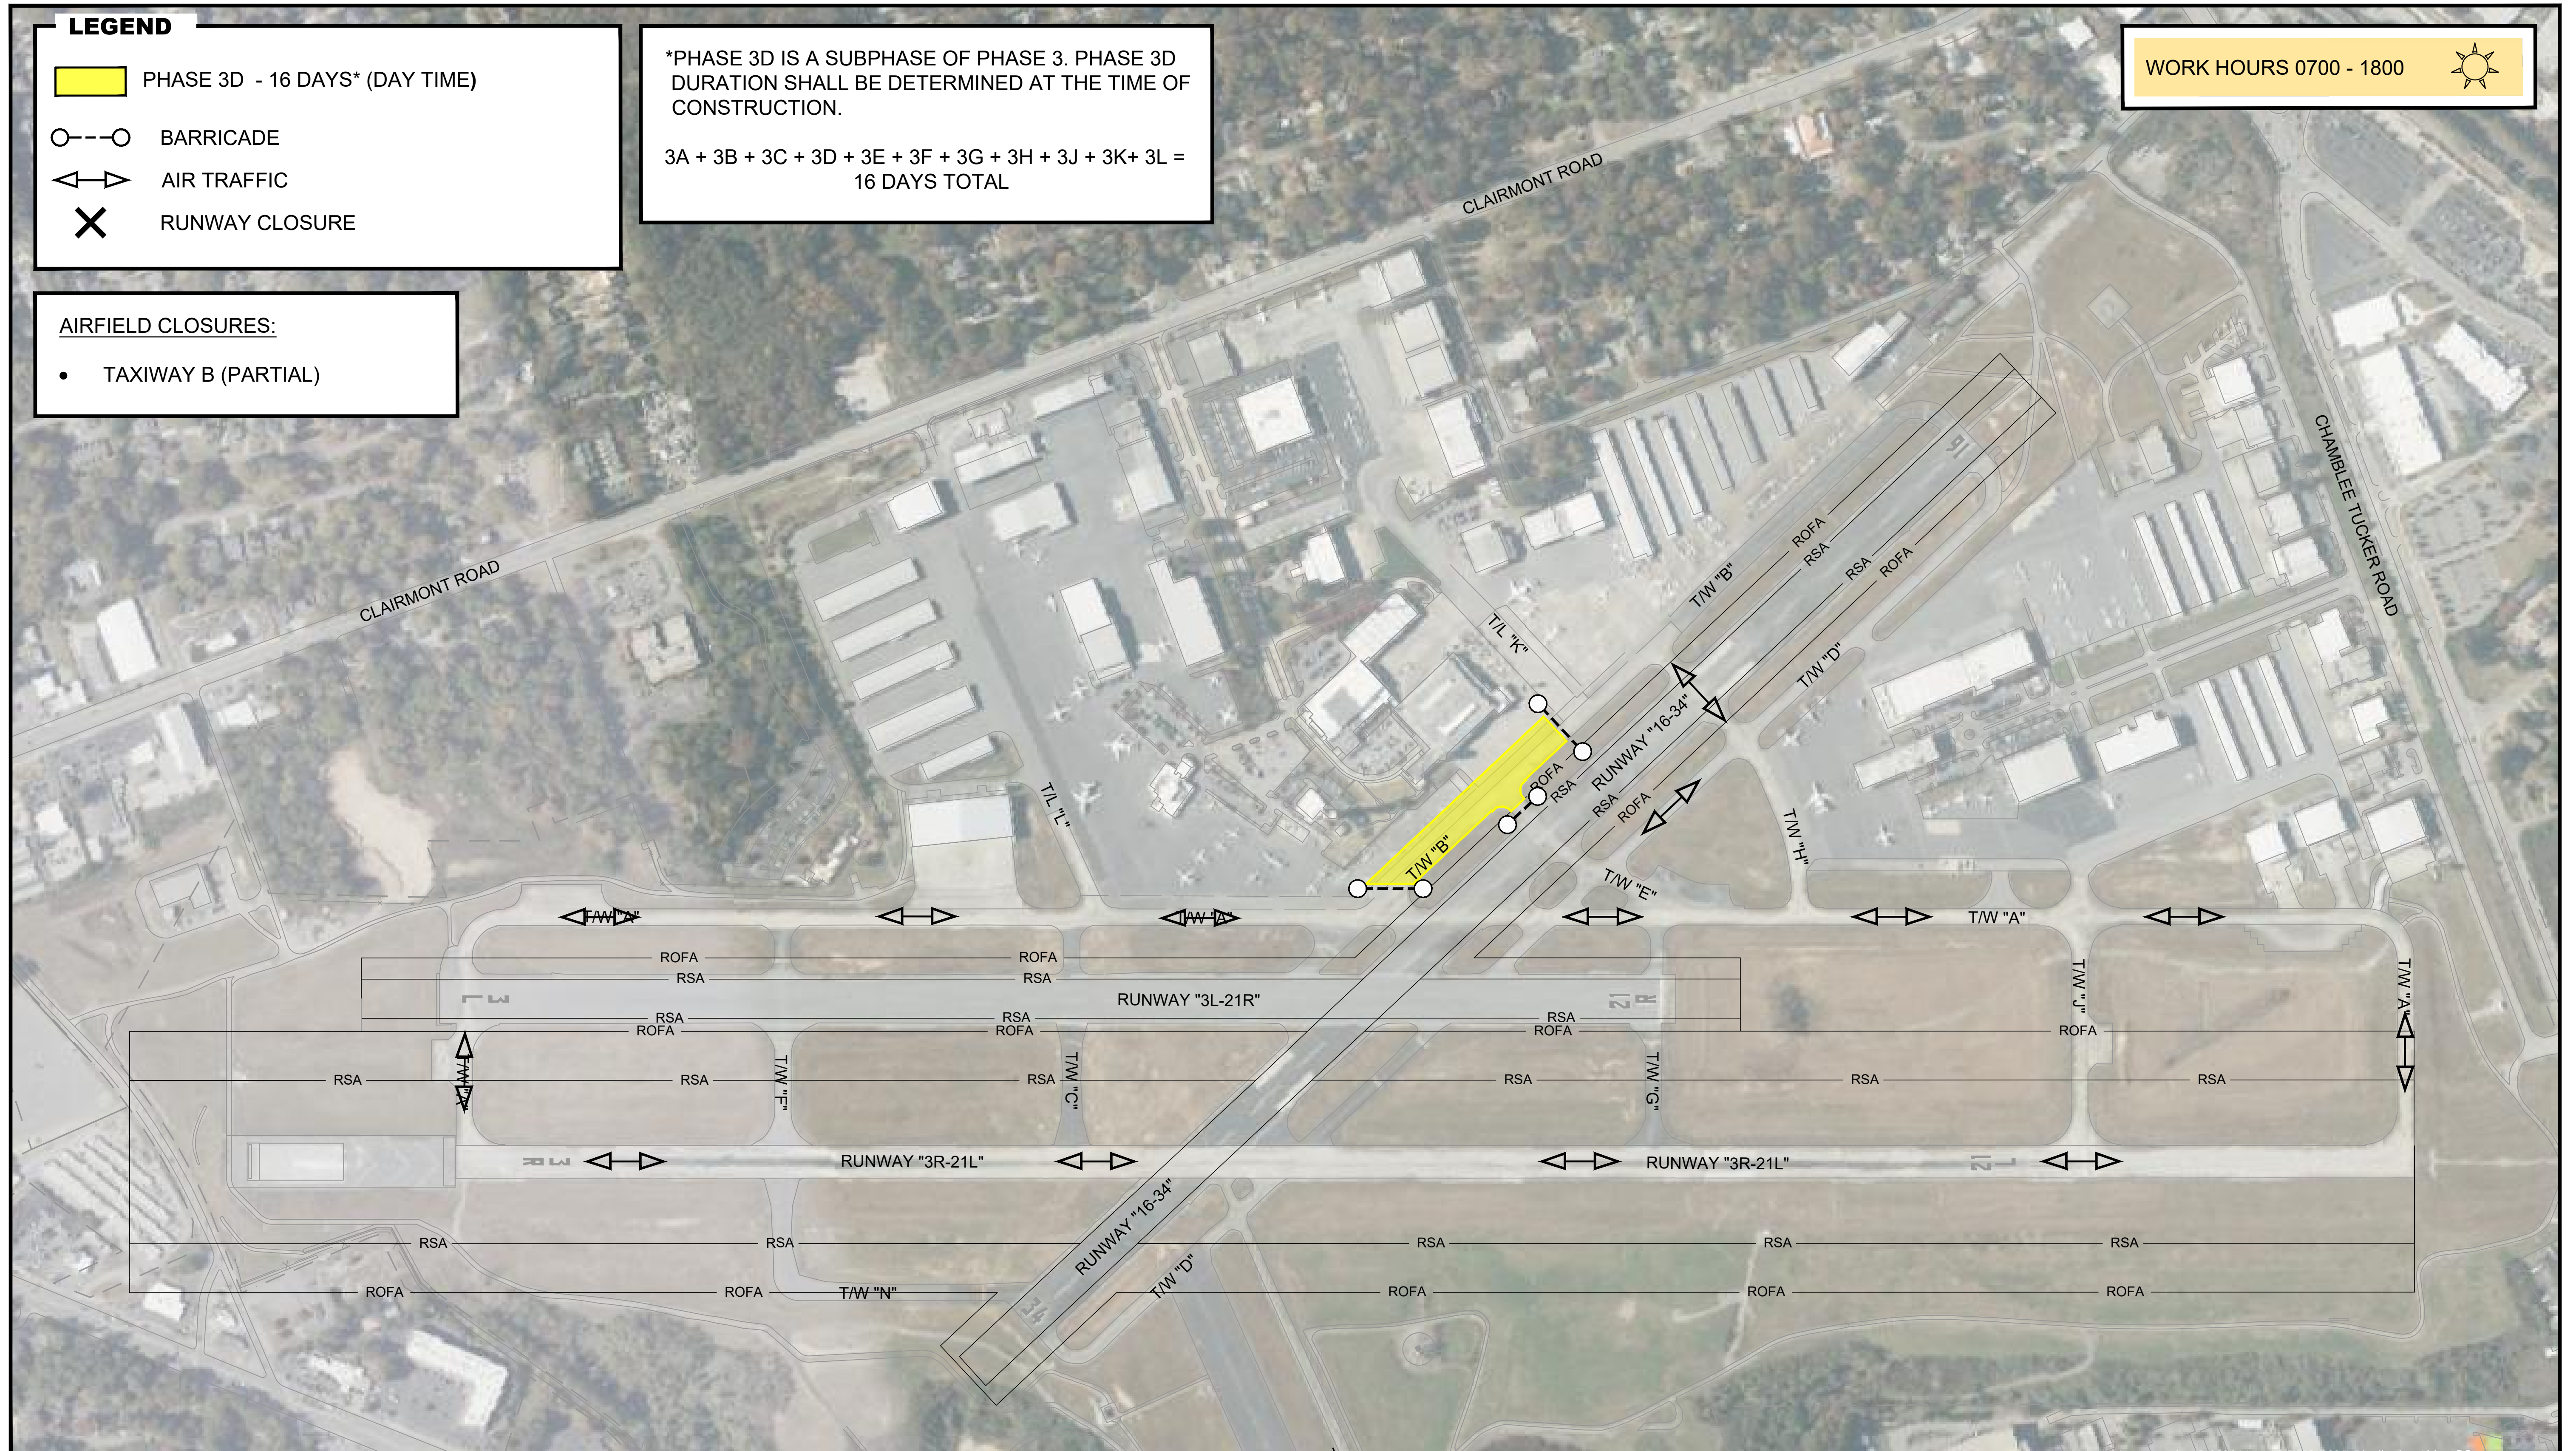

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3D


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3E - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY B (PARTIAL)


*PHASE 3E IS A SUBPHASE OF PHASE 3. PHASE 3E DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L =
16 DAYS TOTAL

WORK HOURS 0700 - 1800

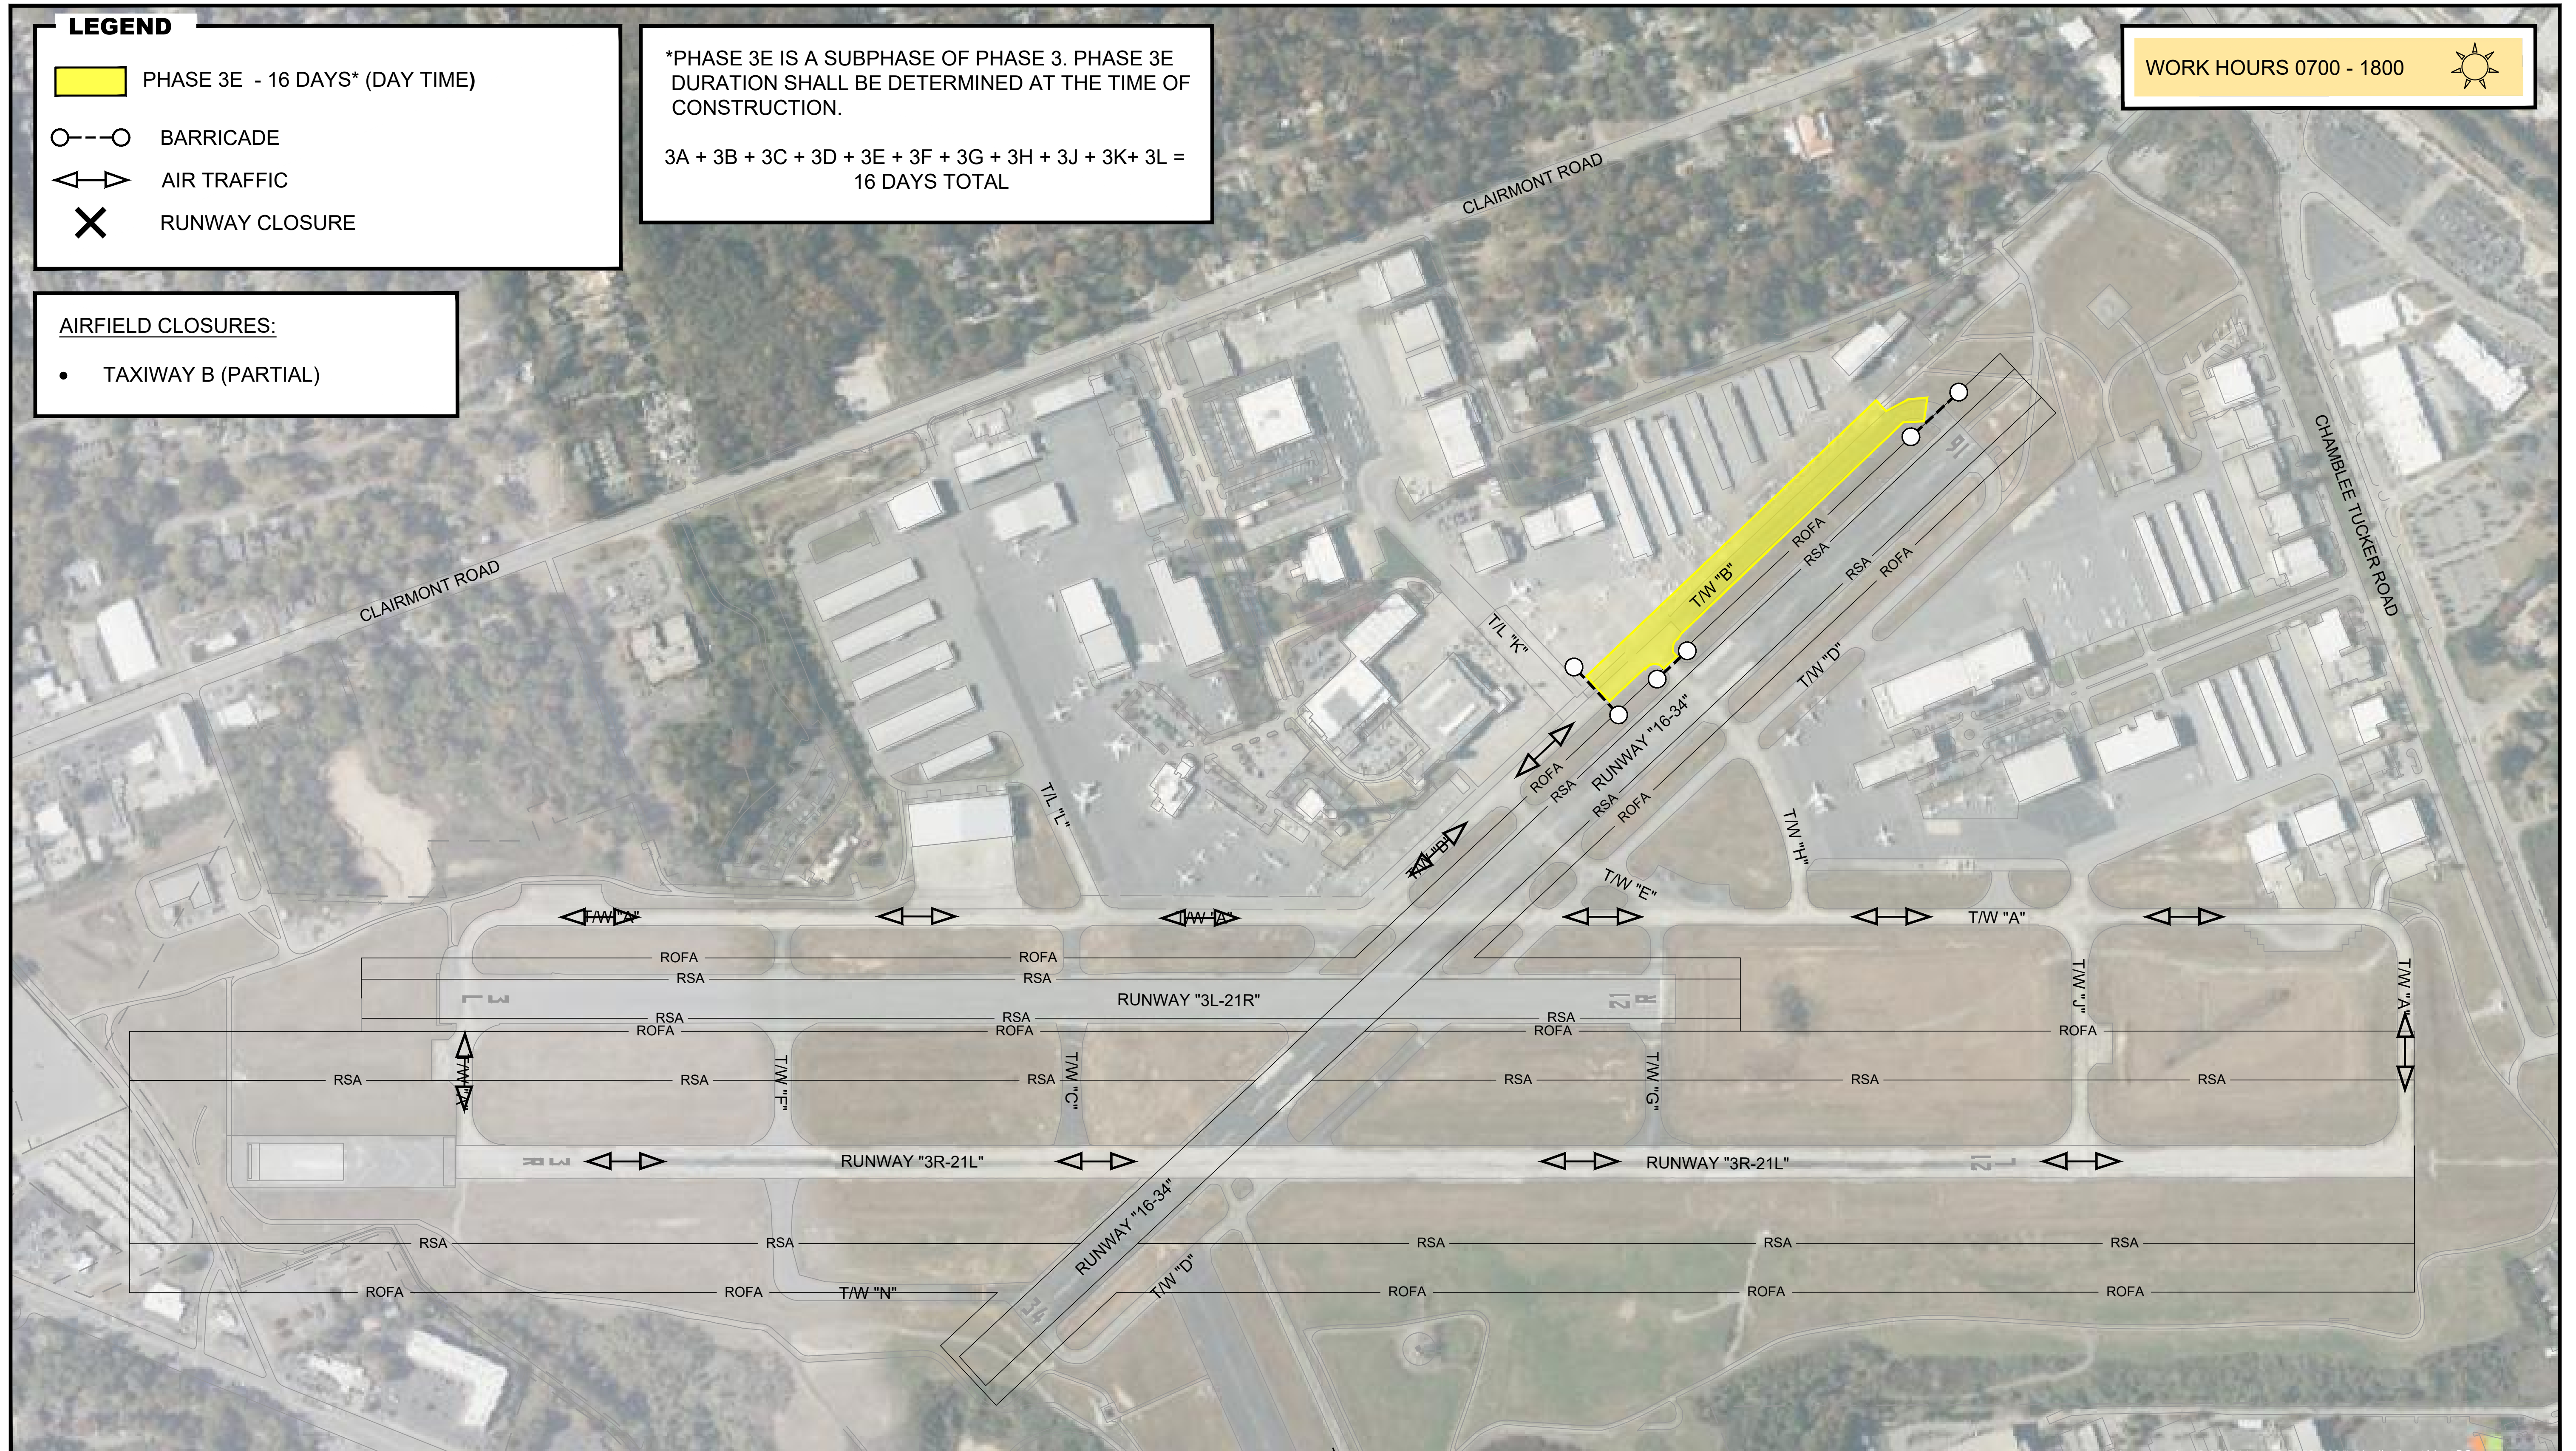

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3E


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3F - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY A (PARTIAL)
- TAXIWAY J


*PHASE 3F IS A SUBPHASE OF PHASE 3. PHASE 3F DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800

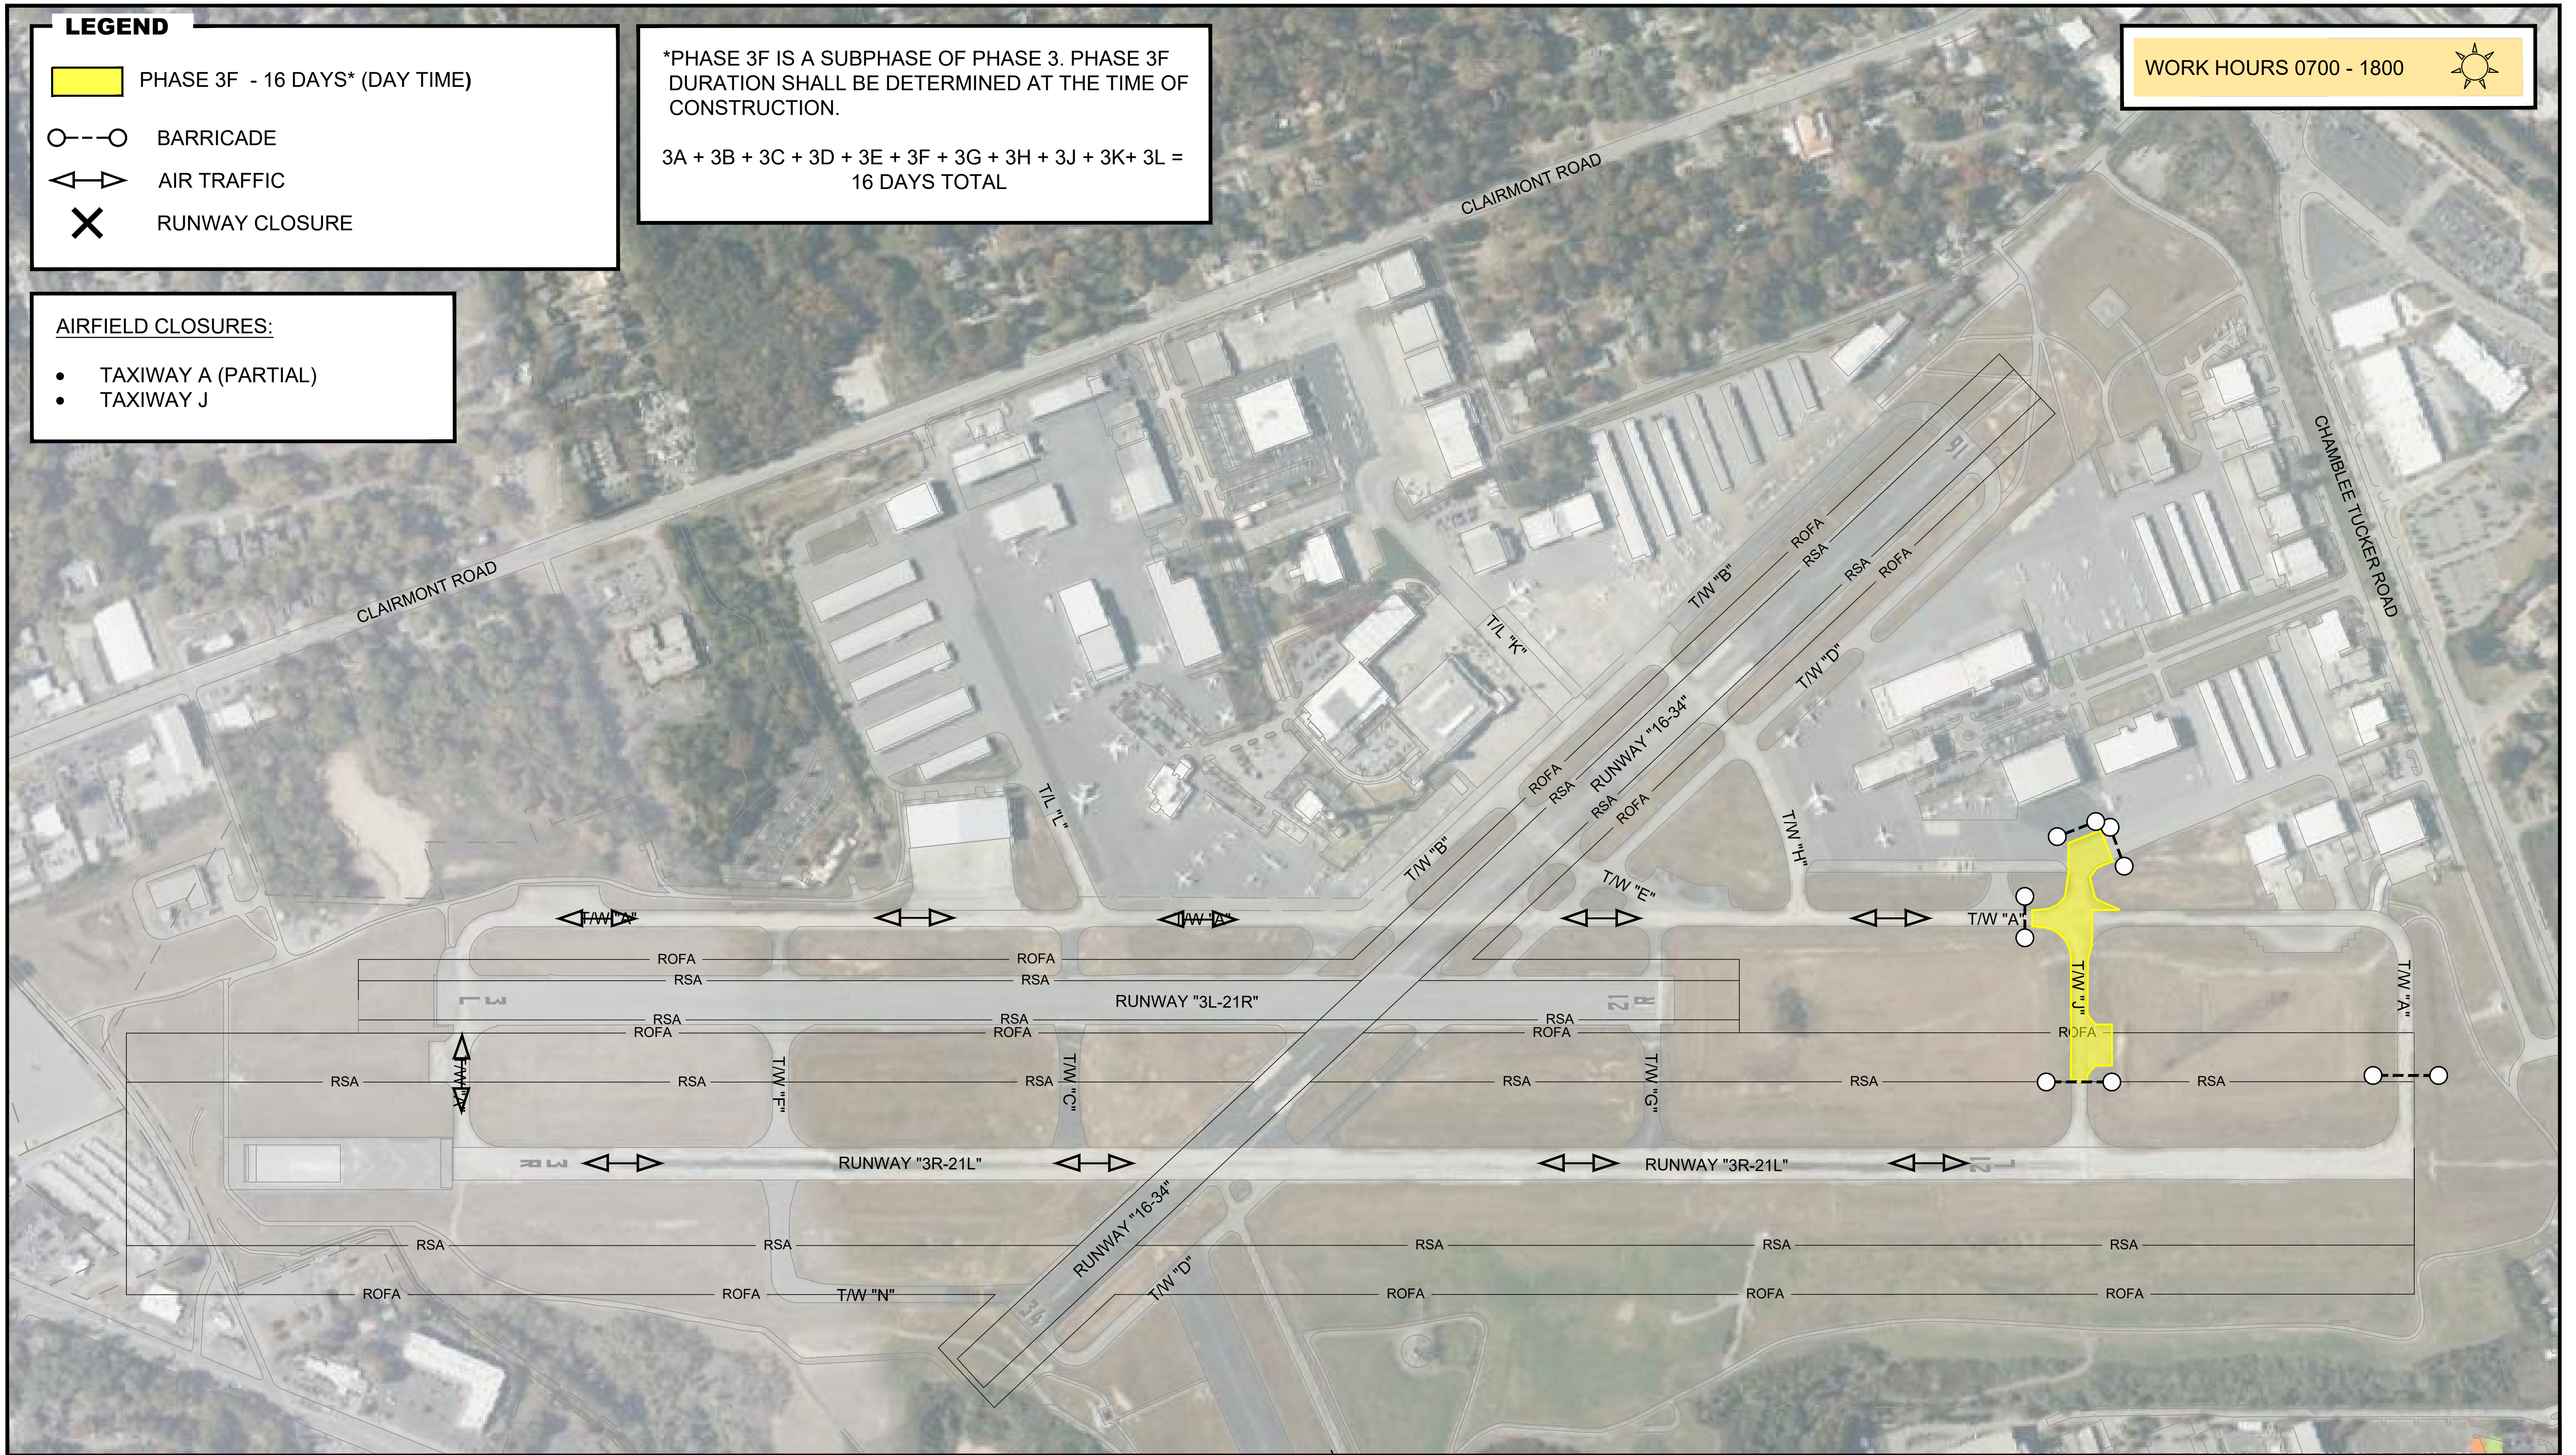

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3F


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3G - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY A (PARTIAL)


*PHASE 3G IS A SUBPHASE OF PHASE 3. PHASE 3G DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L =
16 DAYS TOTAL

WORK HOURS 0700 - 1800

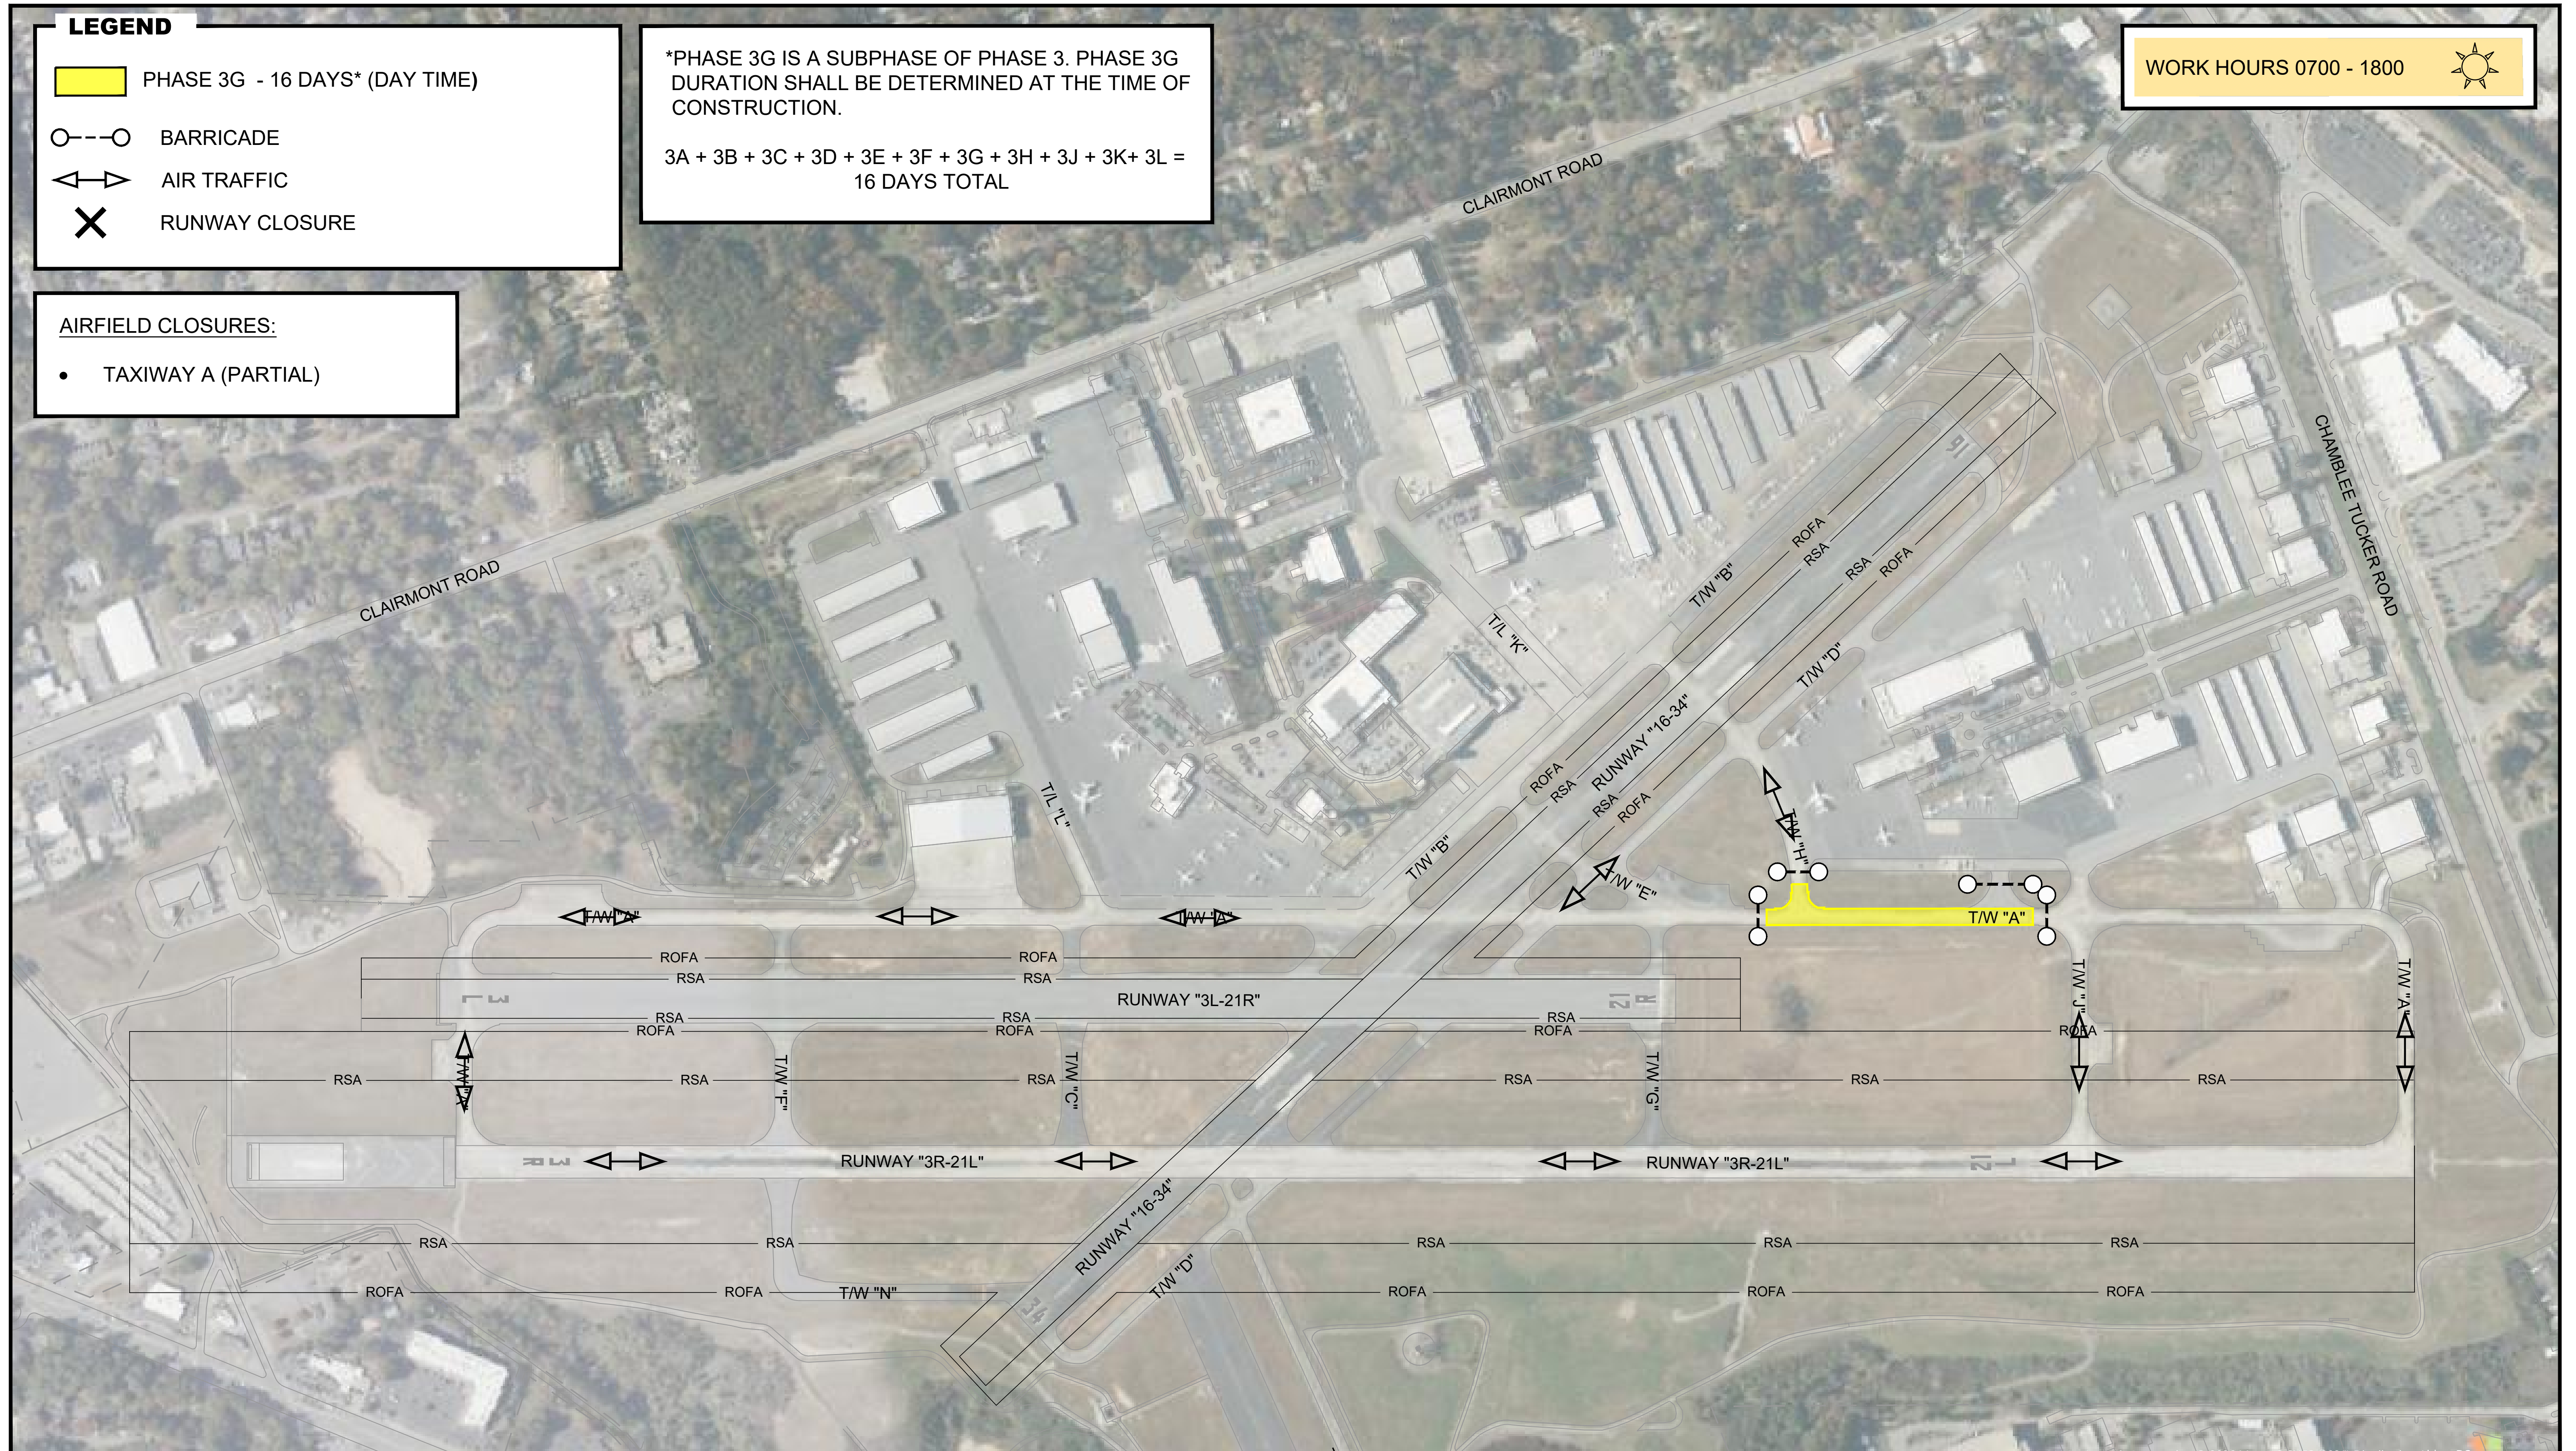

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3G


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3H - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY A (PARTIAL)
- TAXIWAY E (PARTIAL)


*PHASE 3H IS A SUBPHASE OF PHASE 3. PHASE 3H DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800

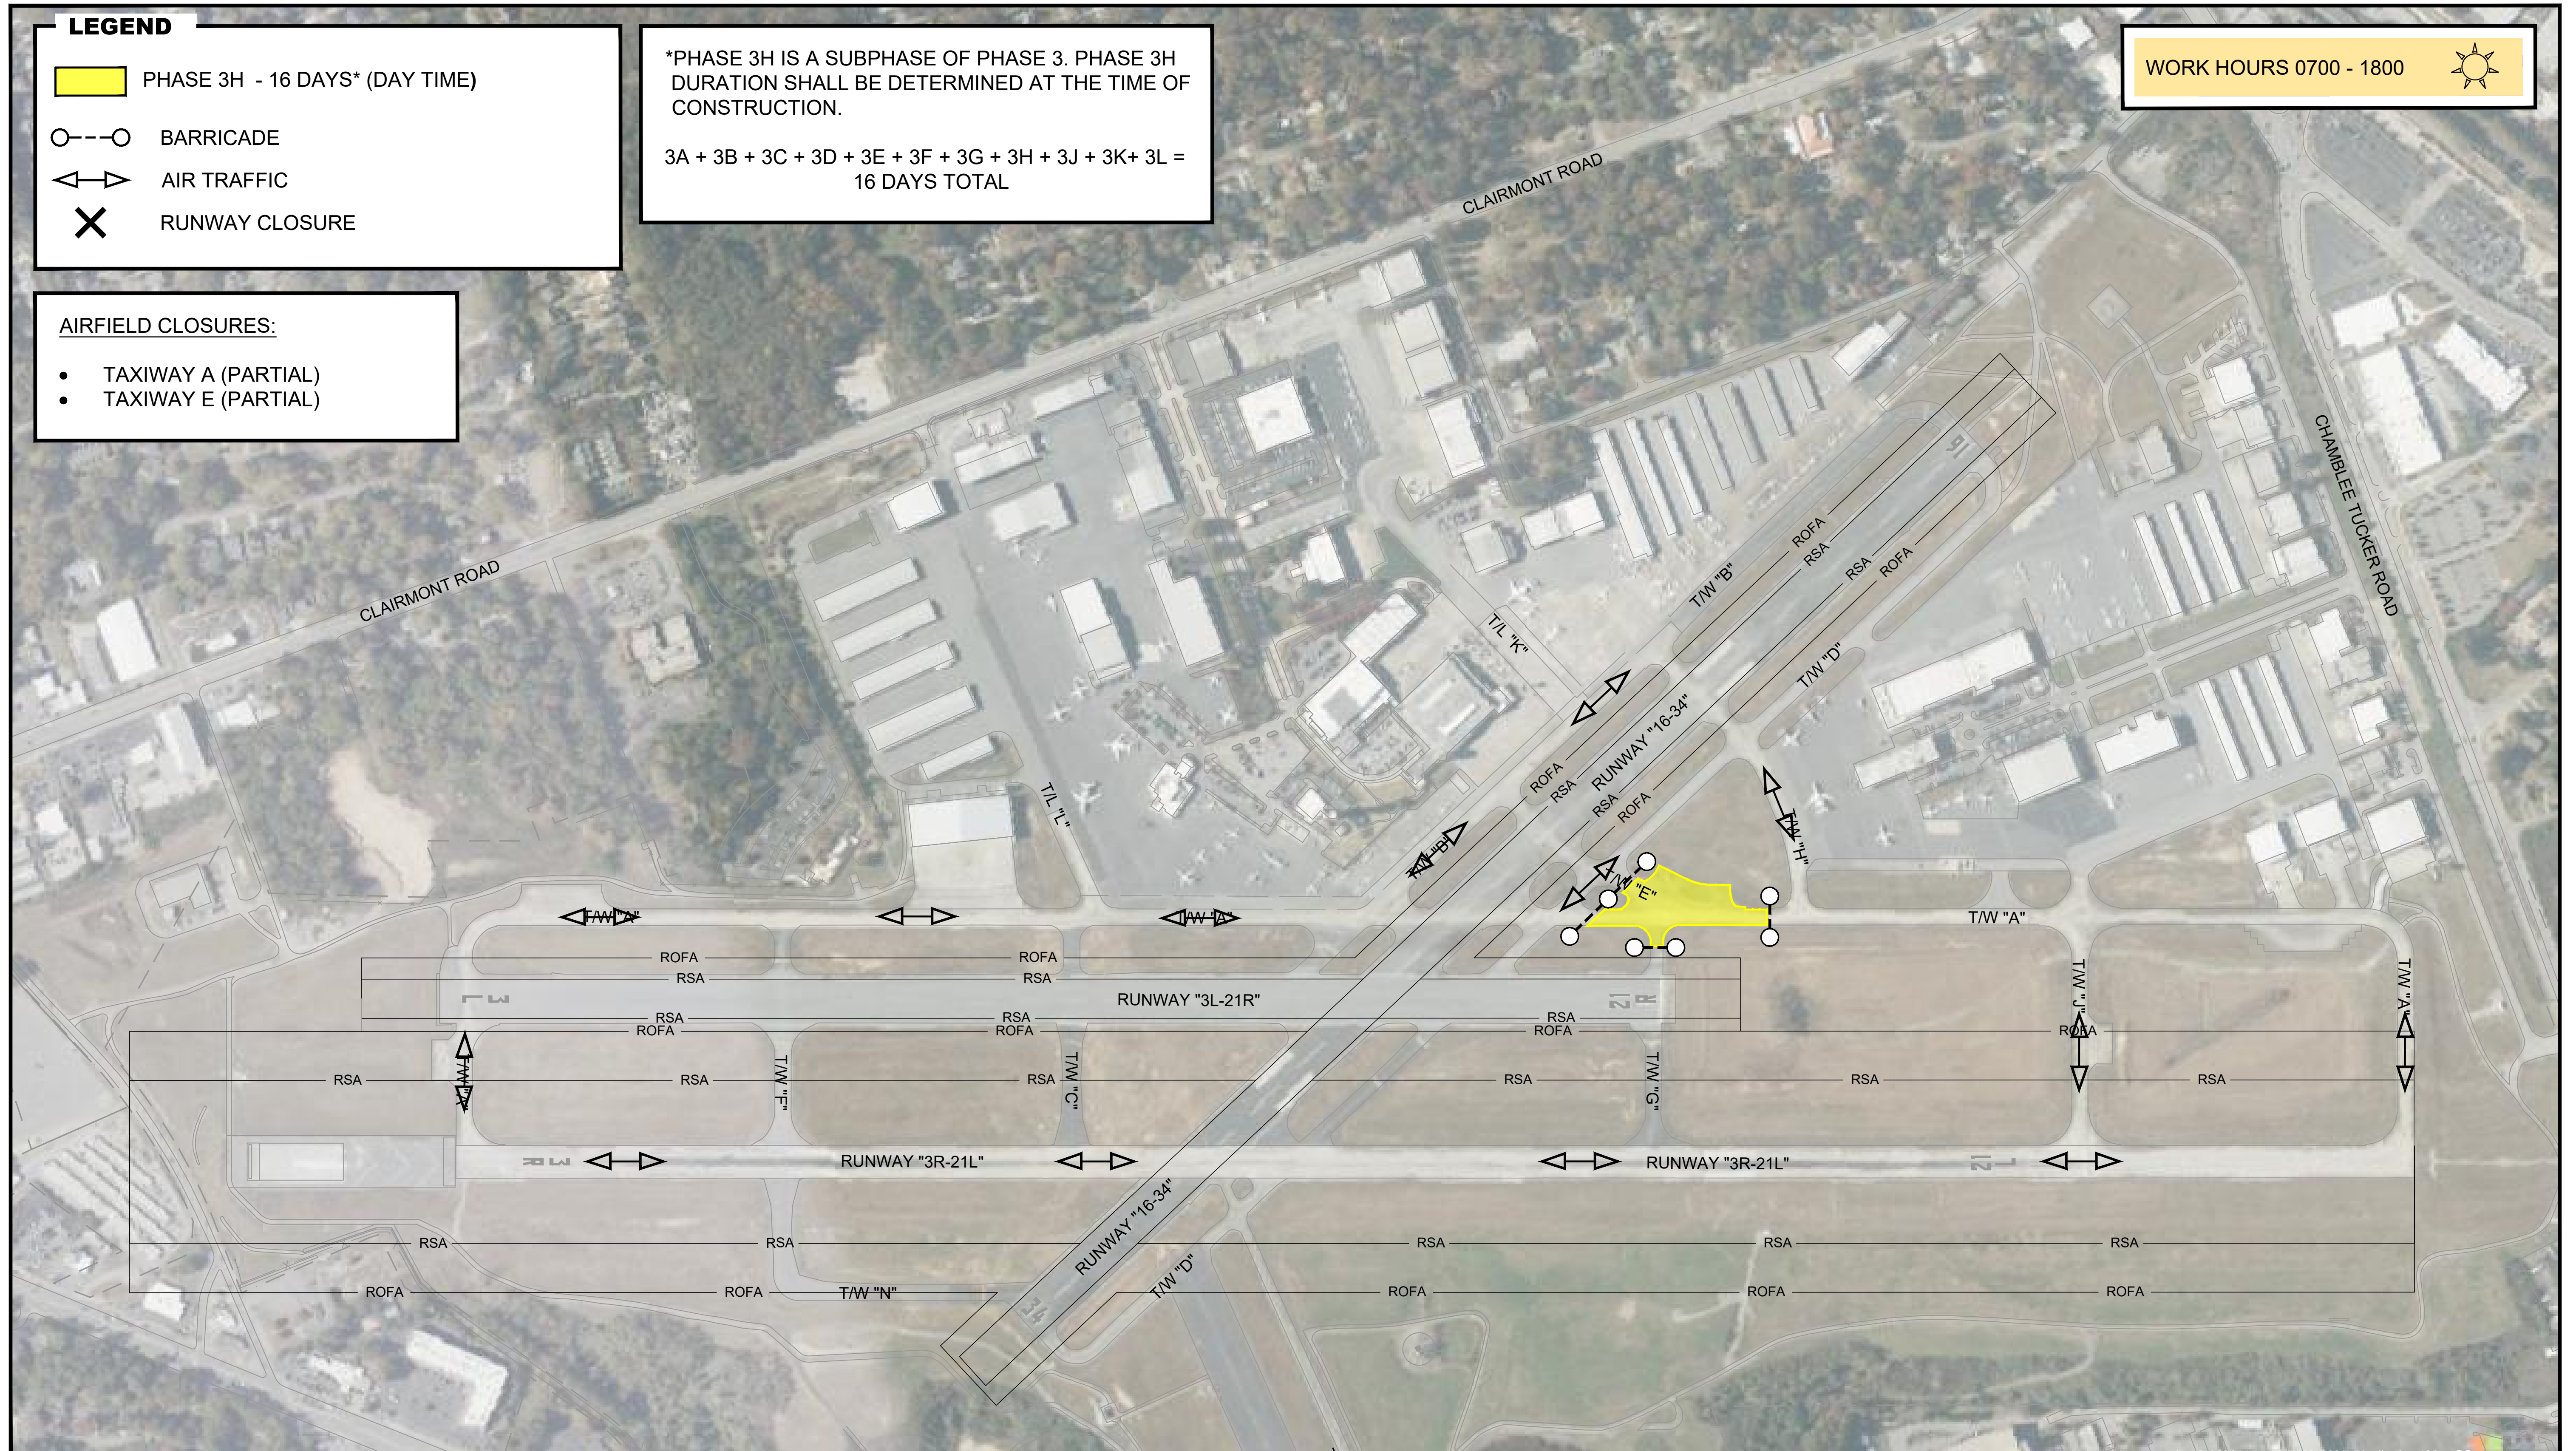

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3H


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3J - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY A (PARTIAL)
- TAXIWAY D (PARTIAL)
- TAXIWAY E (PARTIAL)


*PHASE 3J IS A SUBPHASE OF PHASE 3. PHASE 3J DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800

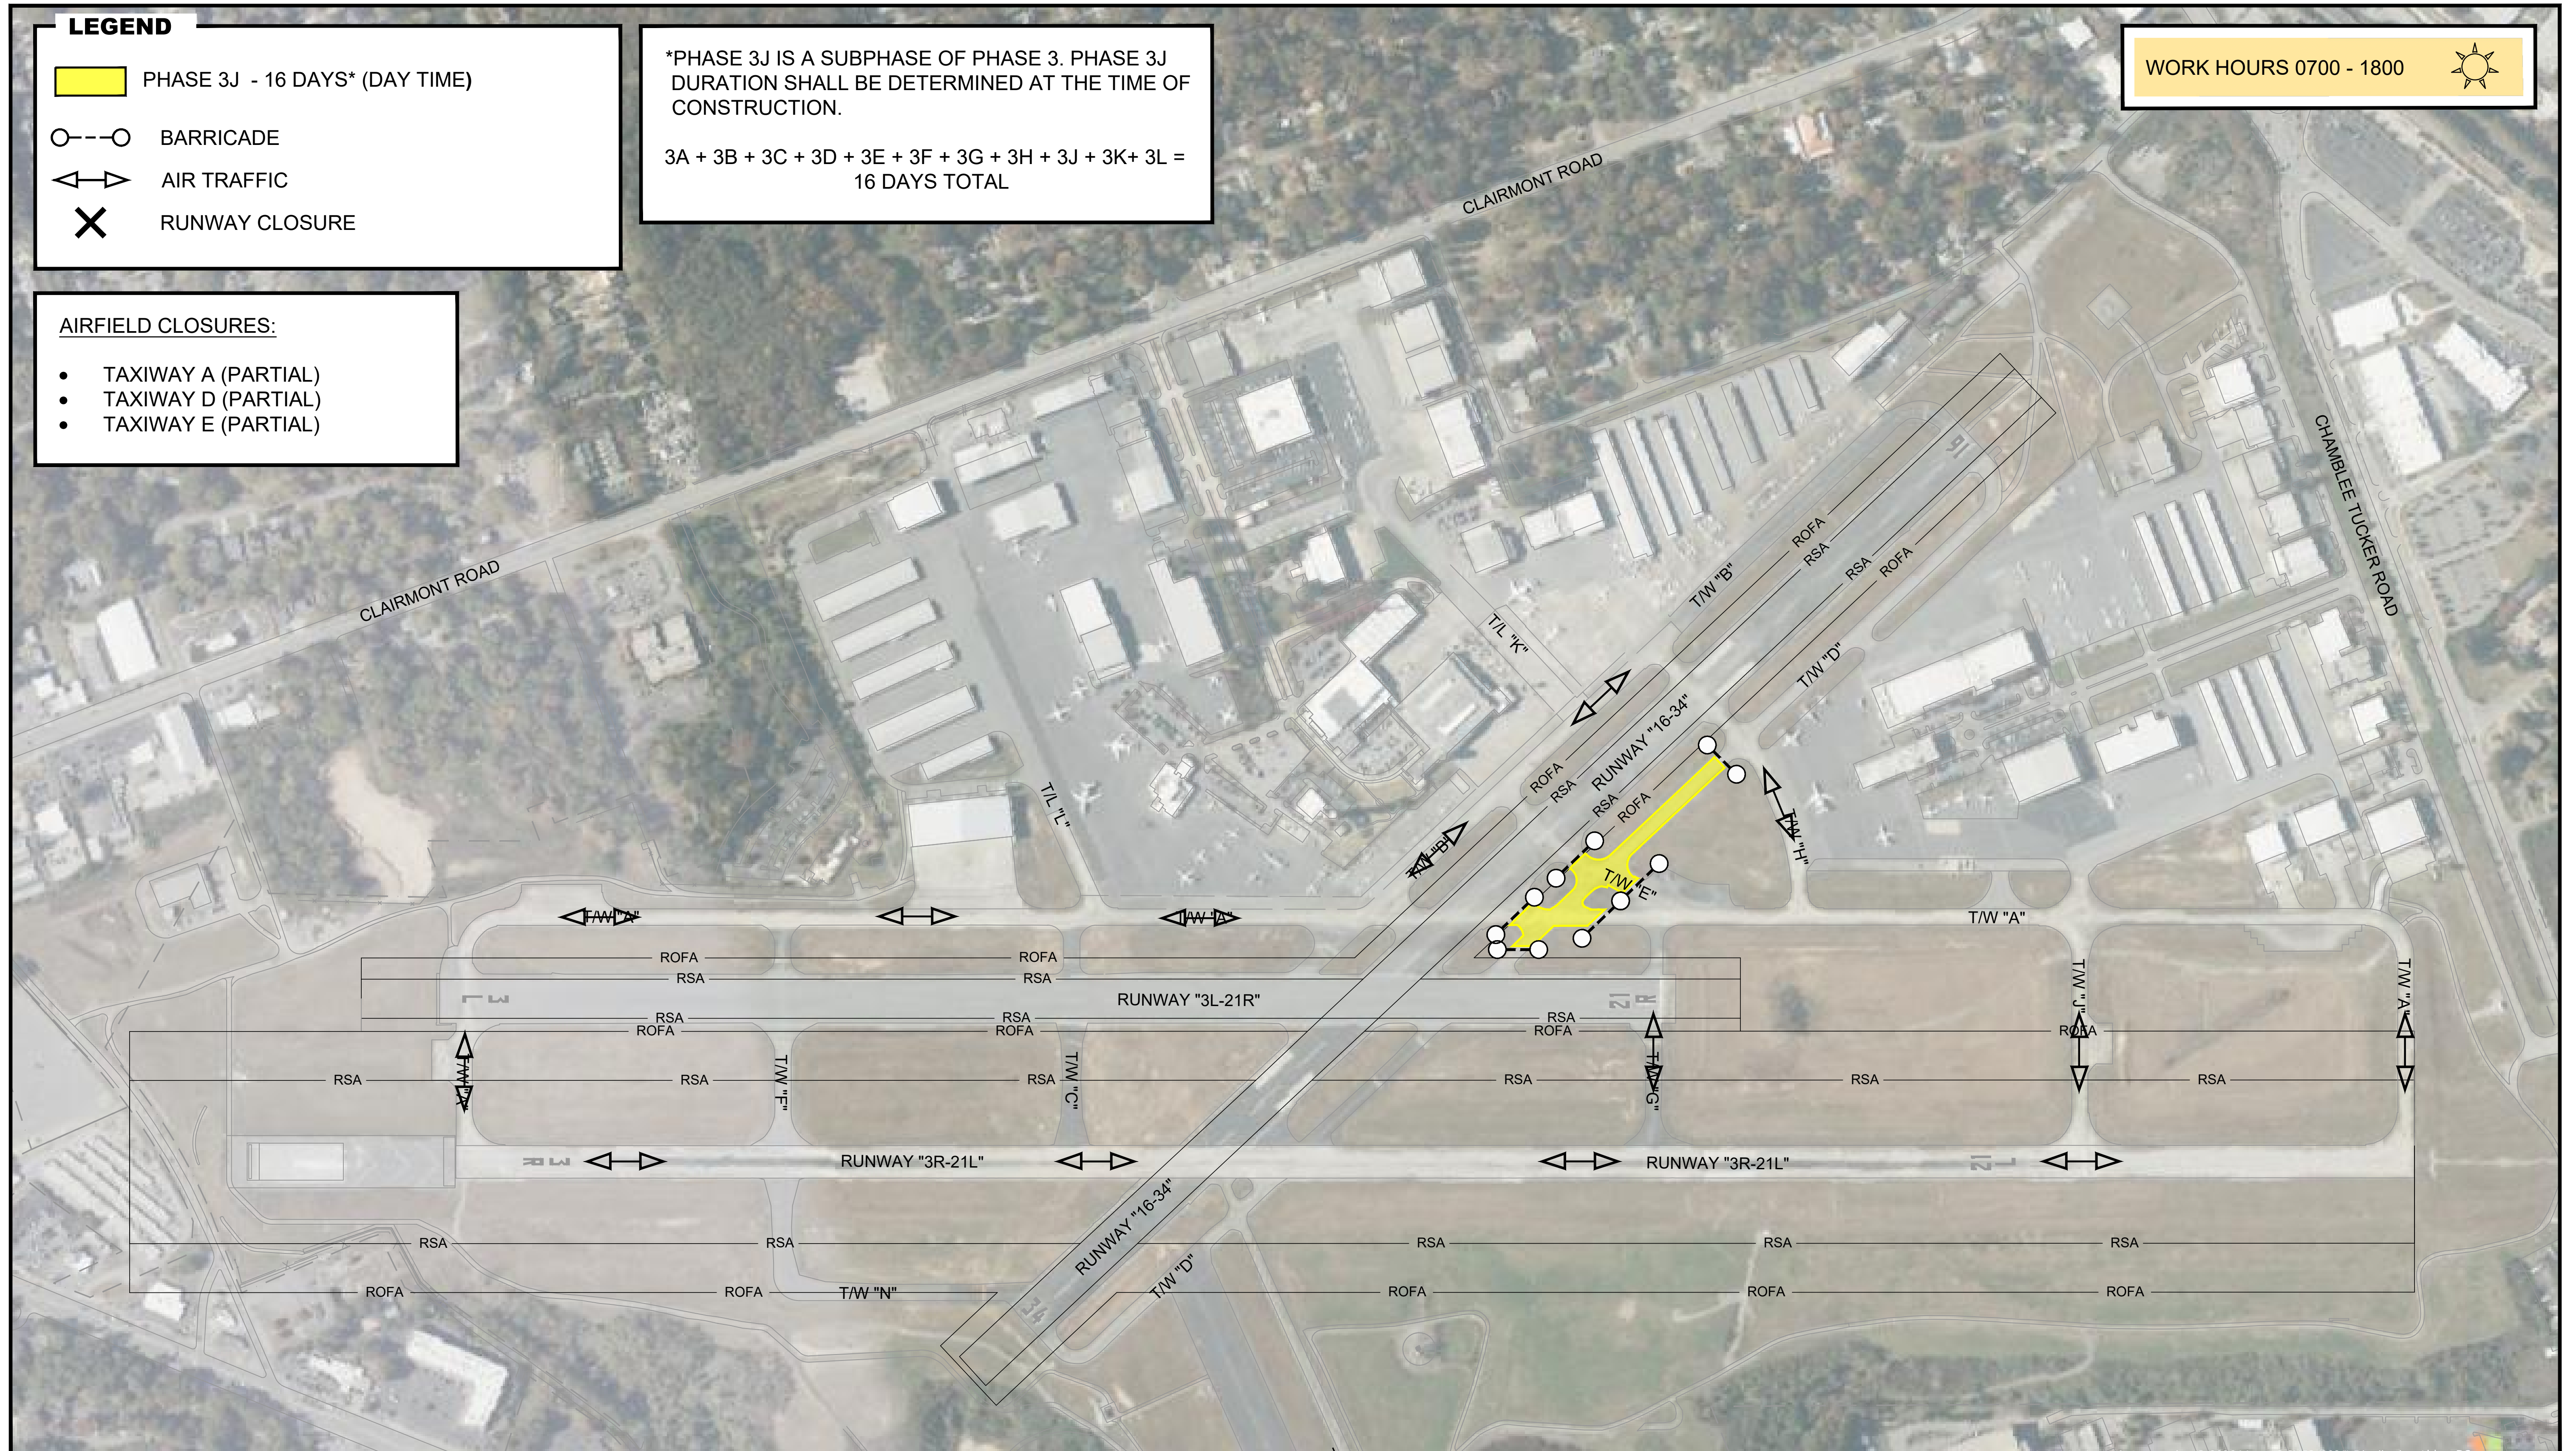

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3J


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 1:59pm

LEGEND

 PHASE 3K - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY D (PARTIAL)
- TAXIWAY H


*PHASE 3K IS A SUBPHASE OF PHASE 3. PHASE 3K DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L = 16 DAYS TOTAL

WORK HOURS 0700 - 1800

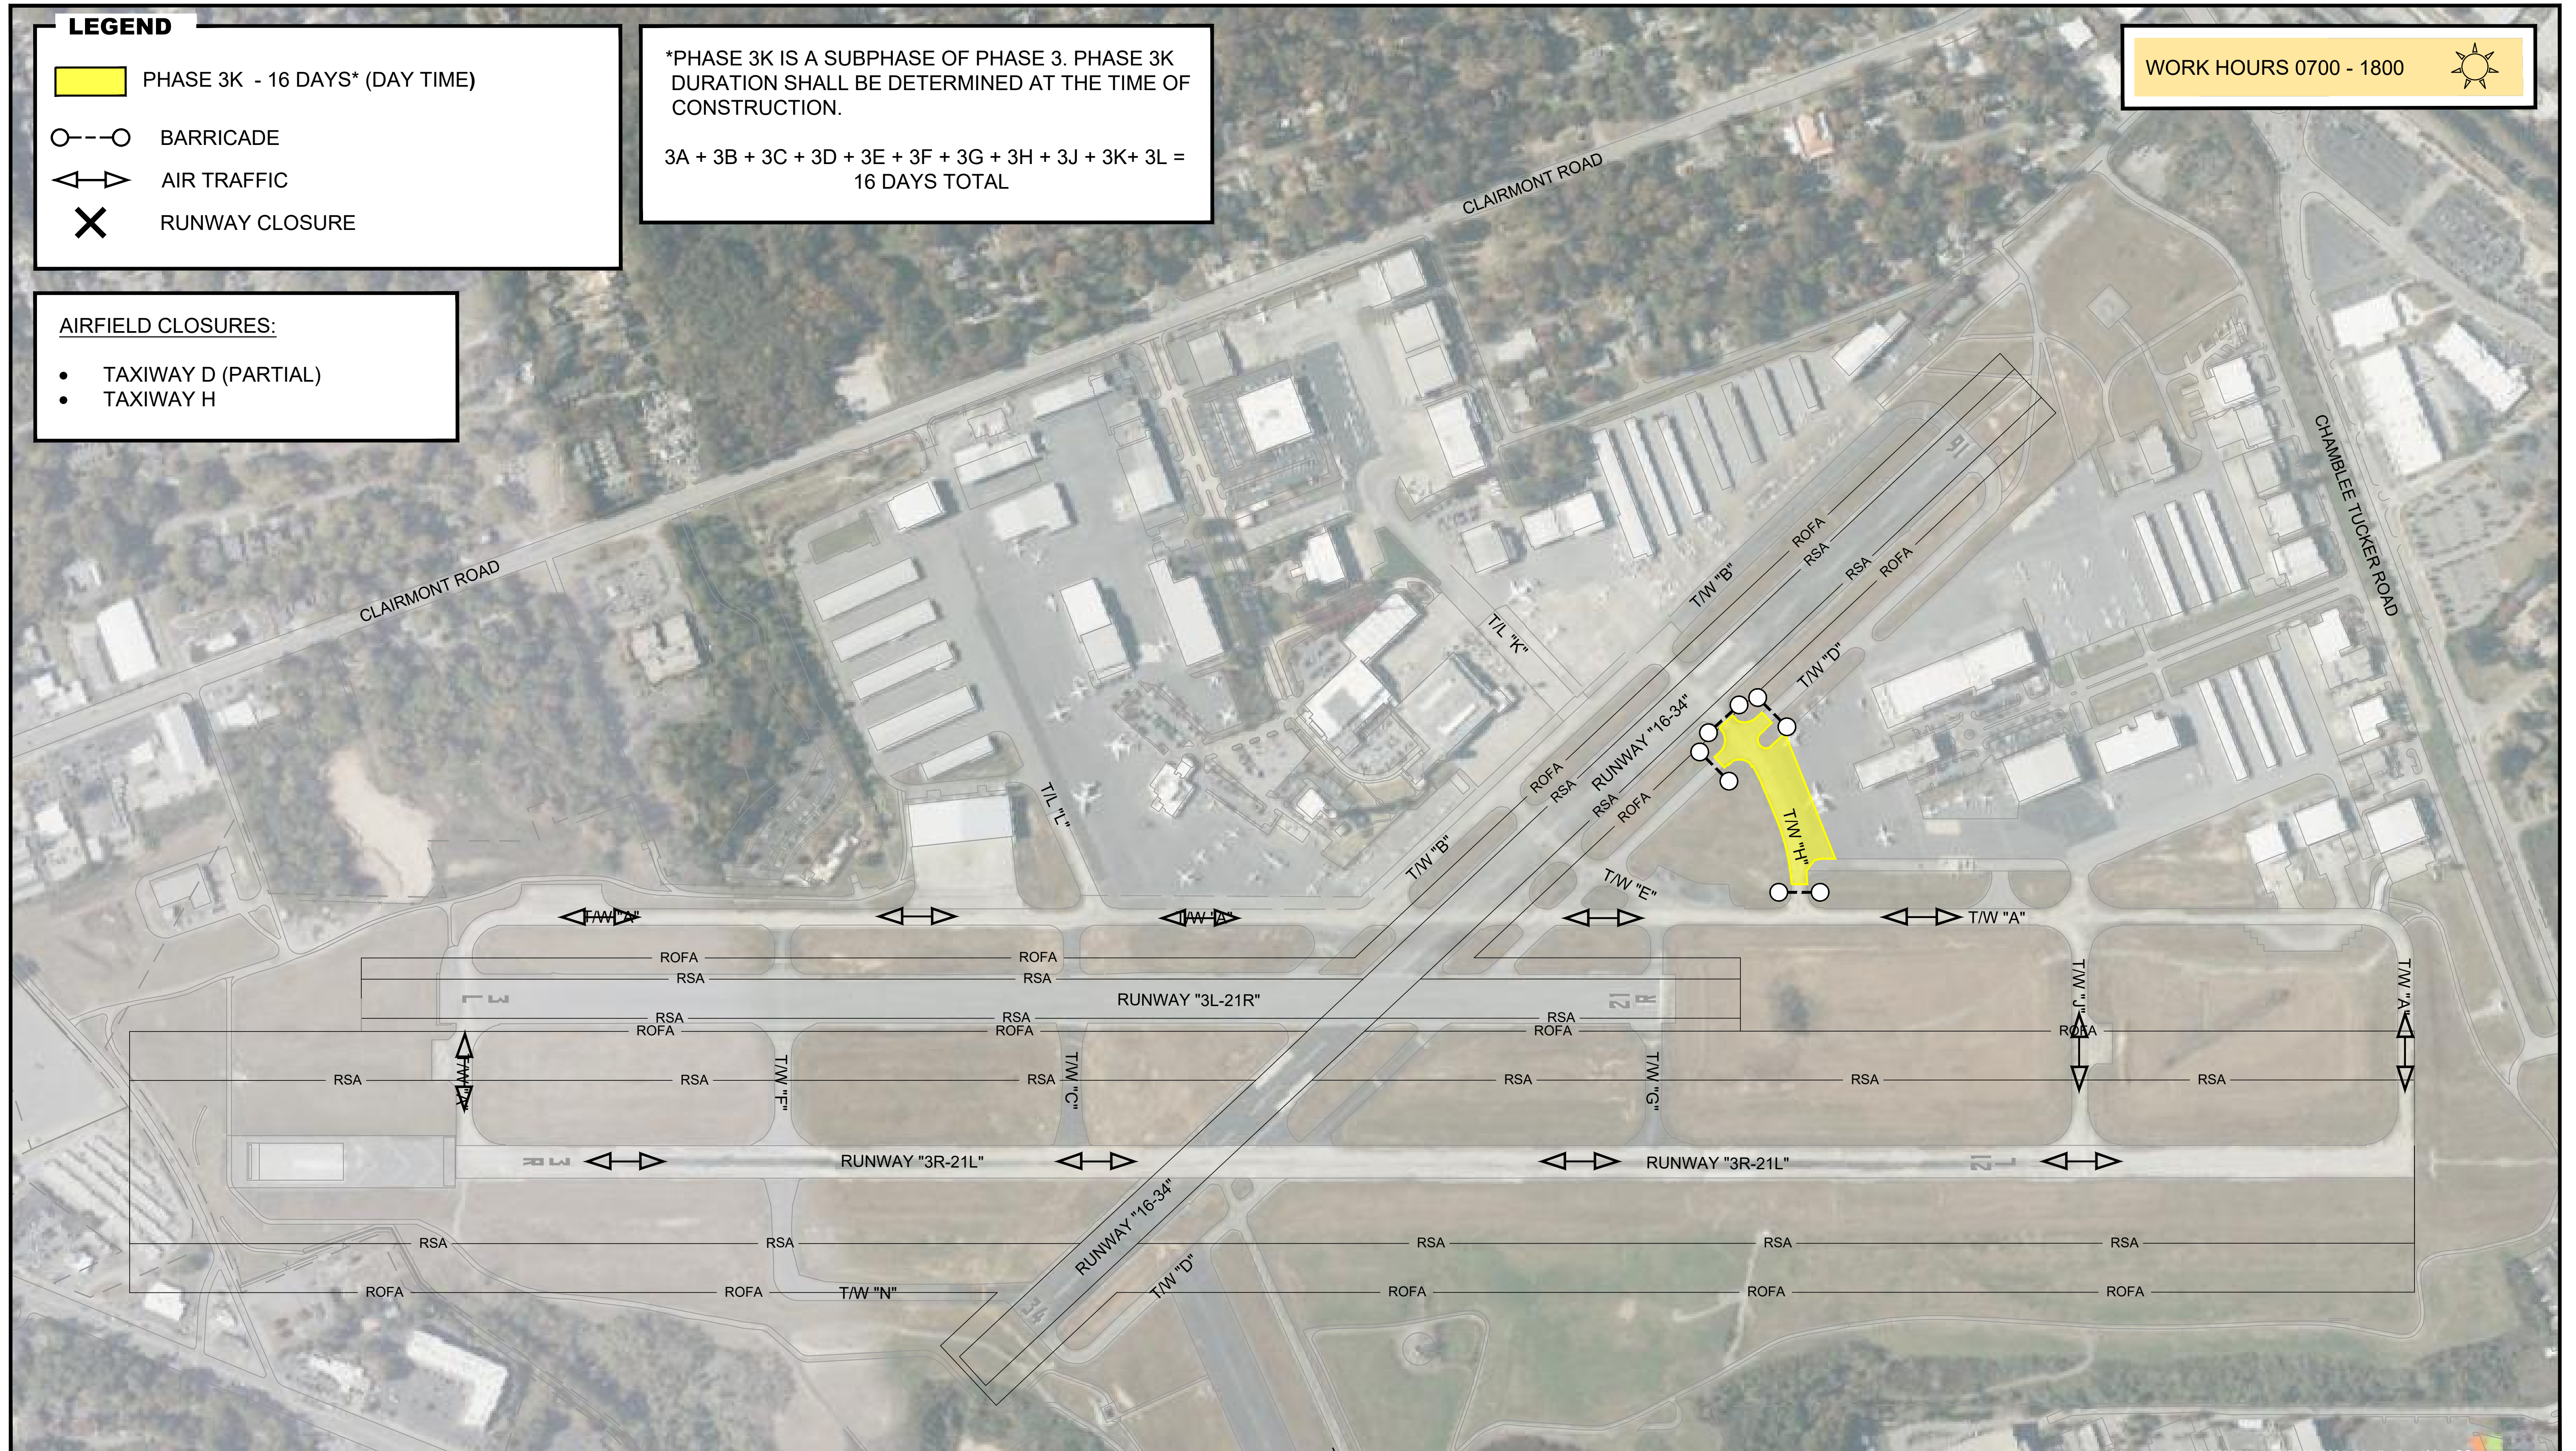

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3K


EXHIBIT
1" = 250'




Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND

 PHASE 3L - 16 DAYS* (DAY TIME)

 BARRICADE

 AIR TRAFFIC

 RUNWAY CLOSURE



AIRFIELD CLOSURES:

- TAXIWAY D (PARTIAL)


*PHASE 3L IS A SUBPHASE OF PHASE 3. PHASE 3L DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

3A + 3B + 3C + 3D + 3E + 3F + 3G + 3H + 3J + 3K + 3L =
16 DAYS TOTAL

WORK HOURS 0700 - 1800

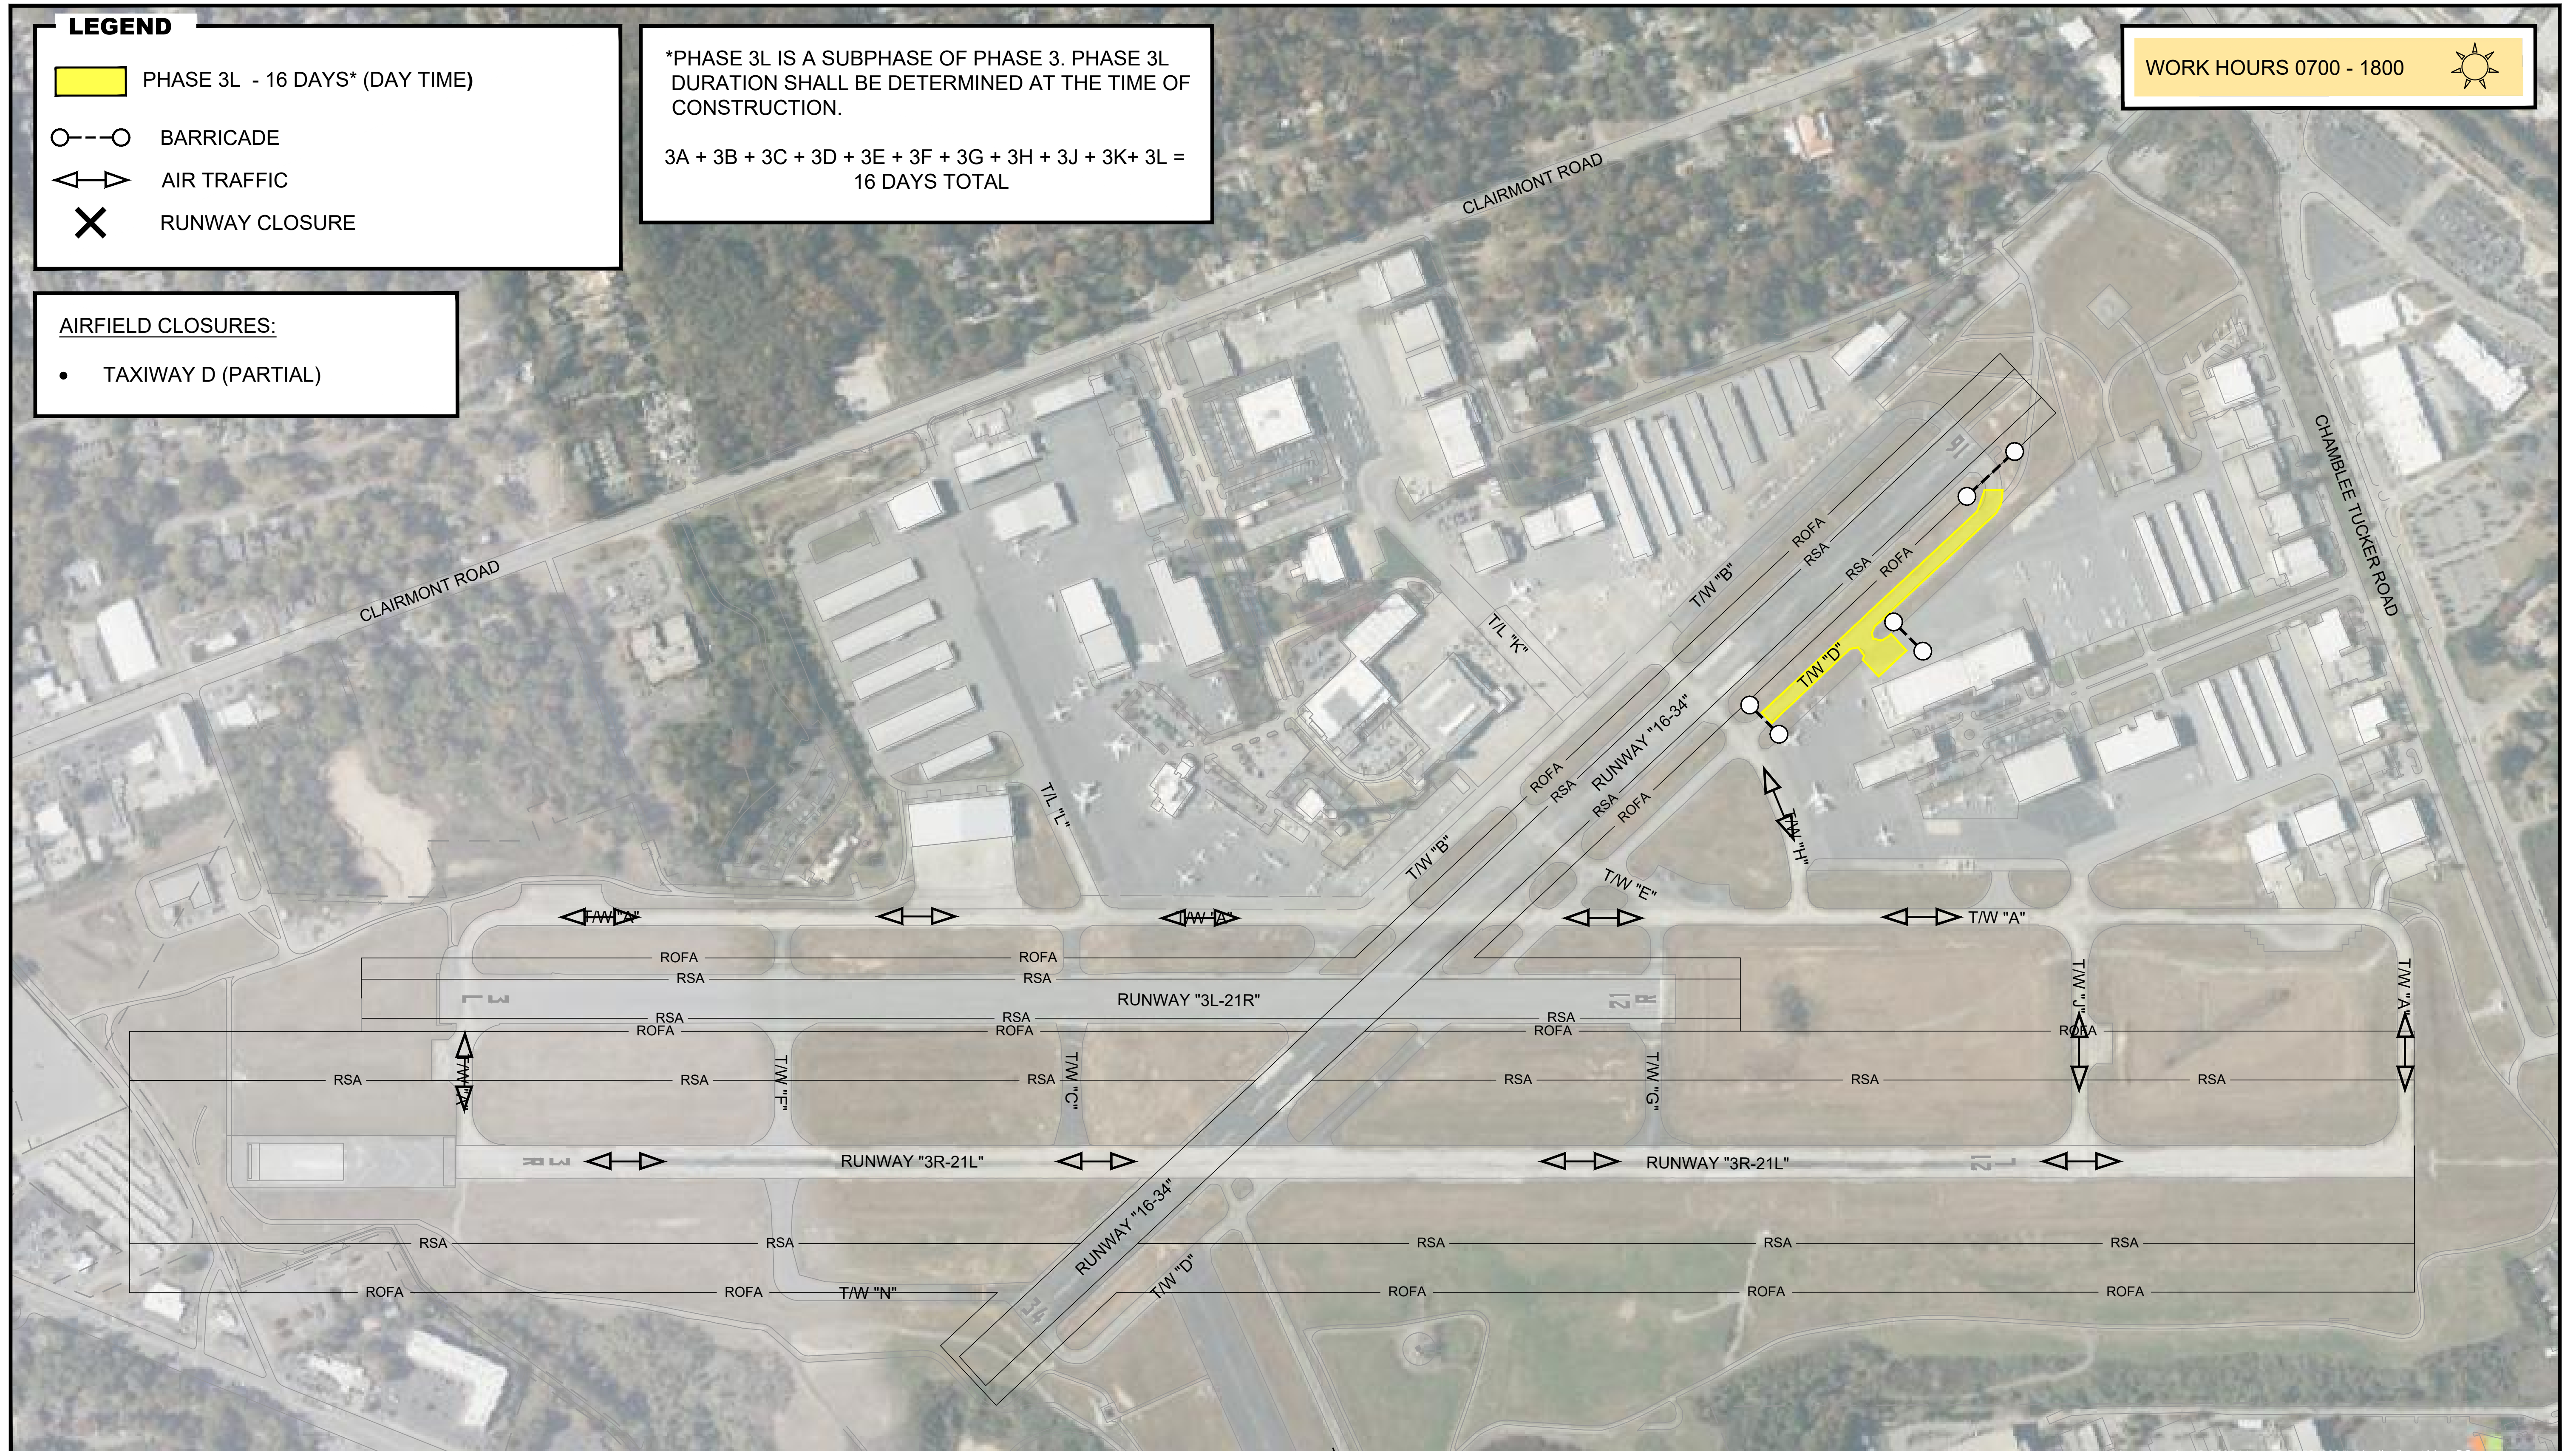

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 3L

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND

- PHASE 4A - 10 DAYS* (24 HR/DAY)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE


AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- TAXIWAY C
- TAXIWAY F


*PHASE 4A IS A SUBPHASE OF PHASE 4. PHASE 4A DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

$$4A + 4B + 4C = 10 \text{ DAYS TOTAL}$$

WORK HOURS 24 HR/DAY

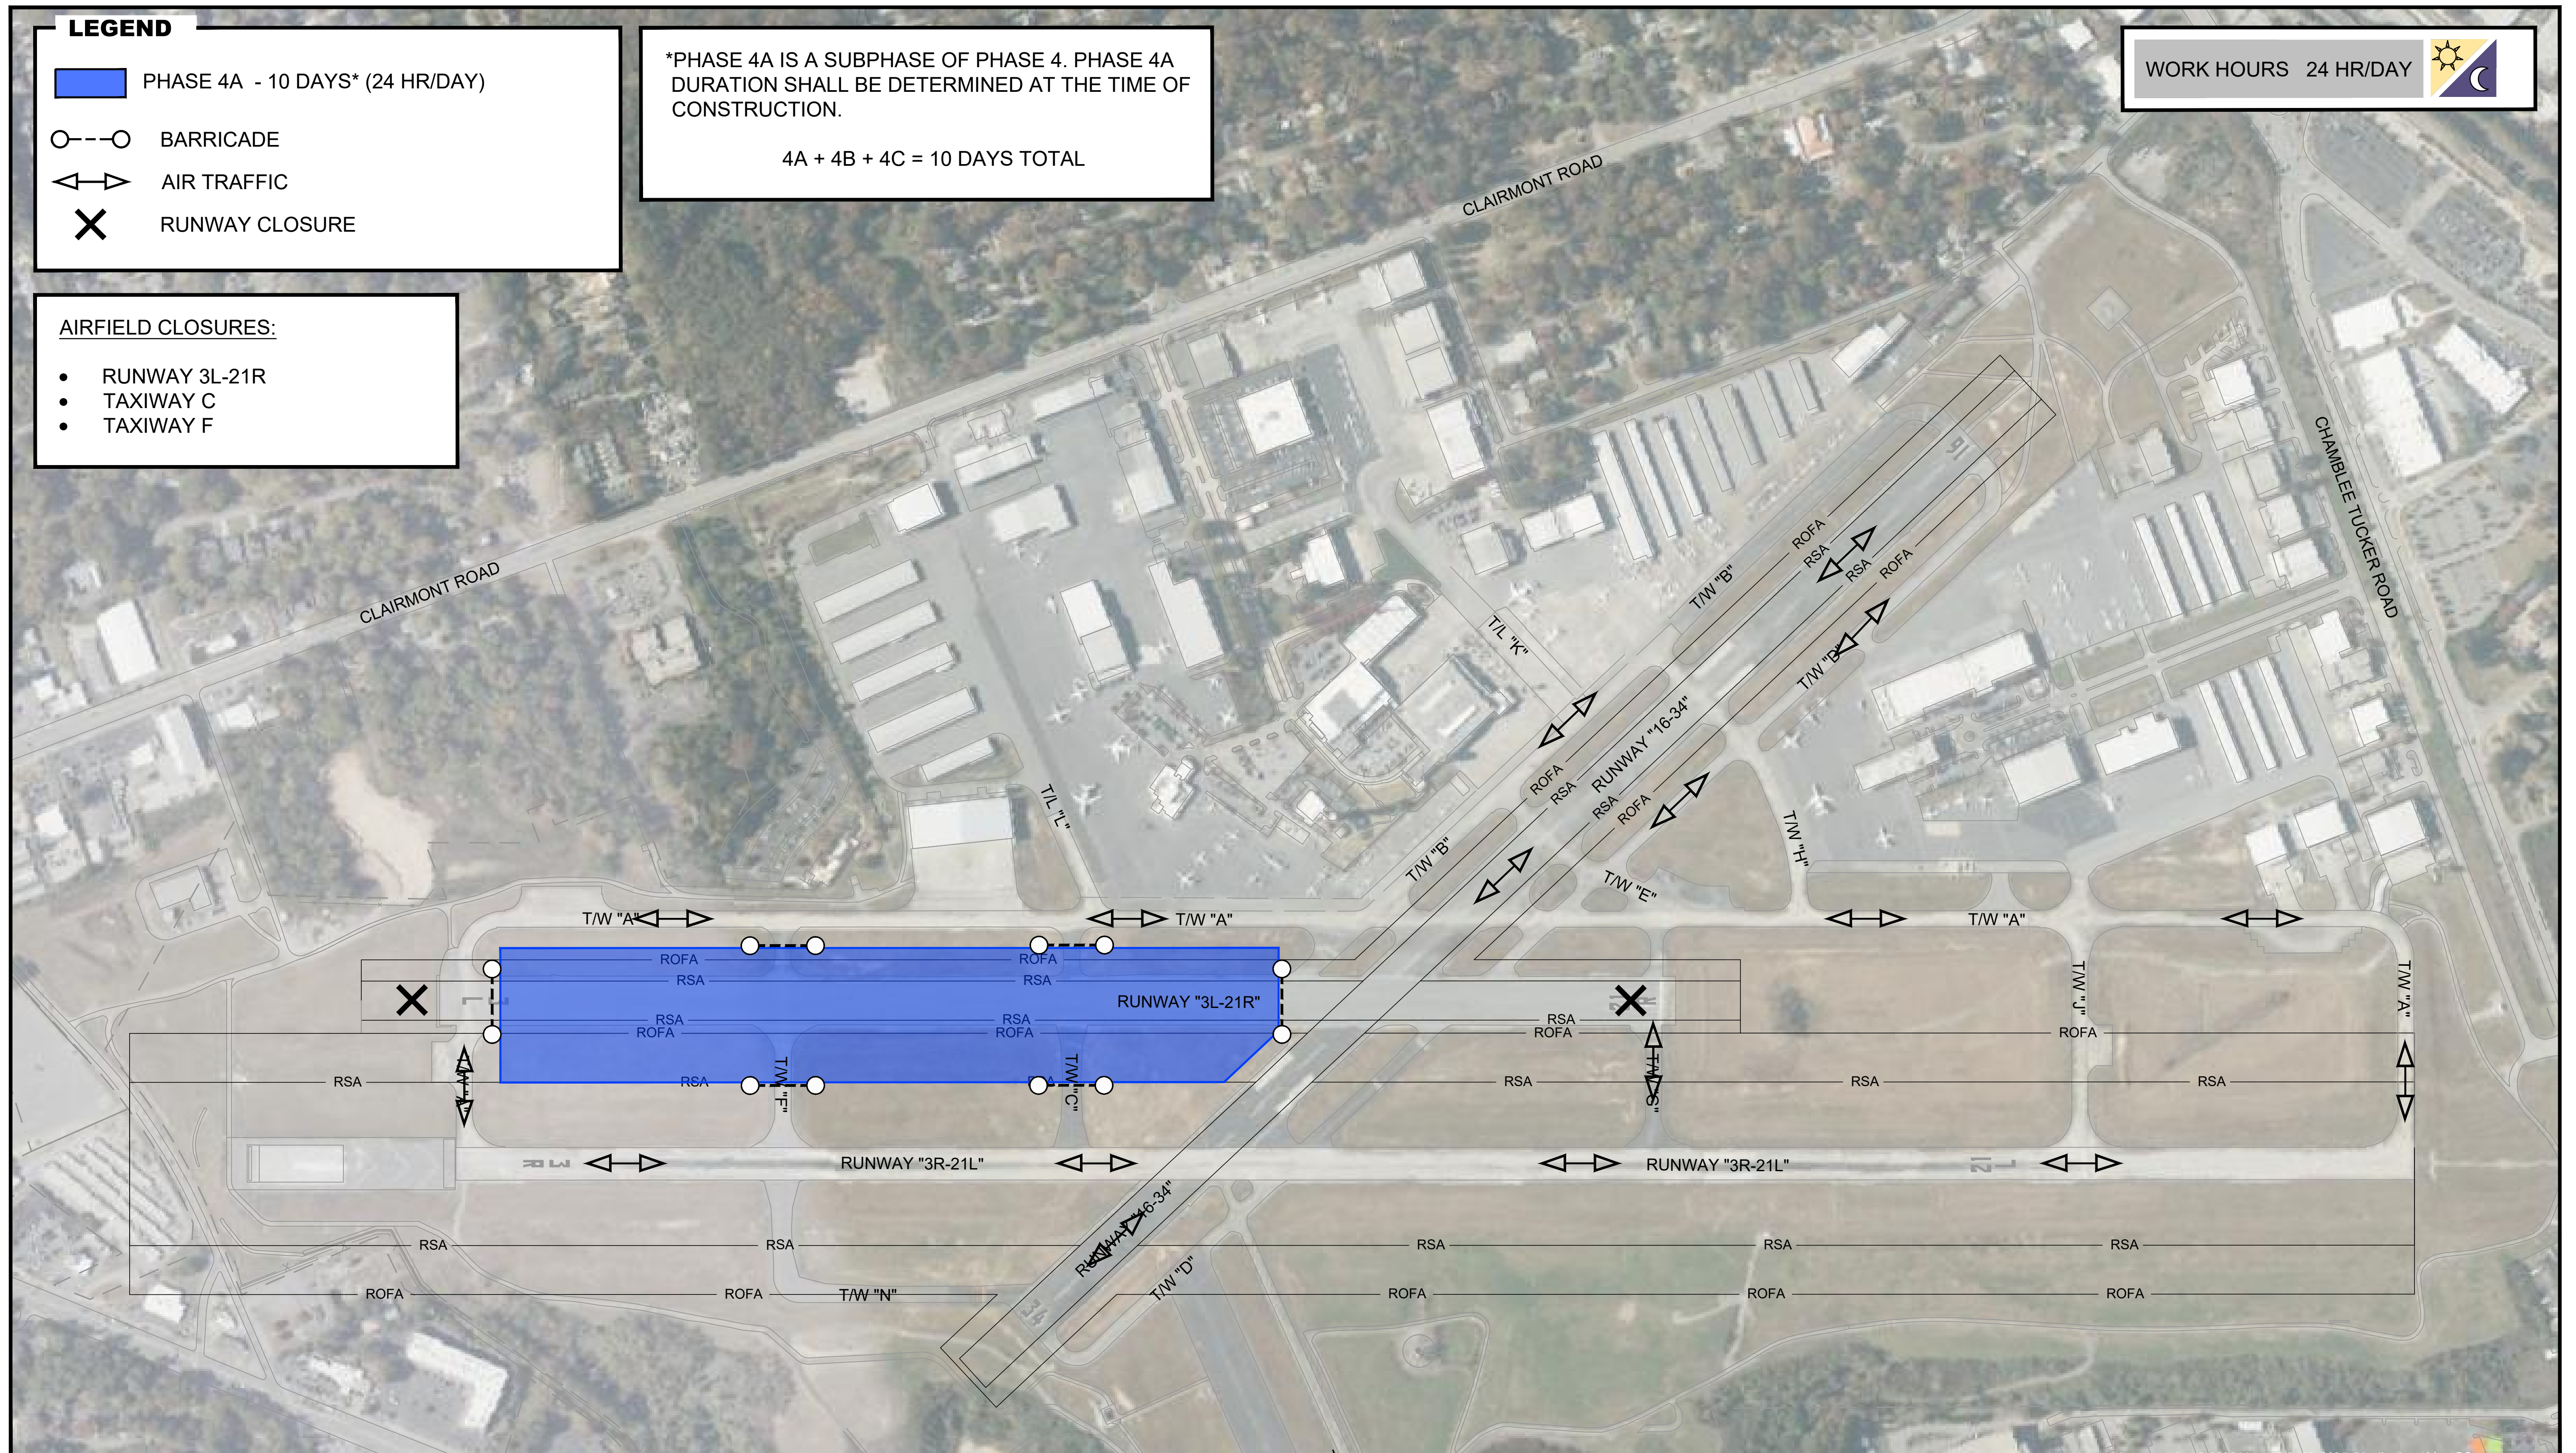

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 4A

EXHIBIT
1" = 250'



Y:\Airports\PD\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND

- PHASE 4B - 10 DAYS* (24 HR/DAY)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE


AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- RUNWAY 16-34
- TAXIWAY D (PARTIAL)
- TAXIWAY G


*PHASE 4B IS A SUBPHASE OF PHASE 4. PHASE 4B DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

$$4A + 4B + 4C = 10 \text{ DAYS TOTAL}$$

WORK HOURS 24 HR/DAY

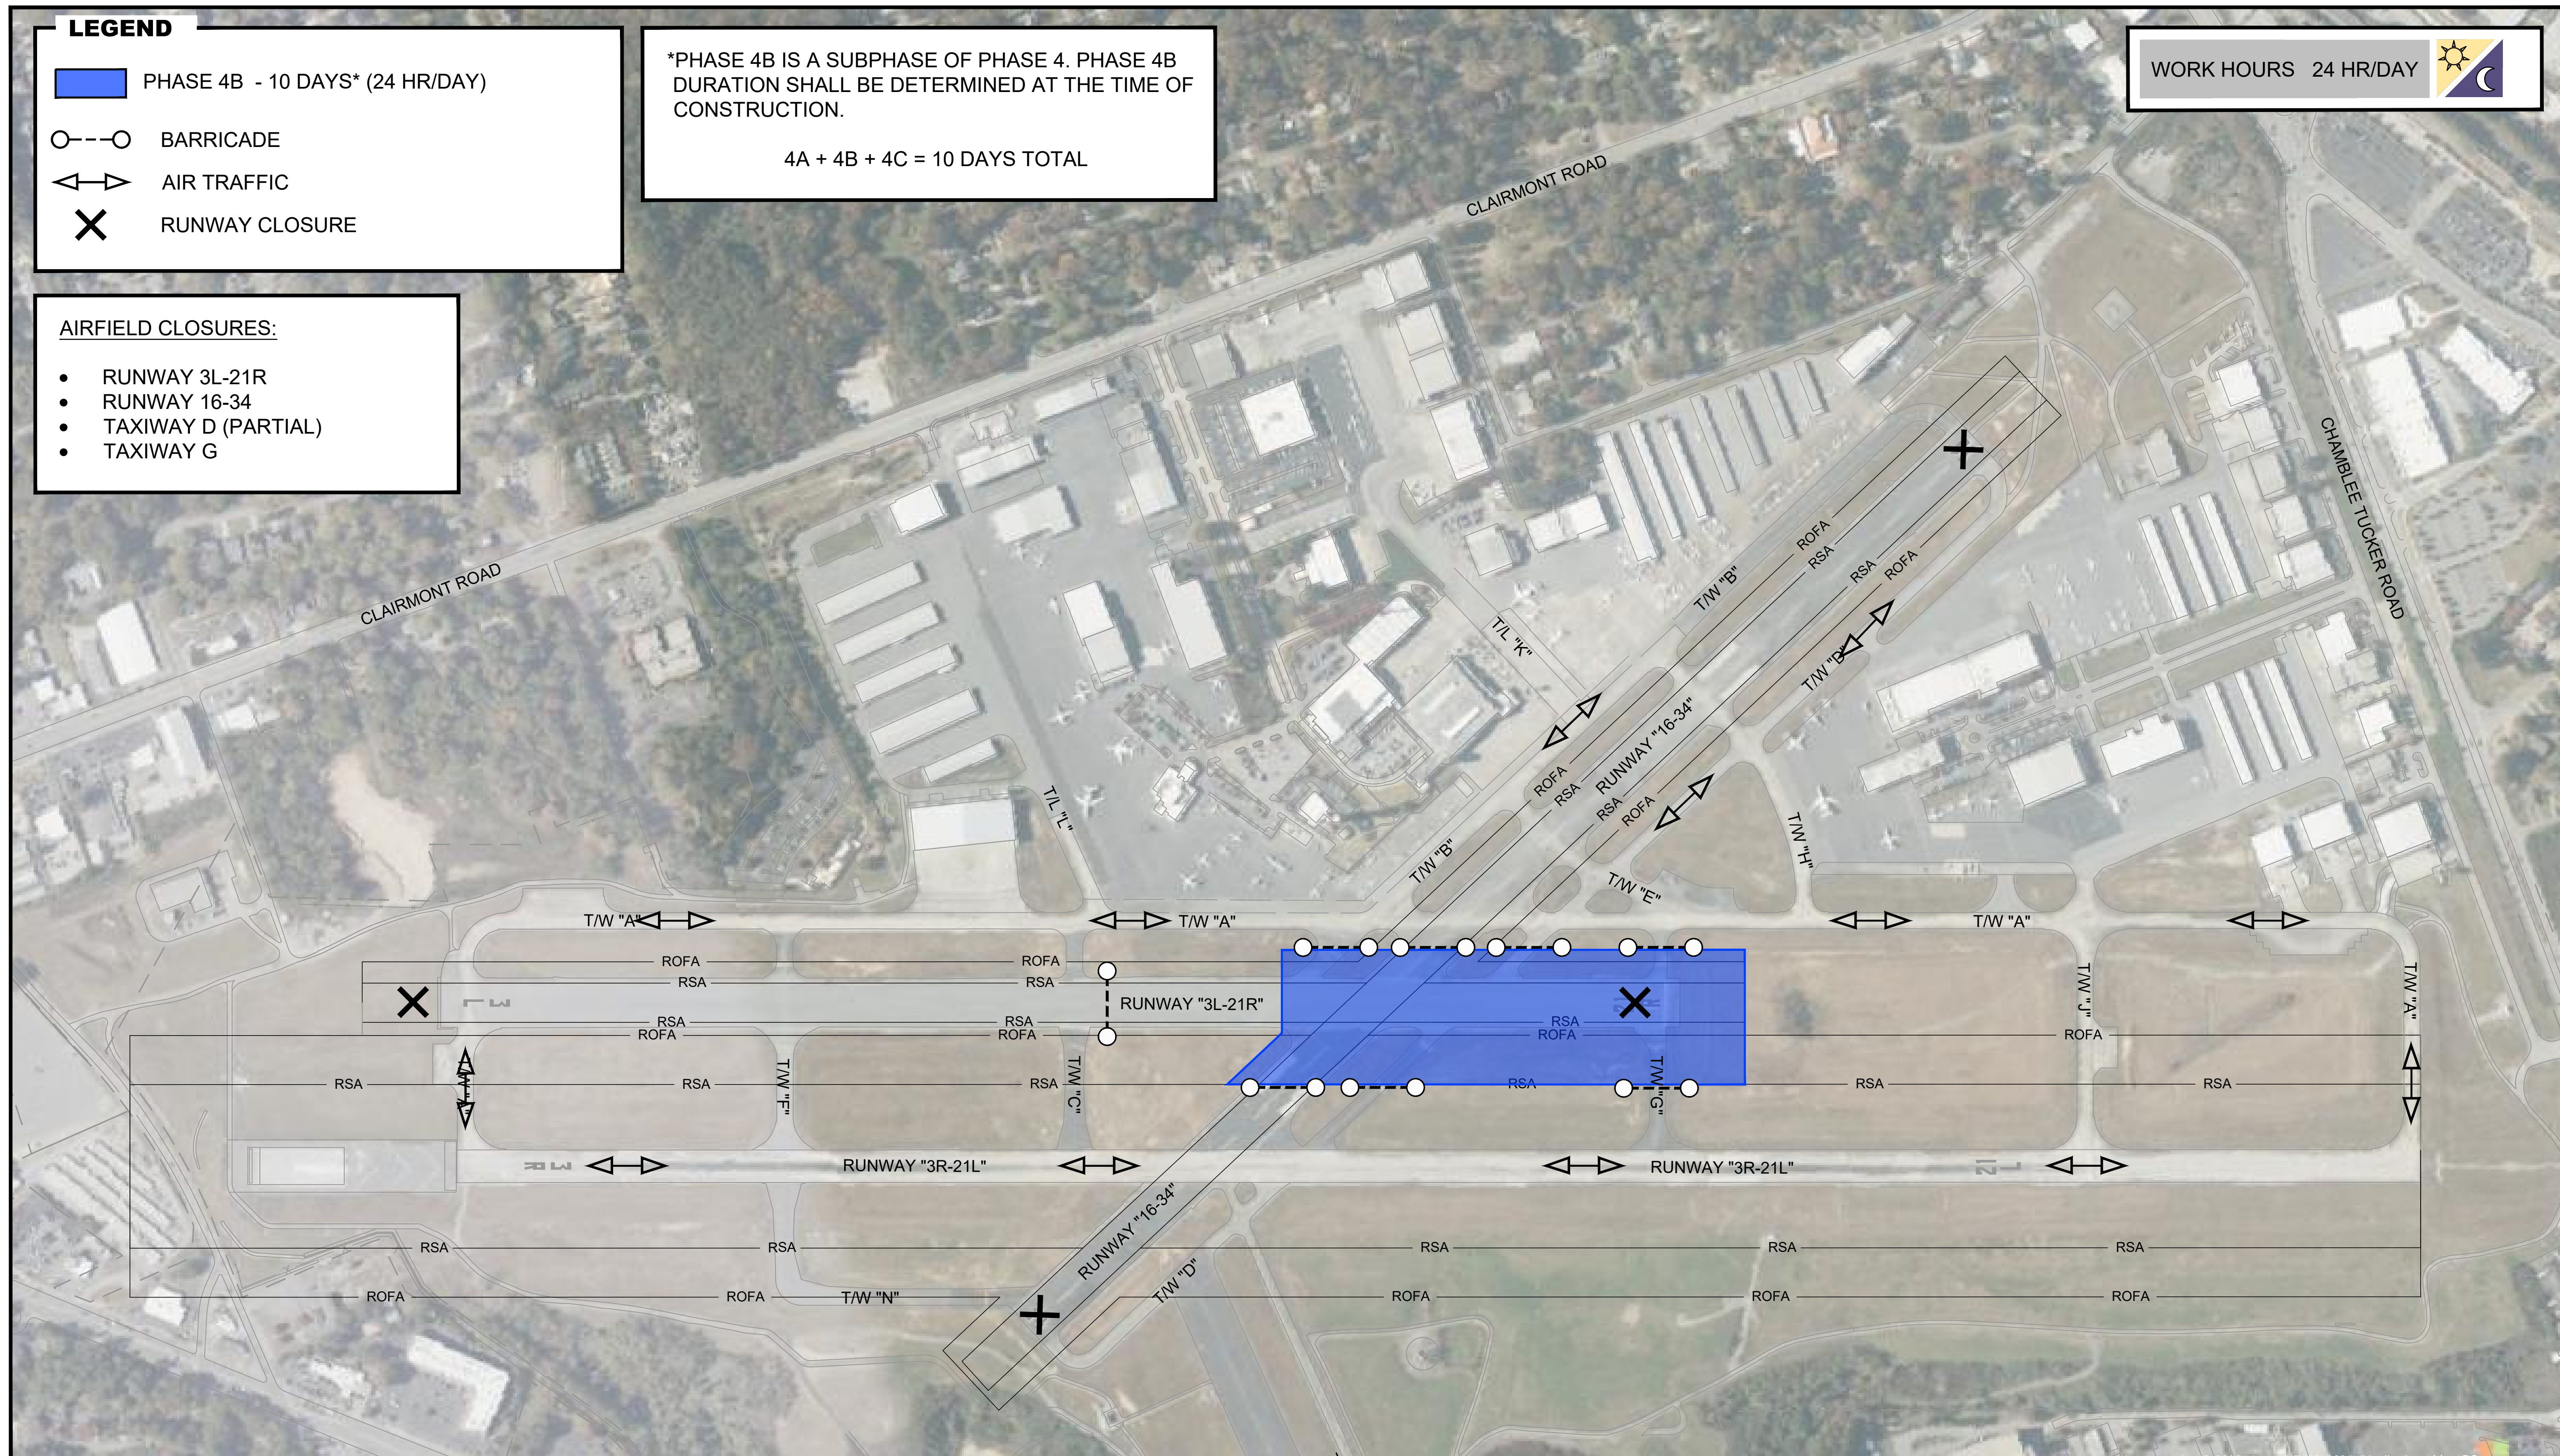

Michael Baker
INTERNATIONAL





DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 4B

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND

-  PHASE 4C - 10 DAYS* (24 HR/DAY)
-  BARRICADE
-  AIR TRAFFIC
-  RUNWAY CLOSURE


AIRFIELD CLOSURES:

- RUNWAY 3L-21R
- TAXIWAY A (PARTIAL)

*PHASE 4C IS A SUBPHASE OF PHASE 4. PHASE 4C DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

$$4A + 4B + 4C = 10 \text{ DAYS TOTAL}$$

WORK HOURS 24 HR/DAY

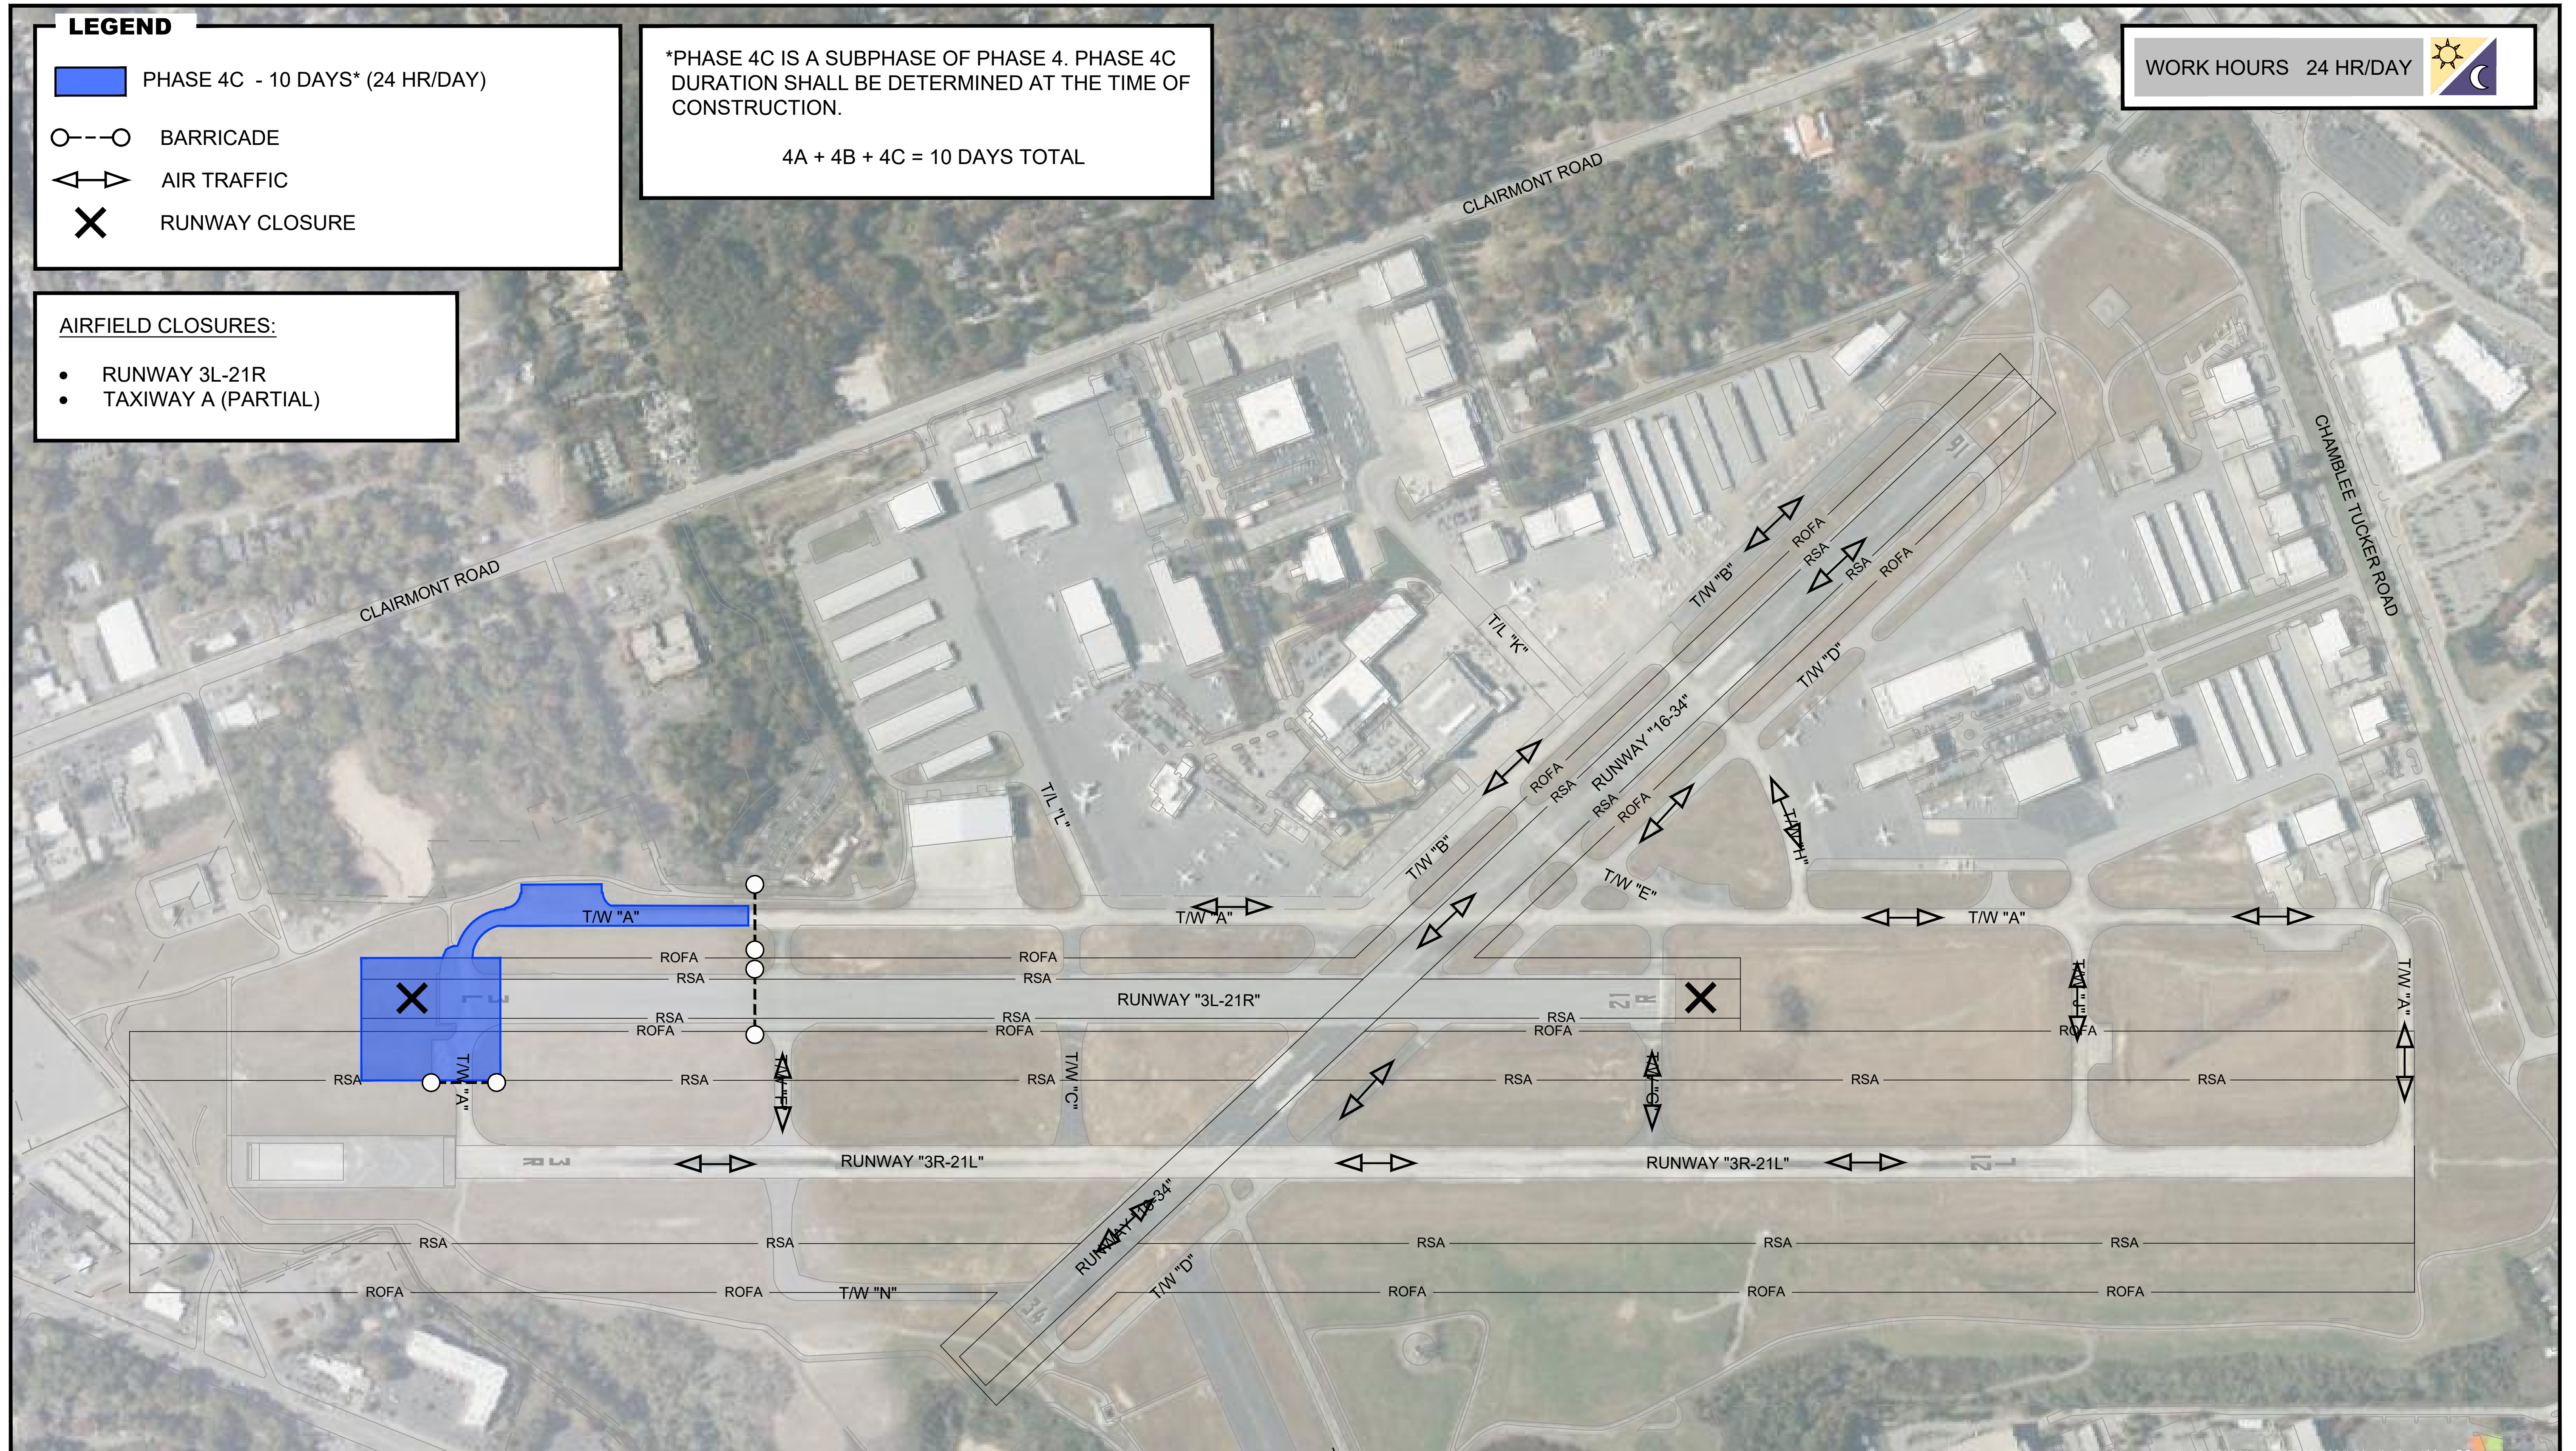

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 4C

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND



PHASE 5 - 5 DAYS (DAY TIME)

- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE


AIRFIELD CLOSURES:

- TRACT 5 APRON

WORK HOURS 0700 - 1800

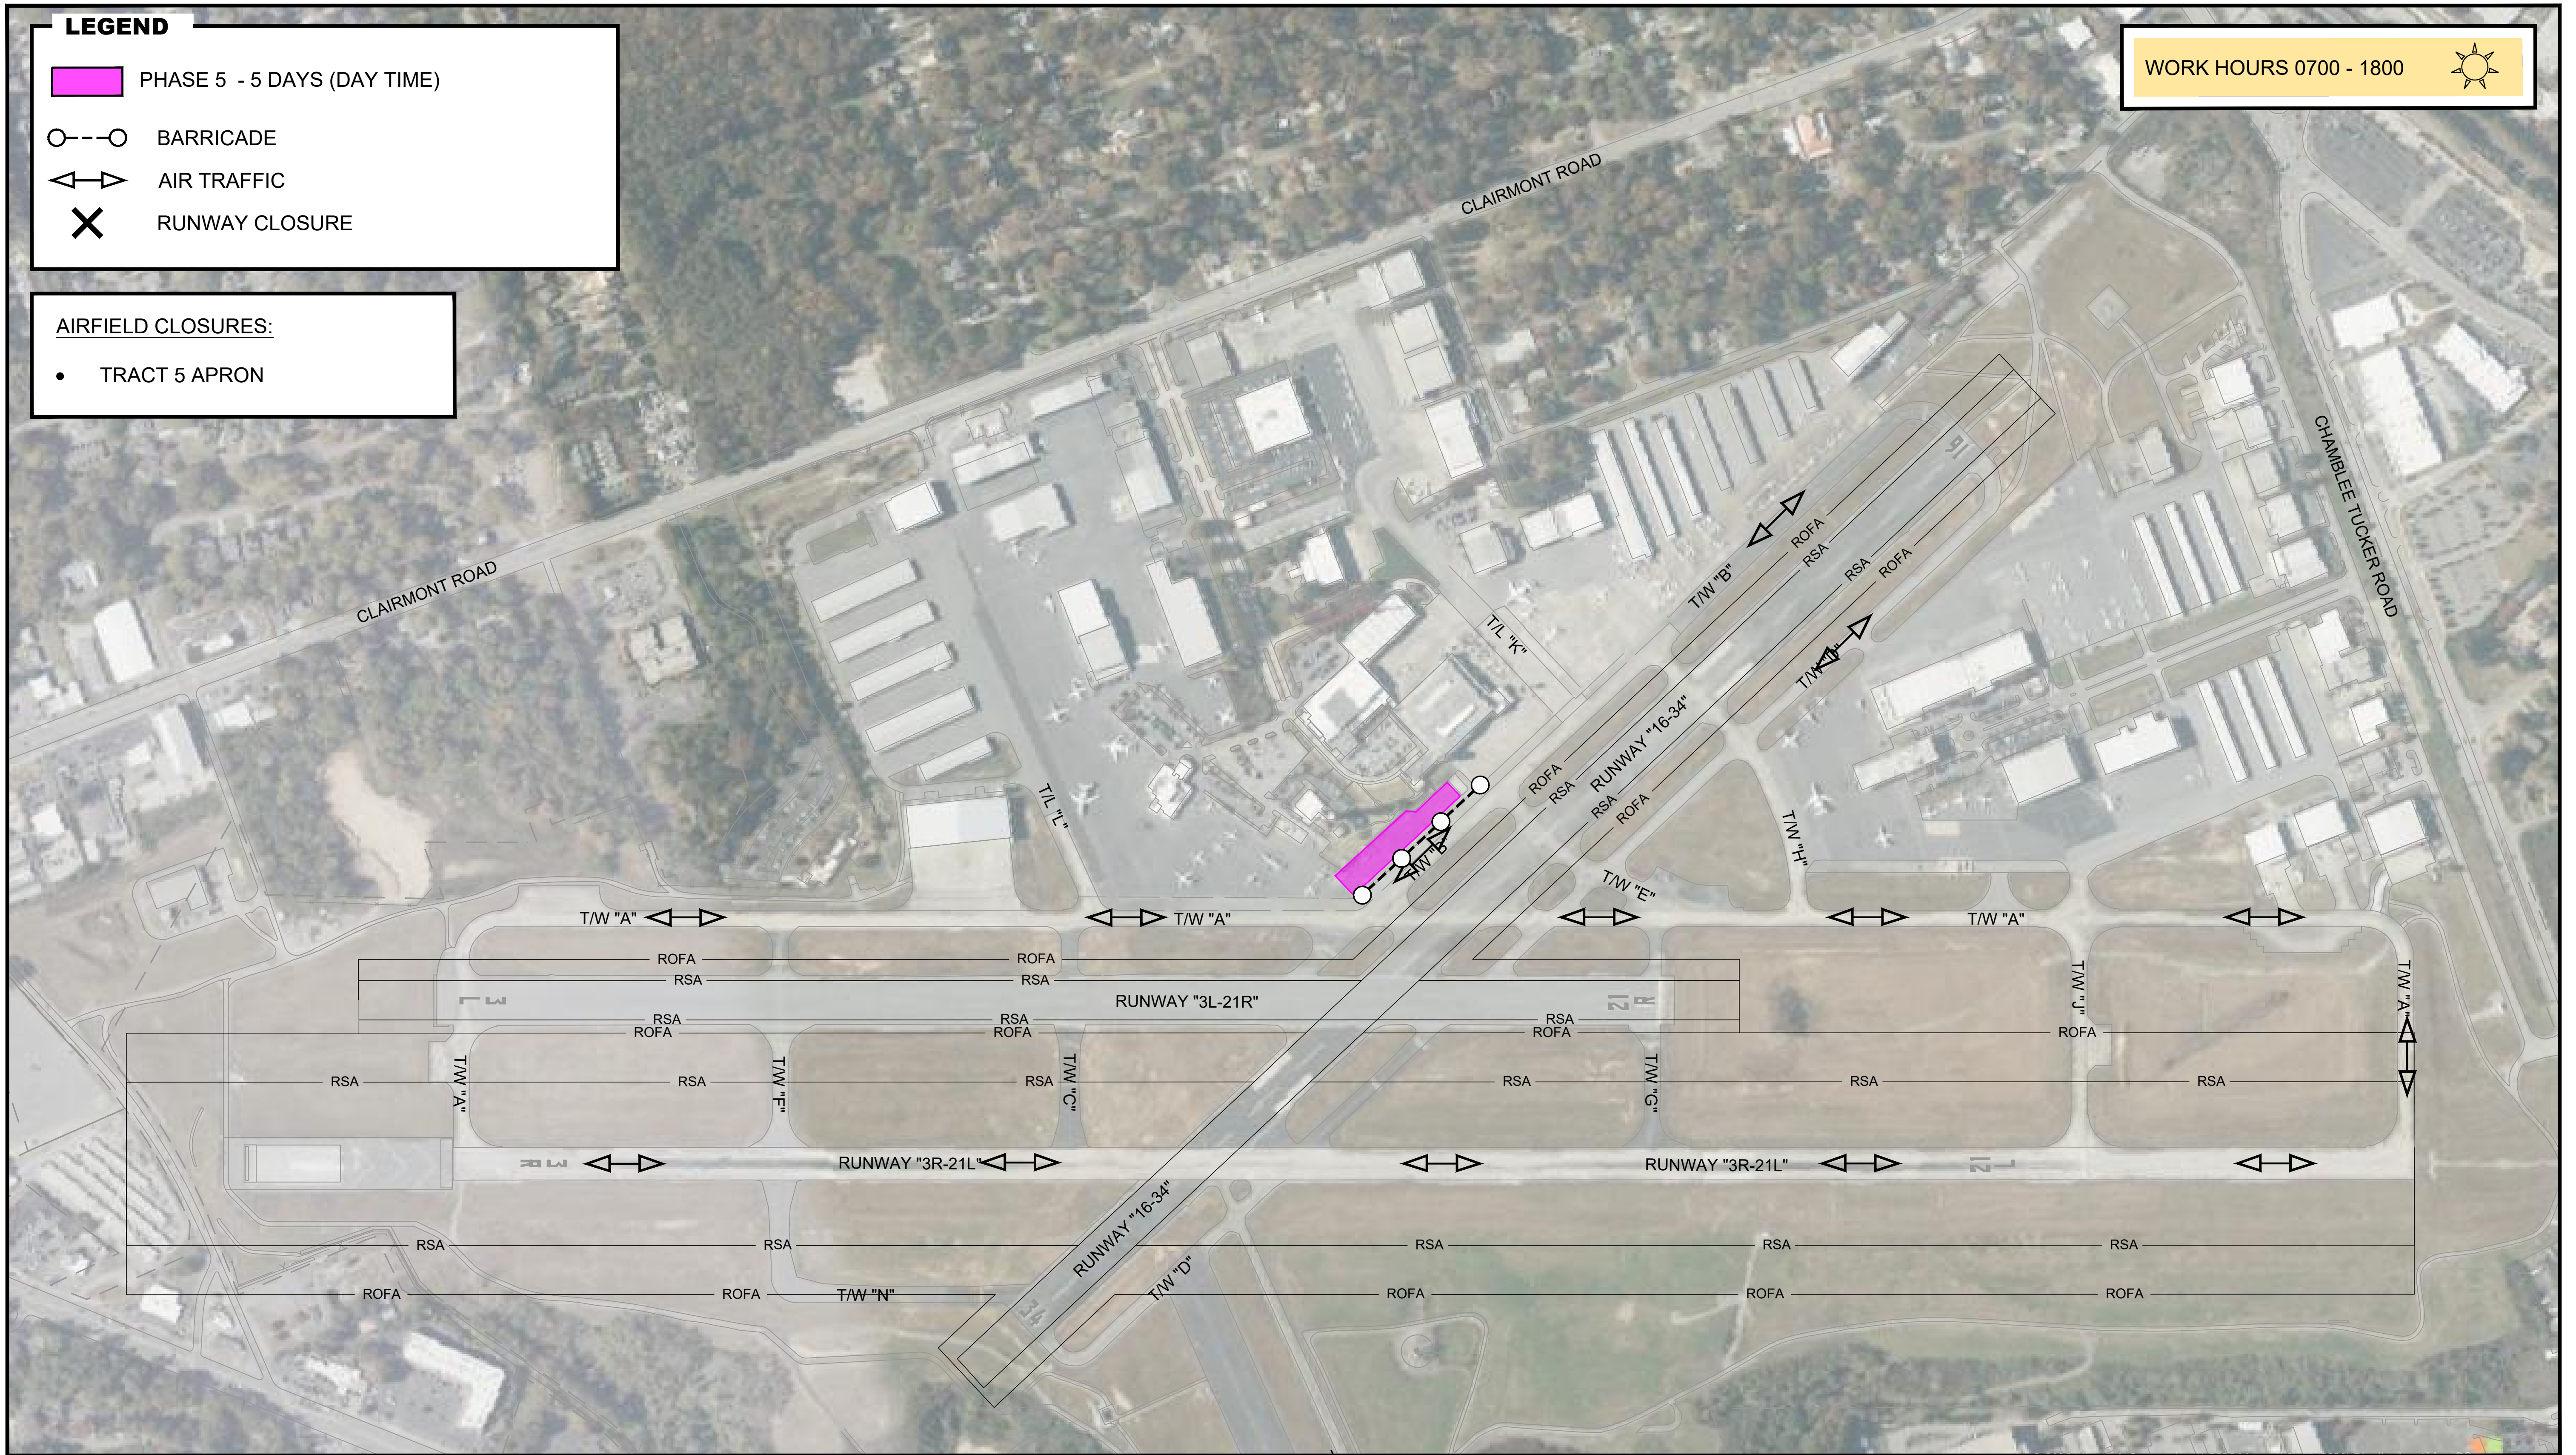

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 5

EXHIBIT
1" = 250'



Y:\Airports\PD\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:00pm

LEGEND


PHASE 6 - 5 DAYS (DAY TIME)

- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE


AIRFIELD CLOSURES:

- HELIPAD

WORK HOURS 0700 - 1800



Michael Baker
INTERNATIONAL





DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 6

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:01pm

LEGEND

-  PHASE 7A - 5 DAYS* (DAY TIME)
-  BARRICADE
-  AIR TRAFFIC
-  RUNWAY CLOSURE


AIRFIELD CLOSURES:

- TAXILANE L


*PHASE 7A IS A SUBPHASE OF PHASE 7. PHASE 7A DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

7A + 7B = 5 DAYS TOTAL

WORK HOURS 0700 - 1800



Michael Baker
INTERNATIONAL





DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 7A

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:01pm

LEGEND

-  PHASE 7B - 5 DAYS* (DAY TIME)
-  BARRICADE
-  AIR TRAFFIC
-  RUNWAY CLOSURE


AIRFIELD CLOSURES:

- TAXIWAY B (PARTIAL)
- TAXILANE K


*PHASE 7B IS A SUBPHASE OF PHASE 7. PHASE 7B DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

7A + 7B = 5 DAYS TOTAL

WORK HOURS 0700 - 1800



Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 7B

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Draw\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:01pm

LEGEND

- PHASE 8A - 5 DAYS* (DAY TIME)
- BARRICADE
- AIR TRAFFIC
- RUNWAY CLOSURE


AIRFIELD CLOSURES:

- NORTHEAST RAMP


*PHASE 8A IS A SUBPHASE OF PHASE 8. PHASE 8A DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

8A + 8B = 5 DAYS TOTAL

WORK HOURS 0700 - 1800



Michael Baker
INTERNATIONAL





DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 8A

EXHIBIT
1" = 250'



Y:\Airports\PDK\201383 - WA 23-10 Airfield Crack Seal & Remarking\Design\Drawings\Exhibits\Tenant Phasing\PDK - CS&R Phasing Breakdown.dwg Plotted on: Mar 24, 2026 - 2:01pm

LEGEND

-  PHASE 8B - 5 DAYS* (DAY TIME)
-  BARRICADE
-  AIR TRAFFIC
-  RUNWAY CLOSURE



AIRFIELD CLOSURES:

- NORTH RAMP


*PHASE 8B IS A SUBPHASE OF PHASE 8. PHASE 8B DURATION SHALL BE DETERMINED AT THE TIME OF CONSTRUCTION.

8A + 8B = 5 DAYS TOTAL

WORK HOURS 0700 - 1800

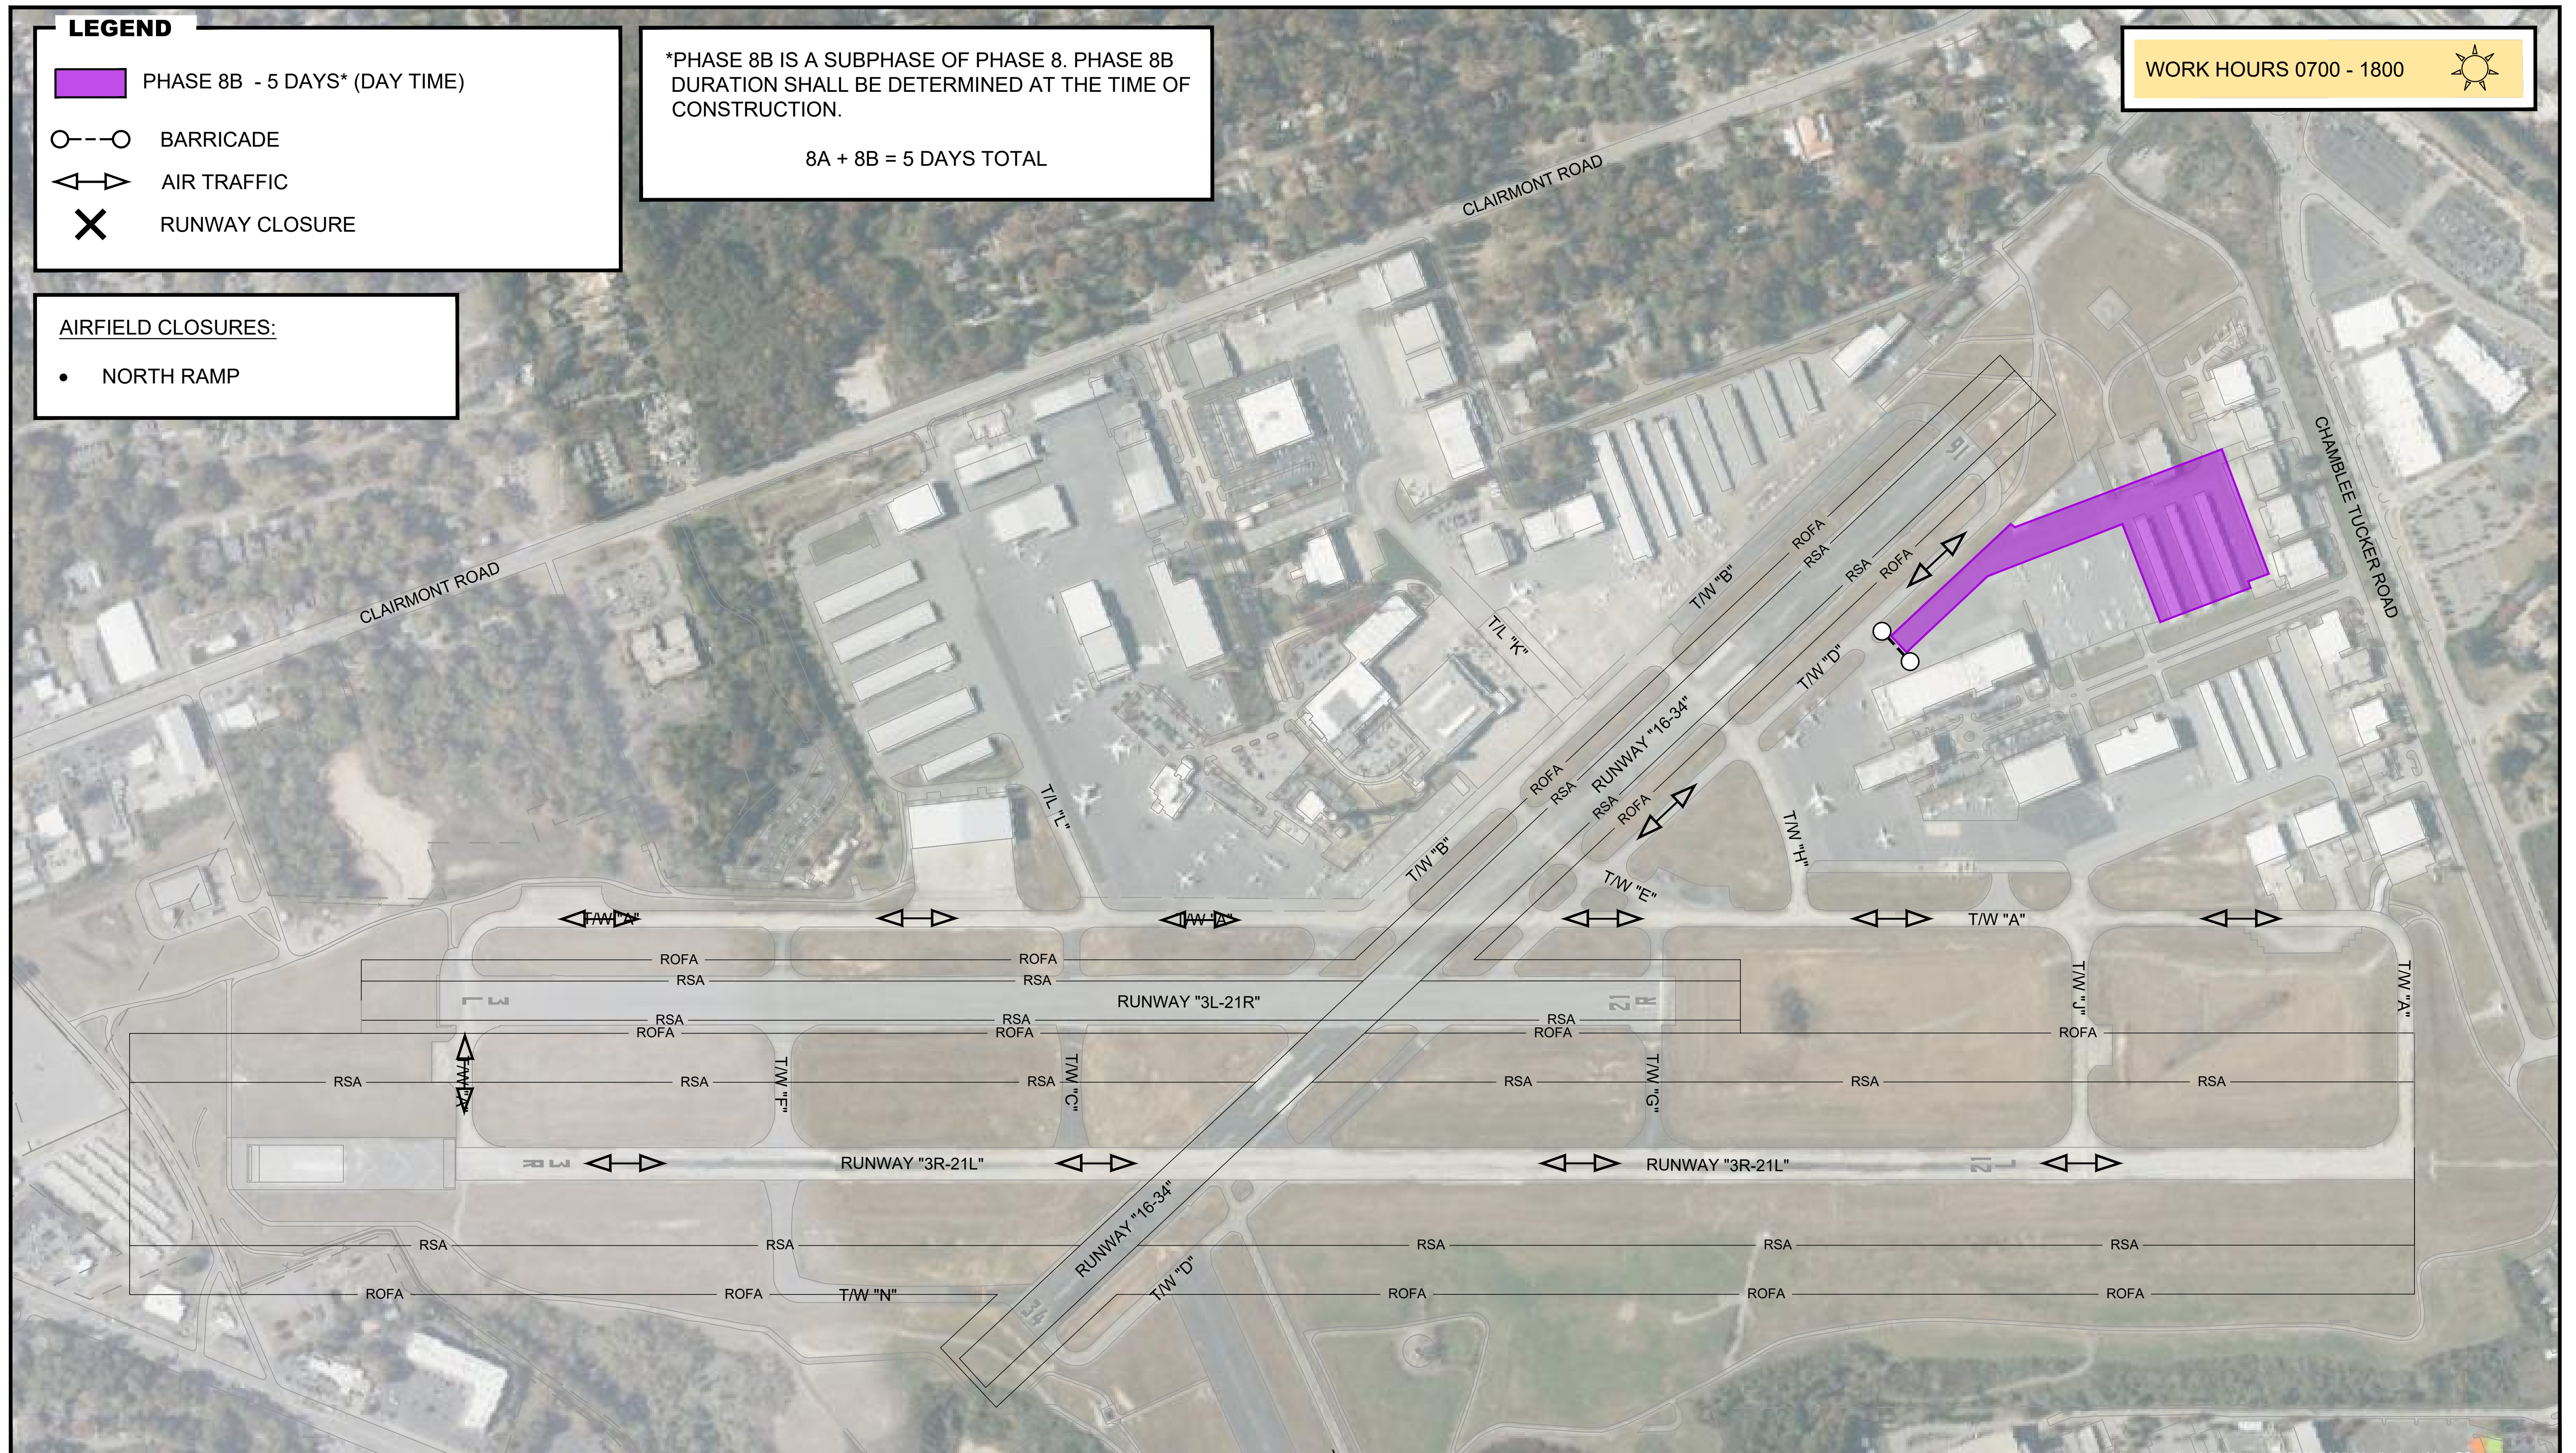

Michael Baker
INTERNATIONAL



DEKALB PEACHTREE AIRPORT
DEKALB COUNTY, GEORGIA
AIRFIELD CRACK SEAL & REMARKING - PHASE 8B

EXHIBIT
1" = 250'

